



I-4 and Sand Lake Road Interchange Design-Build

02/26/2025



Status as of February 24, 2025

Days Used	Total Days	% Days Complete	Last Contract Day
694	1,477	47%	04/18/2027

Sand Lake 3470				Current Week							Week 1							Week 2						
Activity ID	Activity Description	Foreman / Sub	Supt	24-Feb	25-Feb	26-Feb	27-Feb	28-Feb	1-Mar	2-Mar	3-Mar	4-Mar	5-Mar	6-Mar	7-Mar	8-Mar	9-Mar	10-Mar	11-Mar	12-Mar	13-Mar	14-Mar	15-Mar	16-Mar
				MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN
	Roadway																							
	Pic Embankment 4190 - 4209	Kyle Sample	Sample									X	X	X	X	X			X	X	X	X	X	
	Ramp M Detour																X							
	Pic Embankment 4226-4234 (Exist Ramp M)	Dennis Scott	Sample																	X	X	X		
	Reinstall Dewatering - Pond 206	Dennis Scott	Sample					X	X		X	X												
	Saw-cut/Ex for Widening - Ramp M	Dennis Scott	Sample																					
	Ramp M Switch (prerequisite)	Dennis Scott	Sample										X	X	X									
	Demo Mill Ramp M	Dennis Scott	Sample															X	X					
	Support JVD (Ex/Grade/Backfill)	Dennis Scott	Sample																					
STAB230	Place/Finish Lime Rock I4 WB sta. 4217-4226	Jessie Wilson	Greg Lemire					X			X	X	X											
	Drainage / Utilities																							
	Install S-247 to S-247A 24"	Jose Castro C.	Greg Lemire				X	X	X															
	Install S-247 to S-250A	Jose Castro C.	Greg Lemire								X	X	X											
	Install S-253A to S-253B	Jose Castro C.	Greg Lemire											X	X	X								
	Install S-253B to S-253	Jose Castro C.	Greg Lemire															X	X	X				
	Install S-253 S256	Jose Castro C.	Greg Lemire																		X	X	X	
	Install S-805A to CS-206A	Edward	Greg Lemire	X	X	X																		
	Install S-805A to S-516	Edward	Greg Lemire				X	X	X															
	Install S-516 to S-520	Edward	Greg Lemire								X	X	X											
	Install S-805A to S-328	Edward	Greg Lemire											X	X	X		X	X	X	X	X	X	
	Install S-241 to S-241A 36" Pipe	Edward	Greg Lemire	X	X	X	X	X																
	Install S-241A to S-241OF 54" Pipe	Edward	Greg Lemire					X	X		X	X												
	Install S-241A to S-809 48" Pipe	Edward	Greg Lemire										X	X	X	X								
	Install S-809 to S-811 48" Pipe	Edward	Greg Lemire															X	X	X	X			
	Install S-811 to S-808 48" Pipe	Edward	Greg Lemire																			X	X	
	Structures																							
DECK100	Dry run B-1	Jaime Castillo	James															X	X	X	X			
	Wreck B-2 Set B-1	Jaime Castillo	James		X	X	X	X			N	N	N	N										
	Strip keyway/bulkhead B-1	Jaime Castillo	James												X	X	X	X	X					
	Form coping plain under B5,B1&B2	Francisco	Jose P	X	X	X	X	P																
	slope pavement under B5/B6/B2/B1	Francisco	jose P								X	X	X	X	P									
	Approach slab B6-1	francisco	JOSE P		X	X	X	X	X															
	Form moment slab on RW1-2 & RW6-1	Rafael	Jose P								X	X	X	X	X			P						
	Set barrier wall precast on RW1-2, RW6-1 & RW104	Rafael	Jose P	X	X	X	X	X	X		X	X	X	X	X	X								
	Form closure pours RW1-2 & RW6-1	francisco	Jose P															X	X	X	X	X		
	Demo B7&8	victor medina	James							N	N	N	N	N			N	N	N	N	N		N	
	Subs																							
MSE240	Install MSE Wall 1-1	RWH Crew 1	Nate	X	X	X	X	X			X	X	X	X	X									
	Install MSE Wall 103	RWH Crew 2	Nate	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X		
	Slip Crew	JVD	Roberto		X																			
	SLR Existing Pipe Videos Night	APS	Rainer				N																	
	Guardrail Removal & Repair I4	Acme Guardrail	Roberto	X	X																			
	CFP F&I Anchored Wall	TCP	Roberto							N-C	N-C													
	Relocate KWall Ramp M to Ramp L	TCP	Roberto														N-C							
	Relocate Kwall Ramp M	TCP	Roberto														N-C							
	Relocate Low pro SLR to Ramp L	TCP	Roberto								N-C													
	Pavement Markings Ramp M	McShea	Nate										X											
	Temp/Permanent Ramp M	Hubbard	Nate							X														
	Overbuild Ramp L	Hubbard	Nate								X													
	WB Overbuild 1518+65 to 1527+32 (Ph.1C-step 2)	Hubbard	Nate									X												
	Permanent Ramp J (left turns)	Hubbard	Nate										X											
	Lighting Maintenance I4WB Median and SLR Underdecks	Conti	Rainer	X	X	X	X	X																
	MSE Wall 6-1	Conti	Rainer					X							X							X		

N/P - Night Pour	T-N - Tentative
X - Day Schedule	N - Night
NC - Night Time Confirmed	D-Pile Delivery
C - Confirmed or Cure	

Sand Lake 3470				Current Week								Week 1								Week 2							
Activity ID	Activity Description	Foreman / Sub	Supt	24-Feb	25-Feb	26-Feb	27-Feb	28-Feb	1-Mar	2-Mar	3-Mar	4-Mar	5-Mar	6-Mar	7-Mar	8-Mar	9-Mar	10-Mar	11-Mar	12-Mar	13-Mar	14-Mar	15-Mar	16-Mar			
				MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN			
	Ramp K Lighting	Conti	Rainer	X	X	X	X	X			X	X	X	X	X												
	Ramp M Graivty Wall Conduit & Embedded Boxes	Conti	Rainer			X																					
	Ramp M Shoulder Lights	Conti	Rainer	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X					
	Bridge 6 Underdeck Conduit	Conti	Rainer										X							X							
	ITS																										
	ITS Pullboxes I-4WB Sta: 1554 - 1479	Conti	Rainer	X	X	X	X	X			X	X	X	X	X												
	ITS Conduit I-4 WB Sta: 1433 - 1330	Conti/Synergy	Rainer															X	X	X	X	X					
	ITS Conduit I-4 EB Sta: 1554 - 1479	Conti/Synergy	Rainer	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X					
	Ramp M WWDS	Conti	Rainer								X	X	X	X	X			X	X	X	X	X					
	Ramp M Temp Bore	Conti/Synergy	Rainer															X	X	X	X	X					
	Ramp K WWDS	Conti	Rainer								X	X	X	X	X			X	X	X	X	X					
TOLL100	Ramp K Temp ITS Pole 73.3-EB-B	Conti	Rainer									X	X	X													
	MSE Wall 1-1 and 103	Conti	Rainer					X							X												
	Signals																										
	Ramp M Temp Strain Poles	Conti	Rainer								X	X	X	X	X			X	X	X	X	X					
	Ramp J Ped Temp Ped Poles 2	Conti	Rainer										X	X	X												
	Ramp JKPed Temp Ped Poles 1	Conti	Rainer										X	X	X												
	SPM																										
	Ramp K GMS	Conti	Rainer								X	X	X	X	X												
	Ramp K Cantilever Removal	Conti	Rainer										X	X	X												
	Pylon Bores CIP 1-2	Conti/Synergy	Rainer								X	X	X	X	X												
	Install J&B SLR CS-206A - S-2000	CFU	Rainer								X	X	X	X	X			X	X	X	X	X					
	Utilities	UTILITY OWNER	STA																								
	Pole Relocation: Gravity Wall (1/20 -5/14/25: 64 Days UWS)	Duke	TLR	N	N	N	N				N	N	N	N													
	Fiber Relocation	Crown Castle	SLR	X	X	X	X																				
	Sand Lake Officers Scheduled																										
	Place 5 if police are scheduled & # once total of officers confirmed		Nate																								
	Orange County		Nate																								
	FHP		Nate																								
	Critical Protection Services		Nate	N-C	N-C	N-C	N-C																				
	Sand Lake Road Closures /																										
	Sand Lake Rd & Ramps																										
	Sandlake Rd Singles WB (APS / CFU)	APS/CFU	Jamey	N-C	N-C	N-C	N-C																				
	Sandlake Rd Singles EB (APS / CFU)	APS/CFU	Jamey	N-C	N-C	N-C	N-C																				
	Sand Lake Contra-Flow WB	Dennis	Jamey							N-C	N-C	N-C	N-C	N-C			N-C	N-C	N-C	N-C	N-C			N-C			
	Sand Lake Contra-Flow EB	Dennis	Jamey							N-C	N-C	N-C	N-C	N-C			N-C	N-C	N-C	N-C	N-C			N-C			
	Singal Outside Right Lane Ramp L	APS/CFU	Jamey				N-C																				
	Ramp k Shutdown (Sign Removal)	Conti	Jamey									N-C	N-C	N-C													
	Central Florida PKWY																										
	Full Detour CFP (12:30AM to 3:30AM)	Dennis	Jamey																					N-C			

N/P - Night Pour	T-N - Tentative
X - Day Schedule	N - Night
NC - Night Time Confirmed	D-Pile Delivery
C - Confirmed or Cure	



Rosen Inn International





Agenda — Past Project Status

- **Past Project Status — FDOT to review past 7 days**
 - Lighting (Areas 2, 3, 5, 6, and 7)
 - Installing barriers on bridges over Sand Lake Road (Areas 2 and 3)
 - Bridge deck installation (Areas 1, 2, and 3)
 - Place lime rock on loop ramp (Area 3)
 - Turkey Lake median widening
 - Continue installing MSE walls (Area 1)
 - Utility relocation
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Future Project Status

- **Future Project Status — FDOT to review next 7 days**
 - Maintaining existing and installing new Wrong-Way Vehicle Detection Systems (Areas 3, 6, and 7)
 - Bridge deck installation (Areas 1, 2, and 3)
 - Place lime rock on loop ramp (Area 3)
 - Place temporary embankment (Areas 2 and 3)
 - Continue installing MSE walls (Area 1)
 - Turkey Lake median widening
 - Lighting (Areas 6 and 7)
 - Utility relocation
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Future Project Status

- **Future Project Status — FDOT to review next 14 – 21 days**
 - Maintaining existing and installing new Wrong-Way Vehicle Detection Systems (Areas 3, 6, and 7)
 - Bridge deck installation (Areas 1, 2, and 3)
 - Continue installing MSE walls (Area 1)
 - Place temporary embankment (Areas 2 and 3)
 - Turkey Lake median widening
 - Lighting (Areas 6 and 7)
 - Utility relocation
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Cleanliness Review

- **Cleanliness Review**
 - Committee's observations over past 7 days
- **Condition Review**
 - Committee's observations over past 7 days
(fencing, wraps, barricades, temporary signage)



Agenda — Old Business

- **Public Input or Comments**
- **Commitments Update**
 - Bridge underdeck lighting
 - Fencing and screening
 - Mowing and cleaning
 - Clean Team
 - Ponds



Agenda — Old Business


- Bridge deck pours over Sand Lake Road
 - Bridge 1
 - As early as mid March
 - Overnight





Agenda — Old Business

- **S.R. 528 ramp widening**
 - **Bridge deck pour safety diversions**
 - **Westbound I-4 from Adventure Way to Central Florida Parkway**
 - **March 2**
 - **10 p.m. – 6 a.m.**
 - **Eastbound I-4 at S.R. 528 and westbound I-4 exit ramp to eastbound S.R. 528**
 - **March 6**
 - **10 p.m. – 6 a.m.**

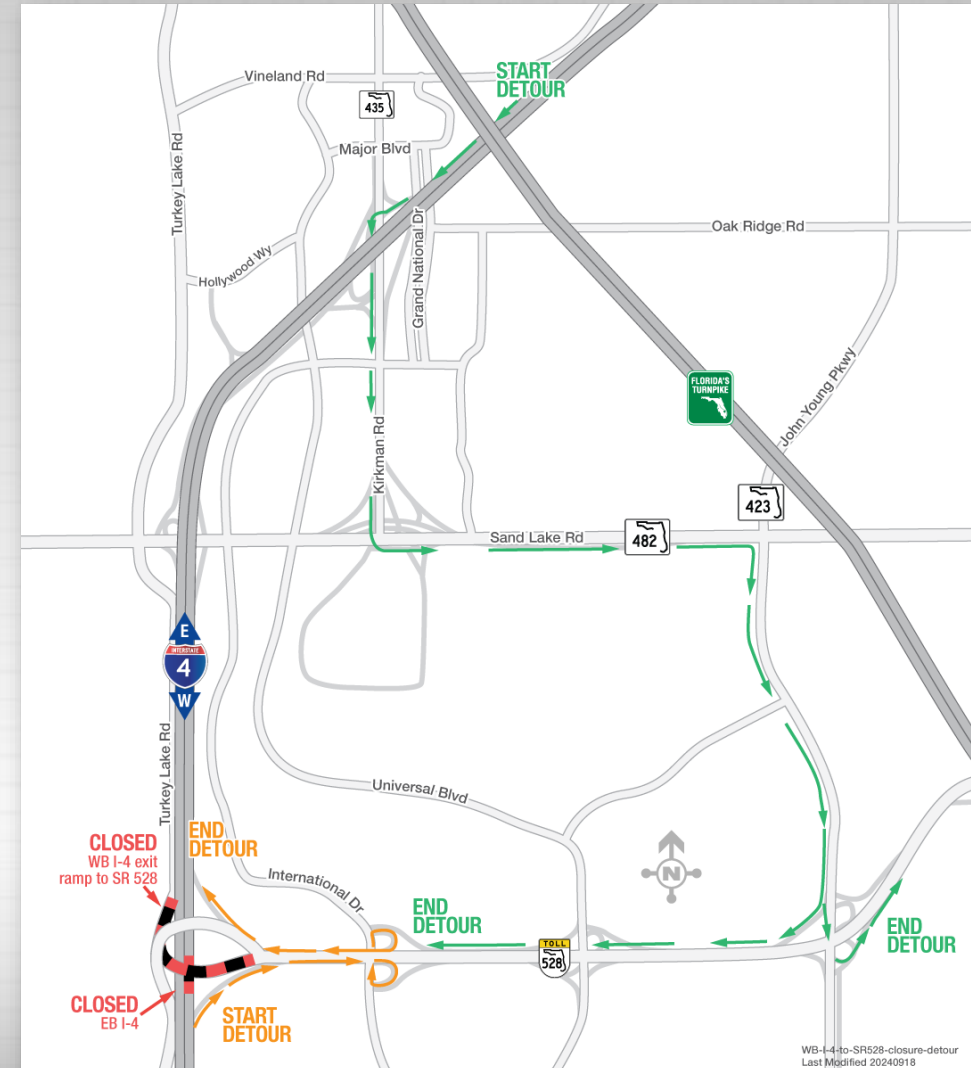



Agenda — New Business

- Next meeting: 03/05/25
