



I-4 and Sand Lake Road Interchange Design-Build

03/19/2025



Status as of March 17, 2025

Days Used	Total Days	% Days Complete	Last Contract Day
715	1,478	48.4%	04/19/2027

[illegible]

Sand Lake 3470				Current Week								Week 1							Week 2						
Activity ID	Activity Description	Foreman / Sub	Supt	17-Mar	18-Mar	19-Mar	20-Mar	21-Mar	22-Mar	23-Mar	24-Mar	25-Mar	26-Mar	27-Mar	28-Mar	29-Mar	30-Mar	31-Mar	1-Apr	2-Apr	3-Apr	4-Apr	5-Apr	6-Apr	
				MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	
	Temp Pavement Ramp K	Hubbard	Nate									N	N												
	Permanent Ramp J (left turns)	Hubbard	Nate							N	N														
	Lighting																								
	Lighting Maintenance Ramp M	Conti	Ralner	X	X	X																			
	Ramp K Lighting Removal	Conti	Ralner	X	X	X	X	X																	
	Ramp M Shoulder Lights	Conti	Ralner								X	X	X	X	X										
	Bridge 6 Underdeck Conduit	Conti	Ralner										X												
	ITS																								
	ITS Conduit I-4 WB Sta: 1433 - 1330	Conti/Synergy	Ralner	X	X	X	X	X			X	X	X	X	X										
	ITS Conduit I-4 EB Sta: 1554 - 1479	Conti/Synergy	Ralner															X	X	X	X	X			
	Ramp M WWDS	Conti	Ralner	X	X	X	X	X			X	X	X	X	X										
	Ramp M Temp Bore	Conti/Synergy	Ralner															X	X	X	X	X			
	Ramp K WWDS	Conti	Ralner	X	X	X	X	X																	
	MSE Wall 1-1 and 103 Conduit	Conti	Ralner					X																	
	Drill Shaft ITS 73.3.EB.B Sta.1476	Conti	Ralner			X																			
	Drill Shaft ITS 73.3.EB.A Sta.1465	Conti	Ralner		X																				
	Drill Shaft ITS 73.9.EB Sta.1493	Conti	Ralner				X																		
	Drill Shaft ITS 73.7 WB Sta.306	Conti	Ralner					X																	
	Drill Shaft ITS 73.9 WB Sta.5227	Conti	Ralner								X														
	Drill Shaft ITS 74.2 WB Sta.5240	Conti	Ralner									X													
	Drill Shaft ITS 74.6 WB Sta.1522	Conti	Ralner										X												
	Drill Shaft ITS 74.3 EB Sta.1510	Conti	Ralner											X											
	Signals																								
	Ramp M Temp Strain Poles	Conti	Ralner															X	X	X	X	X			
	Ramp J Temp Ped Poles 2	Conti	Ralner			X	X	X																	
	Ramp K P Temp Ped Poles 1	Conti	Ralner			X	X	X																	
	SPM																								
	Ramp K GMS	Conti	Ralner	X	X	X	X	X																	
	End Cont.																								
	CFU Locate Utilities SL RD. New POL	CFU	Ralner			NC	NC																		
	Install J&B SLR CS-206A - S-2000	CFU	Ralner	X	X	X	X	X			X	X	X	X	X										
	Utilities	UTILITY OWNER	STA																						
	Pole Relocation: Gravity Wall (1/20 -5/14/25: 64 Days UWS)	Duke	TLR	X	X	X	X				X	X	X	X				X	X	X	X				
	Pole Relocation: Soft Digs and Bores (2)	Duke	TLR							N	N	N	N	N											
	Fiber Relocation	Crown Castle	SLR						N																
	Sand Lake Road Closures /																								
	Sand Lake Rd & Ramps																								
	Sand Lake Rd EB Single Lane	CFU	Jamey	N-C	N-C	N-C	N-C			N-C	N-C	N-C	N-C	N-C											
	Sand Lake Rd WB Single Lane	CFU	Jamey	N-C	N-C	N-C	N-C			N-C	N-C	N-C	N-C	N-C											
	Ramp J Shutdown (CFU) (Paving Hubbard)	CFU	Jamey	N-C	N-C	N-C	N-C			N-C	N-C	N-C	N-C	N-C											
	Ramp K (Hubbard)	Hubbard	Jamey							N-C	N-C	N-C	N-C	N-C											
	Ramp L (Hubbard)	Hubbard	Jamey							N-C	N-C	N-C	N-C	N-C											
	I-4 EB																								
	I-4 Single Lane Closures EB	Dennis	Jamey	N-C	N-C	N-C	N-C			N-C	N-C	N-C	N-C	N-C											
	I-4 WB																								
	I-4 Single Lane Closures WB	Dennis	Jamey	N-C	N-C	N-C	N-C			N-C	N-C	N-C	N-C	N-C											

N/P - Night Pour	T-N - Tentative
X - Day Schedule	N - Night
NC - Night Time Confirmed	D-Pile Delivery
C - Confirmed or Cure	



Rosen Inn International





Agenda — Future Project Status

- **Past Project Status — FDOT to review past 7 days**
 - Prepping for jack and bore (Areas 2 and 3)
 - Maintaining existing and installing new Wrong-Way Vehicle Detection Systems (Areas 3, 6, and 7)
 - Lighting (Areas 2, 3, 5, 6, and 7)
 - Turkey Lake median widening
 - Bridge deck installation (Areas 1, 2, and 3)
 - Continue installing MSE walls (Area 1)
 - Paving (Areas 2, 6, and 7)
 - Utility relocation
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Jack and Bore





Agenda — Future Project Status

- **Future Project Status — FDOT to review next 7 days**
 - Jack and bore (Areas 2 and 3)
 - Maintaining existing and installing new Wrong-Way Vehicle Detection Systems (Areas 3, 6, and 7)
 - Bridge deck installation (Areas 1, 2, and 3)
 - Continue installing MSE walls (Area 1)
 - Turkey Lake median widening
 - Lighting (Areas 6 and 7)
 - Utility relocation
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Future Project Status

- **Future Project Status — FDOT to review next 14 – 21 days**
 - Place lime rock (Areas 2 and 3)
 - Bridge deck installation (Areas 1, 2, and 3)
 - Continue installing MSE walls (Area 1)
 - Turkey Lake median widening
 - Utility relocation
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Cleanliness Review

- **Cleanliness Review**
 - Committee's observations over past 7 days
- **Condition Review**
 - Committee's observations over past 7 days
(fencing, wraps, barricades, temporary signage)



Agenda — Old Business

- **Public Input or Comments**
- **Commitments Update**
 - Fencing and screening
 - Mowing and cleaning
 - Clean Team
 - Ponds



Safety Diversions


- Bridge deck pours over Sand Lake Road
 - Bridge 1
 - As early as April 4
 - Overnight safety diversions





Daryl Carter Parkway Diverging Diamond


- Daryl Carter overpass converted to a diverging diamond
 - March 19
- Ramps to open at the end of April, at the earliest

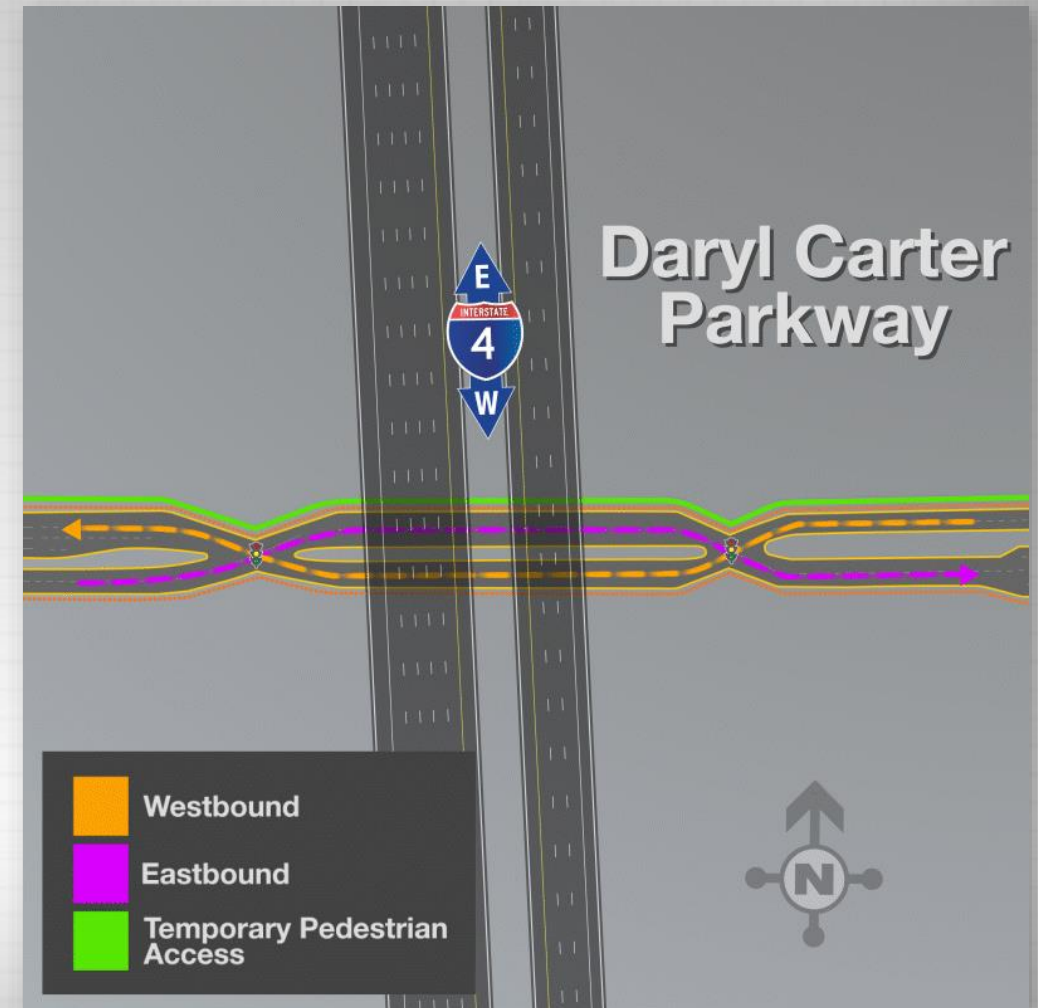



I-4 Safety Diversion

- Removing overhead sign truss
- Diverting eastbound and westbound I-4
 - Between Daryl Carter Parkway and Central Florida Parkway
 - March 20
 - 1 – 5 a.m.

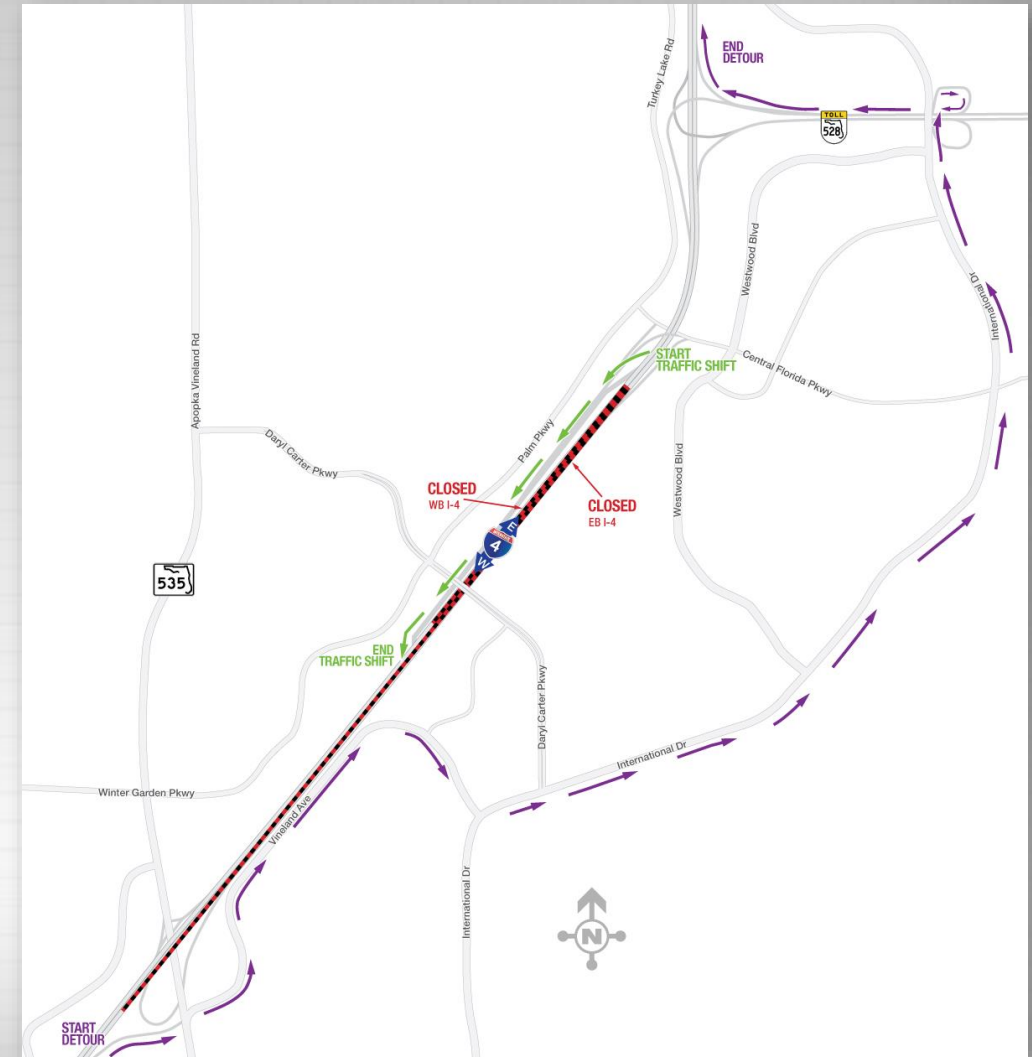



Agenda — New Business

- **Safety Diversion**
 - **Westbound I-4 entrance ramp from Sand Lake Road**
 - **March 19 – 21**
 - **10 p.m. - 5 a.m.**





Agenda — New Business

- Next meeting: 03/26/25
