



I-4 and Sand Lake Road Interchange Design-Build

07/08/2026



Status as of July 6, 2026

Days Used	Total Days	% Days Complete	Last Contract Day
1,191	1,779	66.9%	2/14/2028

Sand Lake 3470				Current Week							Week 1							Week 2						
Activity ID	Activity Description	Foreman / Sub	Supt	6-Jul	7-Jul	8-Jul	9-Jul	10-Jul	11-Jul	12-Jul	13-Jul	14-Jul	15-Jul	16-Jul	17-Jul	18-Jul	19-Jul	20-Jul	21-Jul	22-Jul	23-Jul	24-Jul	25-Jul	26-Jul
				MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN
Roadway																								
MSE320	Exc/Grade Wall 4-2	Marcos C.	Tyler	X	X	X	X	X			X	X	X	X	X									
	Sand Lake Rd. Widening (North)	Marcos C.	Tyler	X	X	X	X	X			X	X	X	X	X									
	Sand Lake Rd. Widening/Ramp K tie-in (South)	Marcos C.	Tyler															X	X	X	X	X		
	Place Embankment Ramp L	Marcos C.	Tyler	X	X	X	X	X			X	X	X	X	X									
EW570	Ph. 2B - EB Widening 1440 - 1450	Jessie W	Tyler	X	X	X	X	X																
BASE450	Ph. 2B - EB/Ramp K - Plc/Fin Lime Rock (7189 - 7210)	Jessie W	Tyler	X	X	X	X	X			X	X	X	X	X									
	EB XL - Mix/Plc/Fin slab (6252- 6262)	Jessie W	Tyler															X	X	X	X	X		
BASE360	M WB Tube - Plc/Fin Lime Rock 1355 - 1335 (bridge 7)	Ian Palasz	Tyler	X	X	X	X	X																
	FG WB Tube Ditch	Ian Palasz	Tyler																					
	Finish Lime Rock - Sand Lake Rd. Widening (South)	Ian Palasz	Tyler								X	X	X	X	X									
	M WB Tube - Balance/Mix (Bridge 7 - Daryl Carter)	Ian Palasz	Tyler								X	X	X	X	LBR			LBR	LBR	LBR	LBR	X		
	Mowing and Litter Pick Up	Billy Worles	Greg L	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X	X	
	Clean Team Sand Lake Sidewalks, Trash pickup and Mowing	Billy Worles	Greg L	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X	X	
	Sand Lake off and on ramps to I-4 - Trash pickup and Mowing	Billy Worles	Greg L															X	X	X	X	X	X	
	Turkey Lake Sidewalks, Trash pickup and Mowing	Billy Worles	Greg L															X	X	X	X	X	X	
	Kirkman ramp - Trash pickup and Mowing	Billy Worles	Greg L															X	X	X	X	X	X	
	Remove existing Curb Turkey Lake	Michael Bloomfield	Jose Castro	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X	X	
	Place Grade Limerock on Turkey Lake for Curb and Gutter	Michael Bloomfield	Jose Castro	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X	X	
Drainage / UTILITIES																								
	Install S-522 To S-524 (18")	Isaias Barcenas	Greg L	X	X	X	X	X																
	Install S-350 to S-350OF (18")	Isaias Barcenas	Greg L								X	X	X											
	Install S-337-S-314 (18")	Isaias Barcenas	Greg L																					
	Install S-528B to S-528A (18") connect to exist.	Isaias Barcenas	Greg L											X	X			X	X	X	X	X		
DRG1390	Install S-715 to S-716 (30")	Dakota Mooney	Greg L																					
DRG1390	Install S-716 to S-717 (30")	Dakota Mooney	Greg L															X	X	X	X	X		
	Install S-717 To S-722 (30")	Dakota Mooney	Greg L	X	X	X	X	X			X	X	X	X	X			X						
U-OCU1540	Install FM Sand Lake across TL	Edward Benitez	Greg L	N	N	N	N	N			N	N	N	N	N			N	N	N	N	N		
Structures																								
Bridge #4																								
	unload rebar for cap, and pylon 4-1	Eusebio Perez	Jose Perez	x																				
CURE220	Form/pour/remove, footer pier 2	Eusebio Perez	Jose Perez	C	C	C	C	C			X	X												
SUB5290	form, pour, remove, column pier 2	Eusebio Perez	Jose Perez	x	x	x												X	X	P	C	C		
	assemble cap forms for pier 2	Eusebio Perez	Jose Perez	x	x	x	X	X			X	X	X	X	X									
	from end bent 1	Jaime Castillo	Jose Perez								X	X	X	X	X			X	X	X	P			
	cut pile end bent 1	Jaime Castillo	Jose Perez								X	X												
	pre built columns form	Eusebio Perez	Jose Perez	X	X																			
	form columns pier 2	Eusebio Perez	Jose Perez				X	X			X	X												
Pylon Footing																								
SUB5200	install protection forms around pylon rebar	Jaime Castillo	Jose Perez																					
SUB5200	form pylon 4-2	Victor Medina	Jose Perez								X	X	X	X	X							X		
	form pylon 4-2	Victor Medina	Jose Perez															X	X	X	X	X		
Subcontractor																								
FLAT160	Turkey Lake Curb and Gutter, Sidewalk	JVD	Rainer	X	X	X	X	X			X													
BW300	Median Barrier - WB GUL, XL's, EB GUL (North)	Blount Sanford	Harry				X	X			X	X	X	X	X			X	X	X	X	X		
BW290	Median Barrier Ramp K	Blount Sanford	Harry	X	X	X																		
	Pylon footer rebar 4-2	Shelby	Harry								X	X	X	X	X									
	B4 column rebar	Shelby	Harry			N	N																	
MSE310	RW 4-1	RWH	Nate	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X		
MSE320	RW 4-2	RWH	Nate								X	X	X	X	X			X	X	X	X	X		
	Barrier Wall Install Area 4 TTCP's	TCP	Nate															N	N	N	N	N		
	WB Tube Ditch - 1330 - 1425	Unlimited Turf	Nate												X	X								
	Shift Traffic Area 4 TTCP's	McShea		N	N																			
DRG310	Install 30" J&B S-55 - S404OF (Tube Area 3) Sta: 1345	CFU	Greg	X	X	X	X	X			X	X	X	X	X									
DRG310	Install 30" J&B S-56 - S422A (Tube Area 3) Sta: 1356	CFU	Greg															X	X	X	X	X		
	Ramp L Tie in	Hubbard																						
PAVE440	Ramp K paving	Hubbard																N	N	N	N	N		
	Guardrail Removal (Sta 1336+00 to 1357+50) & Area	Acme																						
Lighting																								
LGHT110	Lighting Load Center B (Ramp K)	Conti	Rainer	X	X	X	X	X			X	X	X	X	X									
ITS																								
ITS120	ITS Conduit I-4 EB Sta: 1433 - 1330	Conti/Vasi/KDI	Rainer															X	X	X	X	X		
Toll Plaza																								
TOLL110	Load Center	Conti	Rainer	X	X	X	X	X																
TOLL140	Set Building	Conti	Rainer								N	N												
Sand Lake Road Closures / Sidewalk																								
Sand Lake Rd & Ramps																								
	Sand Lake WB Contra flow (Bridge Work)	James	Dennis	N	N	N	N				N	N	N	N	N			N	N	N	N	N		
	Sand Lake EB Contra flow (Bridge Work)	James	Dennis	N	N	N	N				N	N	N	N	N			N	N	N	N	N		
	Sand Lake Rd EB Double Lane Inside (Forcemain)	Lane	Dennis	N	N	N	N				N	N	N	N	N			N	N	N	N	N		
	Sand Lake Rd WB Single Lane Inside (Forcemain)	Lane	Dennis	N	N	N	N				N	N	N	N	N			N	N	N	N	N		
	Turkey Lake & Sandlake Rd Intersection (Detour 12.1A)	Lane	Dennis	N	N	N	N				N	N	N	N	N									
	Turkey Lake & Sandlake Rd Intersection (Detour 12.1B)	Lane	Dennis	N	N						N	N	N											
	Turkey Lake & Sandlake Rd Intersection (Detour 12.2)	Lane	Dennis	N	N	N	N				N	N	N	N	N									
	Turkey Lake & Sandlake Rd Intersection (Detour 12.3)				N	N	N																	
I-4 EB																								
	I-4 Single Lane Closures EB	Lane	Dennis	N	N	N	N				N	N	N	N	N			N	N	N	N	N		
I-4 WB																								
	I-4 Single Lane Closures WB	Lane	Dennis	N	N	N	N				N	N	N	N	N			N	N	N	N	N		

N/P - Night Pour

X - Day Schedule

NC - Night Time Confirmed

TS-Traffic Shift

T-N - Tentative

N - Night

D-Pile Delivery




Rosen Inn
International





Agenda — Current Project Status

- **Past Project Status — FDOT to review past 7 days**
 - Bridge support structure work at Sand Lake Road (Areas 5 and 6)
 - Eastbound I-4 traffic shift near Universal Boulevard
 - Force main installation crossing Sand Lake Road/Turkey Lake Road
 - Turkey Lake Road outside grading and widening
 - Place and compact lime rock (Area 8)
 - Embankment material placement (Areas 5 and 6)
 - Barrier wall installation (Areas 4, 6, and 8)
 - Signal and sign structure installation
 - Excavate and grade ponds
 - Utility relocation
 - Drainage installation (Areas 5 and 6)
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**

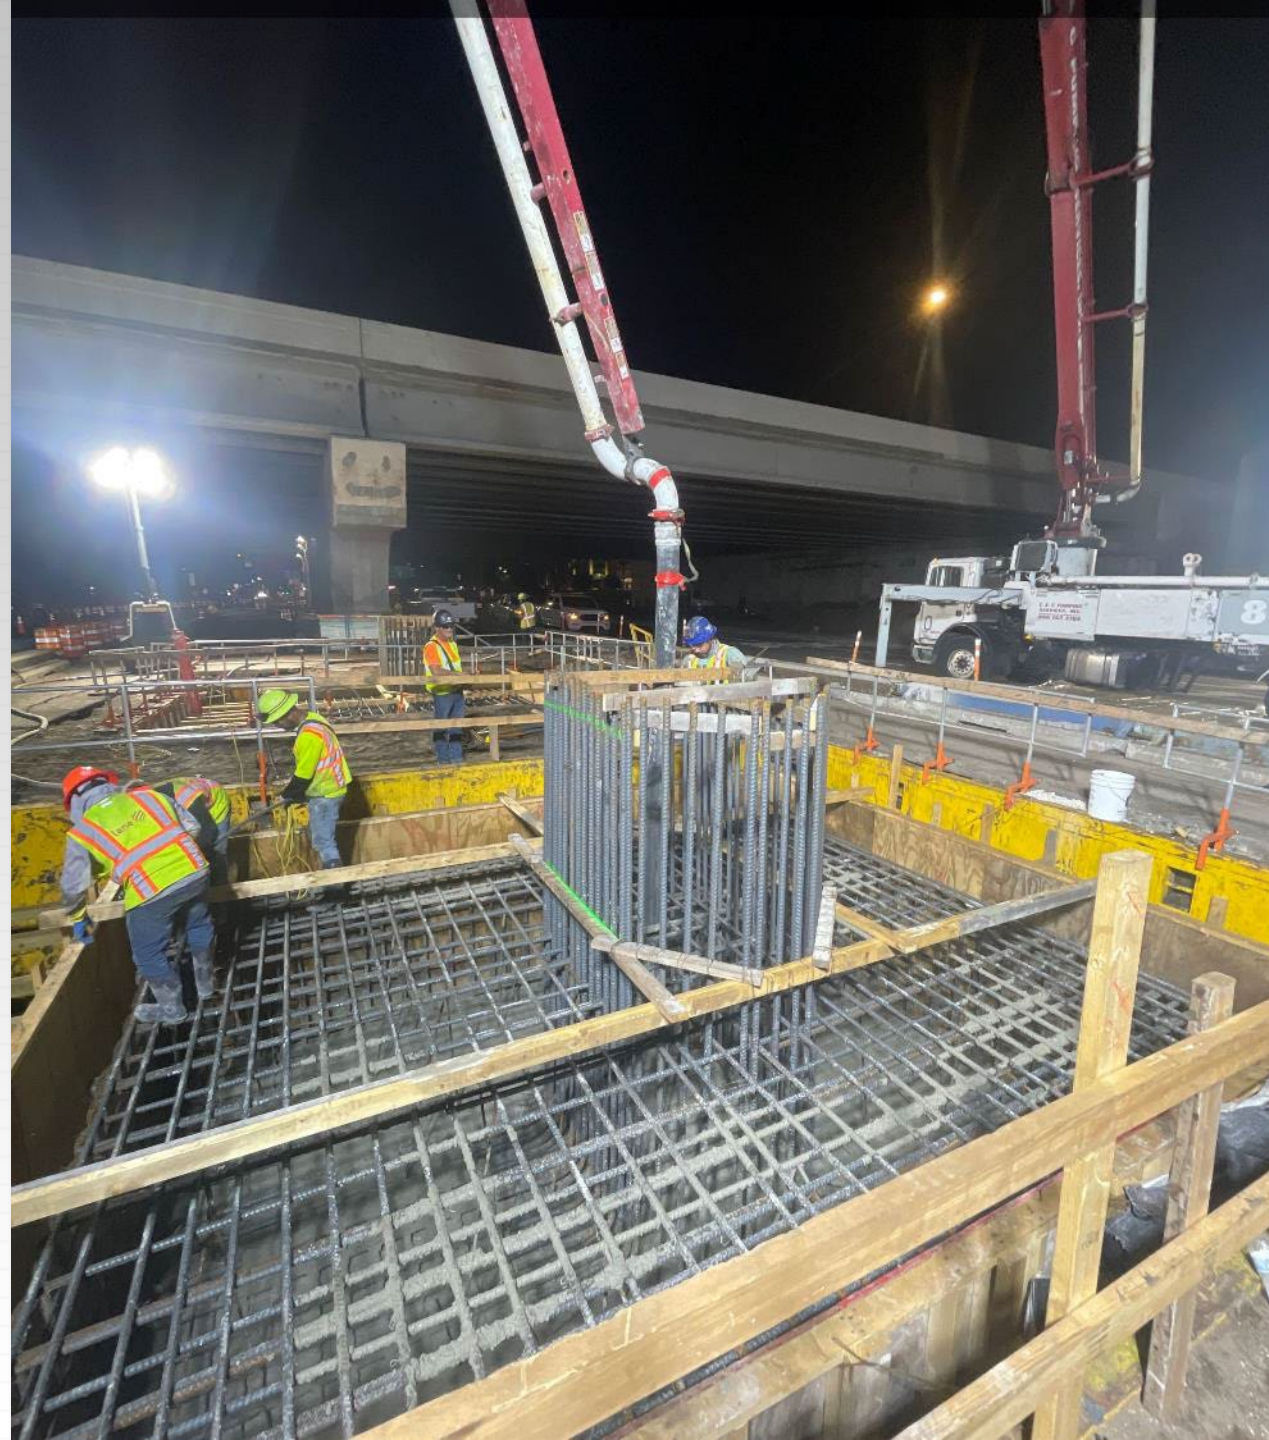







Agenda — Future Project Status

- **Future Project Status — FDOT to review next 7 days**
 - Bridge support structure work at Sand Lake Road (Areas 5 and 6)
 - Force main installation crossing Sand Lake Road/Turkey Lake Road
 - Turkey Lake Road outside grading and widening
 - Place and compact lime rock (Area 8)
 - Embankment material placement (Areas 5 and 6)
 - Barrier wall installation (Areas 4, 6, and 8)
 - Signal and sign structure installation
 - Excavate and grade ponds
 - Utility relocation
 - Drainage installation (Areas 5 and 6)
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Future Project Status

- **Future Project Status — FDOT to review next 14 – 21 days**
 - Force main installation crossing Sand Lake Road/Turkey Lake Road
 - Bridge support structure work at Sand Lake Road (Areas 5 and 6)
 - Bridge pier concrete pour in Sand Lake Road median
 - Turkey Lake Road outside grading and widening
 - Place and compact lime rock (Areas 5, 6, and 8)
 - Embankment material placement (Areas 5 and 6)
 - Barrier wall installation (Areas 4, 6, and 8)
 - Signal and sign structure installation
 - Excavate and grade ponds
 - Utility relocation
 - Drainage installation (Areas 5 and 6)
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Cleanliness Review

- **Cleanliness Review**
 - Committee's observations over past 7 days
- **Condition Review**
 - Committee's observations over past 7 days
(fencing, wraps, barricades, temporary signage)




Agenda — Old Business

- **Public Input or Comments**
- **Commitments Update**
 - Fencing and screening
 - Mowing and cleaning
 - Clean Team
 - Express lanes signage/access
 - Hardscaping and aesthetics
 - Ponds



Safety Diversions


- **July 6–9 (overnight)**
 - Left-turn lanes from southbound Turkey Lake Road to eastbound Sand Lake Road
 - Force main installation
 - 11 p.m. to 6 a.m.

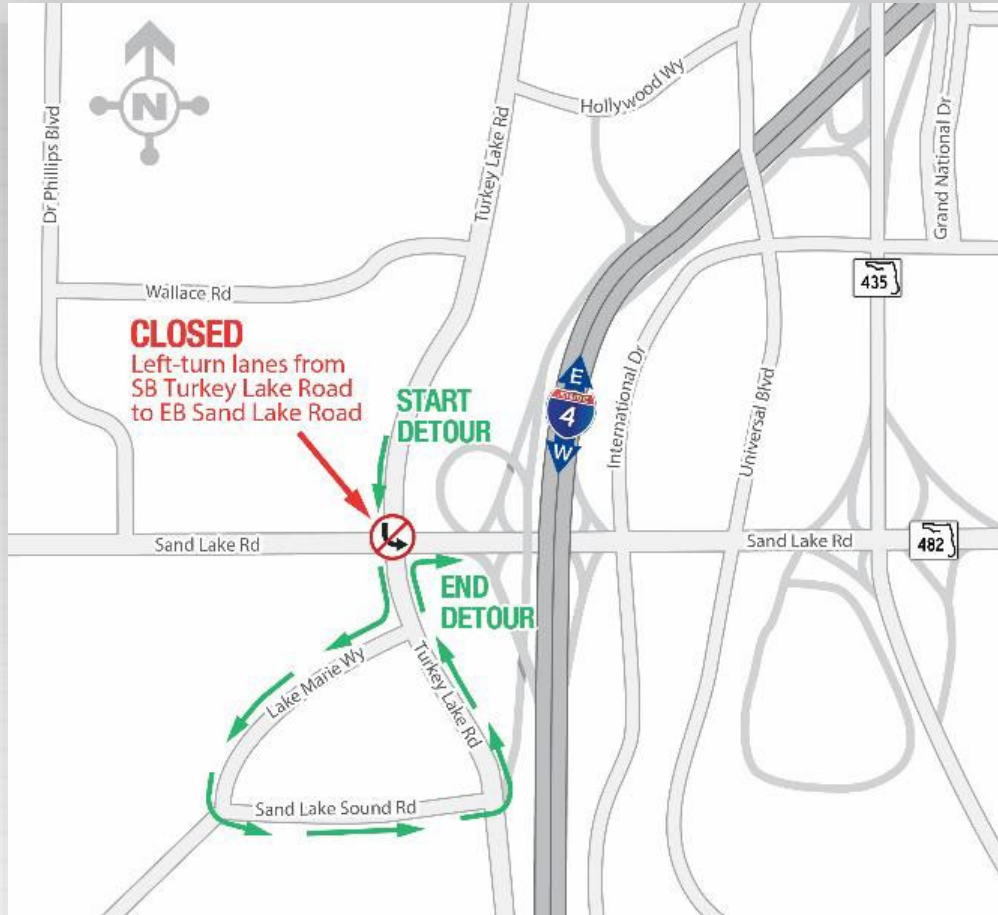



Safety Diversions

- **July 7–9 (overnight)**
 - Northbound Turkey Lake Road at Sand Lake Road
 - Force main installation
 - 11 p.m. to 6 a.m.

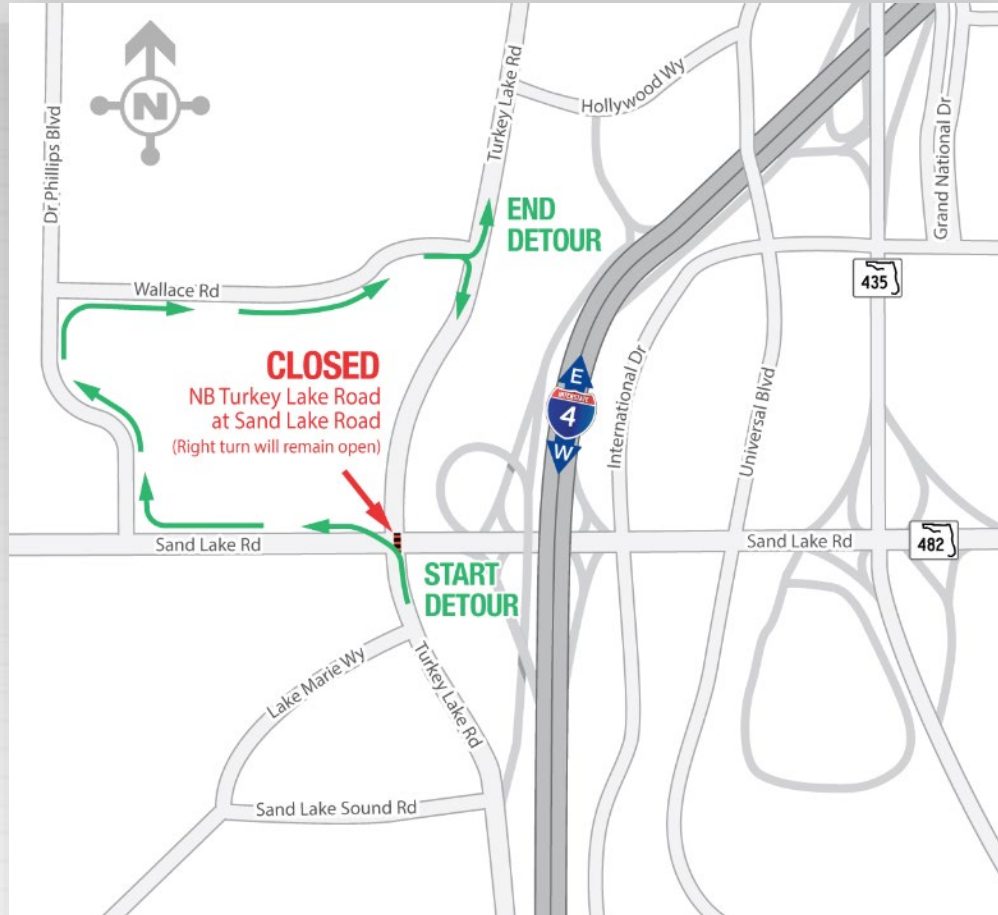



Agenda — New Business

Next meeting: 08/12/2026
