



I-4 and Sand Lake Road Interchange Design-Build

9/18/2024



Status as of September 16, 2024

Days Used	Total Days	% Days Complete	Last Contract Day
533	1,420	37.5%	02/20/2027

Sand Lake 3470				Current Week								Week 1								Week							
Activity ID	Activity Description	Foreman / Sub	Supt	16-Sep	17-Sep	18-Sep	19-Sep	20-Sep	21-Sep	22-Sep	23-Sep	24-Sep	25-Sep	26-Sep	27-Sep	28-Sep	29-Sep	30-Sep	1-Oct	2-Oct	3-Oct	4-Oct	5-Oct	6-Oct			
				MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN			
	Roadway																										
	Halloween Horror nights																										
	MOT Nightly Lane Closures	Dennis Scott	Jamie Leone	N	N						N	N						N	N								
	Excavate/Grade Level Pad 1-2	Kyle Sample	Tyler Sample																								
	Excavate/Grade Level Pad 6-1/TWM9-2	Kyle Sample	Tyler Sample																	X	X	X	X				
	Excavate/Grade Level Pad 103	Kyle Sample	Tyler Sample															X	X								
	Excavate/Grade Pond 207	Kyle Sample	Tyler Sample	X	X	X	X	X	X		X	X	X	X	X												
	Pressure Wash/Paint 3-2 FG line	Kyle Sample	Tyler Sample													X											
	Support RWH (A3 Select Import)	Stephanie C	Tyler Sample															X	X	X	X	X	X				
	WB Embankment 4198-4203 (outside strapzone)	Stephanie C	Tyler Sample	X	X	X	X	X			X	X	X	X	X												
	Grade for Sod WB Ditch 4177-4201	Stephanie C	Tyler Sample	X	X	X																					
BASE350	Place/Finish Lime Rock WB I4 1438-1439 (Ramp J tie-in)	Jessie Wilson	Greg Lemire																								
	Misc. Asphalt EB I4	Jessie Wilson	Greg Lemire	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X					
	Erosion Deficiency Items	Ferold Metelus	Greg Lemire	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X					
	Mowing and Litter Pick Up	Billy Worles	Greg Lemire	SL	SL	SL	SL	SL	X		535	535	535	535	535	X							X				
	Clean Team	Billy Worles	Greg Lemire	X	X	X	X	X	X		X	X	X	X	X	X		X	X	X	X	X	X				
	Drainage / Utilities																										
DRG470	Ramp M S-292 to S-291	Jose Castro C.	Greg Lemire	X	X																						
DRG470	Ramp M S-291 to S-291A	Jose Castro C.	Greg Lemire		X	X	X	X																			
DRG470	Ramp M S-291A to S-277	Jose Castro C.	Greg Lemire								X	X	X	X	X	X											
DRG470	Ramp M S-277 to S-277A	Jose Castro C.	Greg Lemire															X	X	X	X	X	X				
DRG470	Ramp M - Install CS-207 to S-800	Jose Castro C.	Greg Lemire	X	X	X	X	X	X		X	X	X	X	X	X											
	Install S-319 to S-319OF	Jose Castro C.	Greg Lemire																								
DRG470	Ramp M - S-322 to S-322OF (18")	Edward	Greg Lemire		X	X	X	X	X		X	X															
DRG470	Ramp M - S-323 to S-323OF	Edward	Greg Lemire																								
DRG470	Ramp M - S-323 to S-258 Stub-out	Edward	Greg Lemire	X	X	X														X	X	X	X				
DRG470	Ramp M - S-321 to S-321OF	Edward	Greg Lemire																								
DRG470	Ramp M - Install S-275OF to S-275	Edward	Greg Lemire				X	X			X	X	X														
DRG470	Ramp M - Install S-275 to S-276 Stub-Out	Edward	Greg Lemire												X	X	X	X	X								
DRG470	Ramp M - Install S-800 to S-336	Edward	Greg Lemire																	X	X						
DRG470	Ramp M - Install CS-207 to S-800	Edward	Greg Lemire																			X	X				
	Structures																										
SP100																											
OH100	Bridge S Overhangs & Sideforms	Jaime Castillo	James	x	x																						
BEINF110	Rebar B-5	Jaime Castillo	James	X	X	X	X	X	X		X	X	X	X	X	X											
DECK110	Dry run B-5	Jaime Castillo	James															X	X	X	X	X	X				
DECK110	Pour B-5	Jaime Castillo	James																								
		Eusebio Perez	Jose P																								
		Eusebio perez	Jose P																								
OH110/120	B2 Overhangs & Sideforms	Eusebio Perez/Jaime	Jose P		x	x	X	X	X	N	N	N	X	X	X	X											
											N																
	Rebar B-2	Eusebio Perez	Jose P															X	X	X	X	X	X				
	Dry run B-2	Eusebio Perez	Jose P																								
	Pour B-2	Eusebio Perez	Jose P																								
	Organize efco forms to ship out	Eusebio Perez	Jose P	x	x													N									
	SIP B-2	Eusebio Perez	Jose P							n	n	n	n	n			n	n	n	n	n			n			
	Build up S-1.7 Coping	Fransico	Jose P	X	X	X	X	X	X		X	X	X	X	X	X		X	X	X	X	X	X				
	set precast 42in wall S-1							X	X		X	X	X	X	X	X		X	X	X	X	X	X				
		N/P - Night Pour					C - Confirmed or Cure																				
		X - Day Schedule					N - Night																				
		NC - Night Time Confirmed					D-Pile Delivery																				

Sand Lake 3470				Current Week							Week 1							Week 2						
				16-Sep	17-Sep	18-Sep	19-Sep	20-Sep	21-Sep	22-Sep	23-Sep	24-Sep	25-Sep	26-Sep	27-Sep	28-Sep	29-Sep	30-Sep	1-Oct	2-Oct	3-Oct	4-Oct	5-Oct	6-Oct
Activity ID	Activity Description	Foreman / Sub	Spot	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN
	Subs																							
MSE340	Install MSE Wall 5-1	RWH Crew 1	Nate	X	X	X	X	X	X		X	X	X	X	X	X		X	X	X	X	X	X	
MSE170	Install MSE Wall 5-2	RWH Crew 2	Nate	X	X	X	X	X	X		X	X	X	X	X	X		X	X	X	X	X	X	
REINF110	Bridge 2 SIP	Shelby	James							X	X	X												
	Bridge 5 Rebar	Shelby	James	X	X	X	X	X			X	X	X	X	X									
	B1 S.I.P	Shelby	James																					
	12kv Primary Underground Bore Relocation	Duke	John																					
	JVD Barrier Wall on Ramp J	JVD	Nate																					
	JVD 528/SLR Pier Protection	JVD	Nate	X	X	X	X	X																
	Guardrail on Ramp J	Acme Guardrail	Nate																					
	Existing Drainage Cleaning/ Inspection (TLR)	APS	John																					
	Existing Drainage Cleaning/ Inspection (East SLR)	APS	John																					
	Conti																							
	Repairs Light Poles (HI Ranger-10 LP's)	Conti	John																					
	Officers Scheduled																							
	Place 5 if police are scheduled		Note																					
	Orange County		Note																					
	FHP		Note																					
	Critical Protection Services		Note	N	N																			
	Road Closures / Sidewalk																							
	Sandlake Rd Singles Lane Closure	APS	Dennis																					
	Sand Lake Contra-Flow	Lane	Dennis																					
	I-4 Single Lane Closures	Lane	Dennis																					
	Turkey Lake Single Lane Closures	Lane	Dennis																					

N/P - Night Pour	C - Confirmed or Cure
X - Day Schedule	N - Night
NC - Night Time Confirmed	D-Pile Delivery



Phillips
Crossing

Rosen Inn
International



Agenda — Past Project Status

- **Past Project Status — FDOT to review past 7 days**
 - Bridge deck installation (Area 1)
 - Continue installing MSE walls (Area 1)
 - Grade sod on the westbound I-4 embankment
 - Excavate loop ramp (Area 3)
 - Install permanent drainage (Area 3)
 - Maintain temp drainage (Areas 3 and 4)
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Future Project Status

- **Future Project Status — FDOT to review next 7 days**
 - Bridge deck installation (Areas 1, 2 and 3)
 - Continue installing MSE walls (Area 1)
 - Excavate loop ramp (Area 3)
 - Maintain temp drainage (Areas 3 and 4)
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Phillips
Crossing

Rosen Inn
International



Agenda — Future Project Status

- **Future Project Status — FDOT to review next 14 – 21 days**
 - Bridge deck installation (Areas 1, 2 and 3)
 - Continue install MSE walls (Areas 1 and 3)
 - Excavate loop ramp (Area 3)
 - Install permanent drainage (Areas 1 and 3)
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Cleanliness Review

- **Cleanliness Review**
 - Committee's observations over past 7 days
- **Condition Review**
 - Committee's observations over past 7 days
(fencing, wraps, barricades, temporary signage)




Agenda — Old Business

- Public Input or Comments
- Commitments Update
 - Business outreach for potential vegetation removal
 - Fencing and screening
 - New screen design in review
 - Banners
 - Mowing and cleaning
 - Clean Team
 - Ponds



Agenda — Old Business

- **Westbound I-4 ramp to S.R. 528 closure (ramp widening work)**
 - **September 17–20**

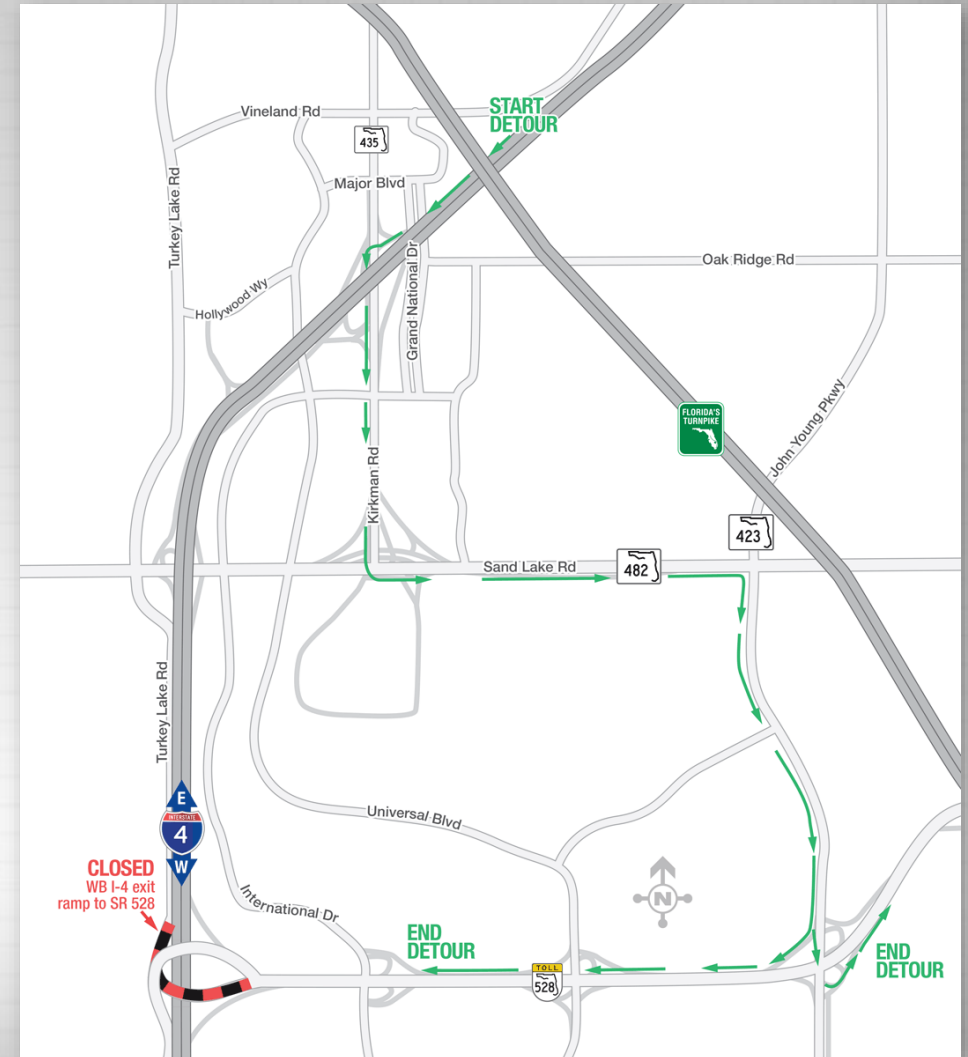



Agenda — New Business

- **Diversions for the S.R. 528 project**
 - **Westbound I-4 from Sand Lake Road to Central Florida Parkway**
 - **September 22–27**
 - **Eastbound and westbound I-4 exit ramps to eastbound S.R. 528**
 - **September 29–October 4**



Agenda — New Business

- Next meeting — 9/25/24
