



I-4 and Sand Lake Road Interchange Design-Build

11/20/2024



Status as of November 18, 2024

Days Used	Total Days	% Days Complete	Last Contract Day
596	1,456	40.9%	03/28/2027

Sand Lake 3470				Current Week								Week 1								Week 2							
				18-Nov	19-Nov	20-Nov	21-Nov	22-Nov	23-Nov	24-Nov	25-Nov	26-Nov	27-Nov	28-Nov	29-Nov	30-Nov	1-Dec	2-Dec	3-Dec	4-Dec	5-Dec	6-Dec	7-Dec	8-Dec			
Activity ID	Activity Description	Foreman / Sub	Supt	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN			
	Roadway							I	I	I	I	I	I	I	I	I	I										
	MOT Nightly Lane Closures	Dennis Scott	Jamie Leone	N	N	N	N			N	N	N						N	N	N	N						
STAB160	Ramp J/SLR tie-in (permanent & temp)	Kyle Sample	Tyler Sample	X	X	X	X	X																			
	Grade Level Pad RW104	Kyle Sample	Tyler Sample								X	X	X														
	Place Embankment WB I4 sta. 4223 - 4234	Kyle Sample	Tyler Sample															X	X	X	X	X					
	Place Embankment Ramp M 1311-1320	Alex	Tyler Sample	X	X	X	X	X																			
	Place Temp Embankment Ramp M	Alex	Tyler Sample								X	X	X														
	Grade for Sod Pond 207	Alex	Tyler Sample	X	X	X	X	X			X	X	X														
	Ramp K Temp Embankment	Alex	Tyler Sample															X	X	X	X	X					
	Ramp J LBR'S	Jessie Wilson	Greg Lemire	X	X	X	X	X				PTO/I.W.	PTO/I.W.														
	Cut Stabilization Ramp J sta. 4190 - B5	Jessie Wilson	Greg Lemire	X	X	X	X					PTO/I.W.	PTO/I.W.														
	Place Lime Rock sta. 4190 - B5	Jessie Wilson	Greg Lemire								X	PTO/I.W.	PTO/I.W.														
	Finish Lime Rock sta. 4190 - B5	Jessie Wilson	Greg Lemire								X	PTO/I.W.	PTO/I.W.					X	X	X	X	X					
	Erosion Deficiency Items	Ferold Metelus	Greg Lemire	X	X	X	X	X			X	X	X					X	X	X	X	X					
	Mowing and Litter Pick Up	Billy Worles	Greg Lemire			SL	SL	SL										SL	SL	SL							
	Clean Team	Billy Worles	Greg Lemire	X	X	X	X	X			X	X	X					X	X	X	X	X					
	Drainage / Utilities																										
	S-110 Turkey Lake	Jose Castro C.	Greg Lemire	X	X	X		PTO/I.C.			PTO/I.C.	PTO/I.C.	PTO/I.C.														
	S-1110A Turkey Lake	Jose Castro C.	Greg Lemire				X	PTO/I.C.			PTO/I.C.	PTO/I.C.	PTO/I.C.														
	S111A Turkey Lake	Jose Castro C.	Greg Lemire					PTO/I.C.			PTO/I.C.	PTO/I.C.	PTO/I.C.														
	S-117 Turkey Lake	Jose Castro C.	Greg Lemire					PTO/I.C.			PTO/I.C.	PTO/I.C.	PTO/I.C.					X	X	X							
	S-119 Turkey Lake	Jose Castro C.	Greg Lemire					PTO/I.C.			PTO/I.C.	PTO/I.C.	PTO/I.C.								X	X					
U-OUC100	Install Water Main Ramp J	Edward	Greg Lemire	X	X	X	X	X	X		X	X	X					X	X	X	X	X					
	Structures																										
DECK110	Dry run B-5	Jaime Castillo	James	X	X	X	X	X			X	X	X														
DECK100	Dry run B-2	Jaime Castillo	James	X	X	X	X	X																			
DECK110	Pour B-5	Jaime/Eusebio	James															N/P	C	C	C	C	C	C			
	form approach slab S-1	Jaime Castillo	Jose P																								
	Gravity wall Ramp M	Francisco	James	X	P	X	X	X			X	P	X							X	X	X	X				
	Build up S-2 Coping	Rafael	Jose P	X	x	x	x	x										X	X	X							
	set precast 36in at S-2 wall	Rafael	Jose P				X	X																			
	form moment slap wall S-2	Rafael	Jose P								X	X	X								X	X					
	Rock at S-2 approach slab	Juan Pinero	James	N	N	N																					
	B-7 Retainer wall	Juan Pinero	James	N	N	N	N																				
	B-7 MATERIAL	Juan Pinero	James								X	X	X					X	X								

N/P - Night Pour
X - Day Schedule
NC - Night Time Confirmed
C - Confirmed or Cure
N - Night
D-Pile Delivery

Sand Lake 3470				Current Week							Week 1							Week 2							
				18-Nov	19-Nov	20-Nov	21-Nov	22-Nov	23-Nov	24-Nov	25-Nov	26-Nov	27-Nov	28-Nov	29-Nov	30-Nov	1-Dec	2-Dec	3-Dec	4-Dec	5-Dec	6-Dec	7-Dec	8-Dec	
Activity ID	Activity Description	Foreman / Sub	Supl	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	
	Subs																								
MSE350	Install MSE Wall 5-2	RWH Crew 1	Nate	X	X	X	X	X																	
MSE200	Install MSE Wall 1-2	RWH Crew 2	Nate	X	X	X	X	X	X		X	X	X					X	X	X	X	X			
MSE180	Install MSE Wall 6-1	RWH Crew 3	Nate	X	X	X	X	X	X		X	X	X					X	X	X	X	X			
MSE360	Install MSE Wall 104	RWH Crew 1	Nate								X	X	X					X	X	X	X	X			
	Shoulder Barrier - Ramp J sta. 1014+60 - 1016+38	JVD	Nate															X	X	X	X	X			
	b5 aproach slabs 1&2	Shelby	Jose P																	X	X	X	X		
	Shift Traffic Outside I4 WB	Oglesby	Nate	NC	NC																				
	I-4 EB Barrier Wall and Attenuator	TCP	Roberto			T	NC			NC	NC	NC													
	North of SL WB I-4	TCP	Roberto																					T	
DRN160	J&B EB 400	CFU	Rainer	X	X	X	X	X			X	X	X					X	X	X	X	X			
	Video New Drainage	APS	Rainer																						
	Lighting Maintenance	Conti	Rainer		X																				
	Bridge 2 Lighting	Conti	Rainer	X	X	X																			
	Wall 5-1	Conti	Rainer	X	X	X	X	X			X	X													
	Ramp K Lighting	Conti	Rainer	X	X	X	X	X			X	X						X	X	X	X	X			
	ITS Conduit North of SLR	Conti/Synergy	Rainer	X	X	X	X	X			X	X						X	X	X	X	X			
	Utilities	UTILITY OWNER	STA																						
	Mini Cell Array Relocation	Verizon	TLR	X	X																				
	Officers Scheduled																								
	Place 5 if police are scheduled		Nate																						
	Orange County		Nate																						
	FHP		Nate	NC	NC	N	N			N	N	N													
	Critical Protection Services		Nate	NC	NC																				
	Road Closures / Sidewalk																								
	Sandlake Rd Singles / Double Lane Closure	OC Utility	Dennis	X	X	X	X																		
	Ramp K Closure	Hubbard	Dennis																						
	Sand Lake Contra-Flow	Lane	Dennis																						
	I-4 Single Lane Closures	Lane	Dennis	X	X	X	X																		
	Turkey Lake Single Lane Closures	Lane	Dennis																						


N/P - Night Pour
 X - Day Schedule
 NC - Night Time Confirmed
 C - Confirmed or Cure
 N - Night
 D-Pile Delivery





Agenda — Past Project Status

- **Past Project Status — FDOT to review past 7 days**
 - Jack and bore under eastbound I-4 north of Sand Lake Road
 - Install bridge lighting (Area 1)
 - Install water main near westbound I-4 entrance ramp (Areas 1 and 2)
 - Bridge deck installation (Areas 1, 2, and 3)
 - Turkey Lake median widening
 - Continue installing MSE walls (Area 1)
 - Excavate loop ramp (Area 3)
 - Install permanent drainage (Area 3)
 - Grade and sod around retention pond
 - Maintain temp drainage (Areas 3 and 4)
 - Utility relocation
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**

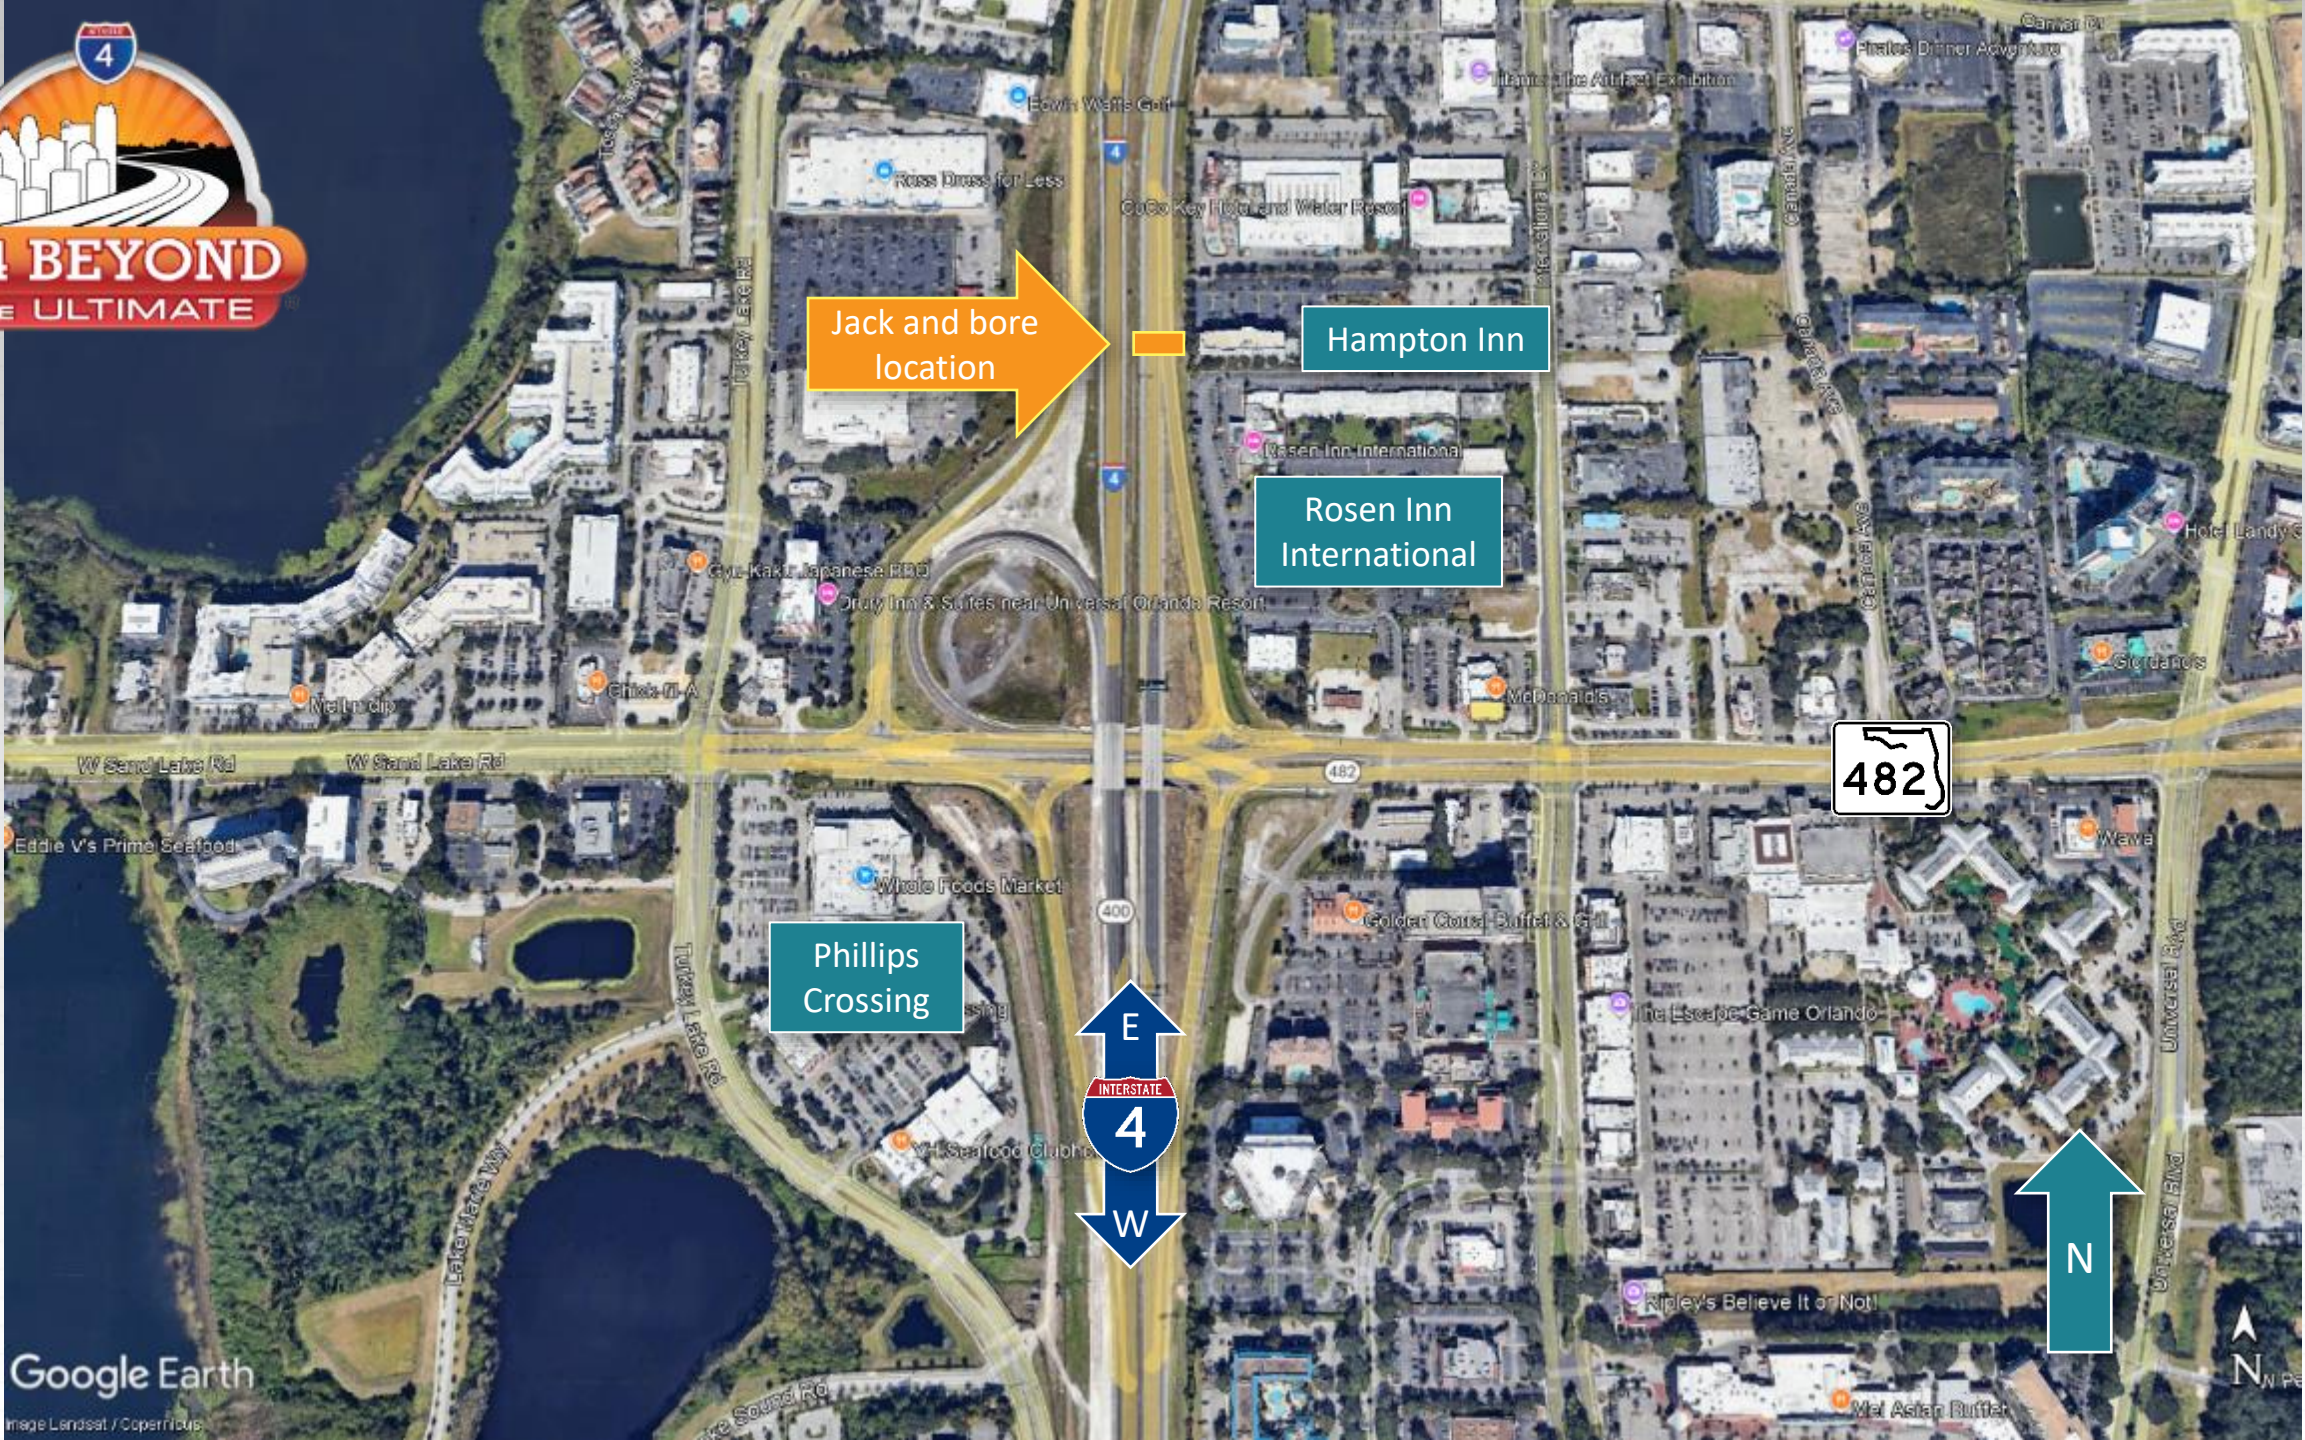





Agenda — Future Project Status

- **Past Project Status — FDOT to review next 7 days**
 - Jack and bore under eastbound I-4 north of Sand Lake Road
 - Place and finish lime rock on the westbound I-4 entrance ramp (Area 1)
 - Install water main near westbound I-4 entrance ramp (Areas 1 and 2)
 - Bridge deck installation (Areas 1, 2, and 3)
 - Turkey Lake median widening
 - Continue installing MSE walls (Area 1)
 - Excavate loop ramp (Area 3)
 - Grade and sod around retention pond
 - Maintain temp drainage (Areas 3 and 4)
 - Utility relocation
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Future Project Status

- **Future Project Status — FDOT to review next 14 – 21 days**
 - Jack and bore under eastbound I-4 north of Sand Lake Road
 - Place and finish lime rock on the westbound I-4 entrance ramp (Area 1)
 - Install water main near westbound I-4 entrance ramp (Areas 1 and 2)
 - Bridge deck installation (Areas 1, 2, and 3)
 - Turkey Lake Road median widening
 - Continue install MSE walls (Areas 1 and 3)
 - Excavate loop ramp (Area 3)
 - Maintain temp drainage (Areas 3 and 4)
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Cleanliness Review

- **Cleanliness Review**
 - Committee's observations over past 7 days
- **Condition Review**
 - Committee's observations over past 7 days
(fencing, wraps, barricades, temporary signage)



Agenda — Old Business

- **Public Input or Comments**
- **Commitments Update**
 - Fencing and screening
 - Mowing and cleaning
 - Clean Team
 - Ponds



Agenda — New Business

- Next meeting — 12/4/24
