



I-4 and Sand Lake Road Interchange Design-Build

04/02/2025



Status as of March 31, 2025

Days Used	Total Days	% Days Complete	Last Contract Day
729	1,478	49.3%	04/19/2027

Sand Lake 3470				Current Week							Week 1							Week 2						
Activity ID	Activity Description	Foreman / Sub	Supt	31-Mar	1-Apr	2-Apr	3-Apr	4-Apr	5-Apr	6-Apr	7-Apr	8-Apr	9-Apr	10-Apr	11-Apr	12-Apr	13-Apr	14-Apr	15-Apr	16-Apr	17-Apr	18-Apr	19-Apr	20-Apr
				MO	TUE	WED	THU	FRI	SAT	SUN	MO	TUE	WED	THU	FRI	SAT	SUN	MO	TUE	WED	THU	FRI	SAT	SUN
	Roadway																							
	Ramp J shift and Open	Kyle Sample	Sample				X																	
	Permanent Ramp M "eyebrow" Base	Kyle Sample	Sample															X	X	X	X	X		
MSE240/250	Grade for Curb & Gutter/Sidewalk Ramp M "eyebrow"	Kyle Sample	Sample															X	X	X	X	X		
	RW102/103	Kyle Sample	Sample	X	X	X	X	X	X		X	X	X	X	X	X								
EW300	Ramp K Relocate Utilities	Conti	Rainer	X	X	X	X	X																
	Ramp K Embankment	Dennis Scott	Sample								X	X	X	X										
	Ramp K Stone (Temp)	Dennis Scott	Sample												X	X		X	X					
	Ramp K Traffic swap	Dennis Scott	Sample																					X
	Support JVD (Ex/Grade/Backfill: Ramp M Shoulder Barrier)	Dennis Scott	Sample	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X		
BAG220/270	Support Blount Sanford (Ex/Grade/Backfill: 14 WB/Ramp M)	Dennis Scott	Sample	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X		
	Place/Finish Lime Rock 14 WB sta. 4217 - 4245	Jessie Wilson	Greg Lemire	X	X	X	X	X	X						X			X	X	X	X	X		
	Mix/Plc/Balance Ramp M 1301 - 1310	Jessie Wilson	Greg Lemire								X	X	X	X	LBR			LBR	LBR	LBR	LBR			
	Grade Stab Ramp M 1301 - 1310	Jessie Wilson	Greg Lemire																			X	X	
	Drainage / Utilities																							
	Install S-212 to S-213 18" Pipe	Jose Castro C.	Greg Lemire	X	X	X	X																	
	Install S-215 to S-216 18" Pipe	Jose Castro C.	Greg Lemire				X	X	X															
	Install 42" steel pipe	Jose Castro C.	Greg Lemire								X	X	X	X	X	X								
	Install S320A to S-334	Jose Castro C.	Greg Lemire															X	X	X				
	Install S-334 to S-335 18" pipe	Jose Castro C.	Greg Lemire																		X	X	X	
	Install S-241A to S-241OF 54" Pipe	Edward	Greg Lemire	X																				
	Install S-241A to S-809 48" Pipe	Edward	Greg Lemire		X	X	X																	
	Install S-809 to S-811 48" Pipe	Edward	Greg Lemire					X	X		X		X	X										
	Install S-811 to S-812 48" Pipe	Edward	Greg Lemire									X	X	X										
	Install S-812 to S-808 48" Pipe	Edward	Greg Lemire												X	X		X	X	X				
	Install S808 to S-325 18" Pipe	Edward	Greg Lemire															X	X	X		X	X	
	Install S-808 to S-810 42" Pipe	Edward	Greg Lemire																		X	X	X	
	Structures																							
	demo endbent B7	Eusebio Perez	Jose Perez		X	X	X																	
	remove temp bracing span 2	jaime castillo	jose perez							N	N	N	N	N										
	Strip Overhang B1	jaime castillo	Jose perez										N	N	N									
DOCK300/120	strip bulkhead/keyway B1	Jaime Castillo	James		X	X																		
	Dry run B1	Jaime Castillo	James	X	X	X	P																	
	gravity wall ramp M	Francisco	Jose P	X	X	X	X	X			P	X	X	X	P									
	Form coping plain under B5,B1&B2	Francisco	Jose P	X	X	X	X	X																
	pylon footer RW1-1	Victor Medina	Jose P	X	X	X	X	P																
	endbent 1 B7	Victor Medina	Jose P								X	X	X	X	X			X	X	X	P			
	rub and patch	Rafael	jose P	X	X	X	X	X																
	Subs																							
MSE240	Install MSE Wall 103	RWH Crew 2	Nate	X	X	X	X	X																
MSE250	Install MSE Wall 102	RWH Crew 2	Nate	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X		
	Shoulder Barrier (WB North)	JVD	Roberto	X	X	X	X	X																
	Shoulder Barrier (WB/Ramp J)	JVD	Roberto								X	X	X	X	X									
	Half-Wall (RW1-1)	JVD	Roberto															X	X	X				
	Grade Separated Median Barrier Wall 14 WB N	Blount Sanford	Roberto	X	X	X	X	X																
	Median Barrier Wall 14 WB N	Blount Sanford	Roberto			X	X	X			X	X	X	X	X			X	X	X	X			
	Relocate Kwall Ramp L	TCP	Roberto	N	N																			
	Lighting																							
	Ramp M Gravity Wall Conduit & Embedded Boxes	Conti	Rainer															X	X	X	X	X		
	Ramp M Shoulder Wall Conduit & Embedded Boxes	Conti	Rainer															X	X	X	X	X		
	Ramp M Shoulder Lights	Conti	Rainer	X	X	X	X	X			X	X	X	X	X									
	Bridge & Underdeck Conduit	Conti	Rainer																		X	X		
	ITS																							
	ITS Conduit I-4 EB Sta: 1433 - 1330	Conti/Synergy	Rainer	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X		
	Ramp M WWDS	Conti	Rainer								X	X	X	X	X			X	X	X	X	X		
	Ramp M Temp Bore	Conti/Synergy	Rainer																					
	Ramp K WWDS	Conti	Rainer	X	X	X	X	X																
	Signals																							
	Ramp M Temp Strain Poles	Conti	Rainer	X	X	X	X	X																
	Ramp M/SLR Signal Head	Conti	Rainer								X	X	X	X	X									
	Ramp J Temp Ped Poles 2	Conti	Rainer	X	X	X																		
	SPM																							
	Ramp K GMS	Conti	Rainer	X	X	X	X	X																
	Install J&B SLR CS-206A - S-2000	CFU	Rainer															X	X	X	X	X		

N/P - Night Pour	T-N - Tentative
X - Day Schedule	N - Night
NC - Night Time Confirmed	D-Pile Delivery
C - Confirmed or Cure	

Sand Lake 3470			Current Week								Week 1							Week 2						
Activity ID	Activity Description	Foreman / Sub	Supt	31-Mar	1-Apr	2-Apr	3-Apr	4-Apr	5-Apr	6-Apr	7-Apr	8-Apr	9-Apr	10-Apr	11-Apr	12-Apr	13-Apr	14-Apr	15-Apr	16-Apr	17-Apr	18-Apr	19-Apr	20-Apr
	Utilities	UTILITY OWNER	STA	MO	TUE	WED	THU	FR	SA	SUN	MO	TUE	WED	THU	FR	SA	SUN	MO	TUE	WED	THU	FR	SA	SUN
	Pole Relocation: Gravity Wall (1/20-5/14/25: 64 Days UWS)	Duke	TLR	X	X	X	X				X	X	X	X				X	X	X	X			
	Sand Lake Road Closures / Sidewalk																							
	Sand Lake Rd & Ramps																							
	Sand Lake Contra-Flow WB	Dennis	Jamey	N	N	N	N-C			N-C	N-C	N-C	N-C	N-C			N-C	N-C	N-C	N-C	N-C			
	Sand Lake Contra-Flow EB	Dennis	Jamey	N	N	N	N-C			N-C	N-C	N-C	N-C	N-C			N-C	N-C	N-C	N-C	N-C			
	Ped Opening South Side						X																	
	Ramp K opening (4/27/25)																							
	Ramp L (TCP)	TCP	Jamey	N-C	N-C	N	N																	
	Ramp J (McShea)	McShea	Jamey	N	N	N	N-C																	
	Ramp M1 Eyebrow opening (5/7/25)																							
	I-4 EB																							
	I-4 Single Lane Closures EB	Dennis	Jamey	N	N	N	N																	
	I-4 Double Lane Closures EB	Dennis	Jamey																					
	I-4 WB																							
	I-4 Single Lane Closures WB	Dennis	Jamey	N	N	N	N																	

N/P - Night Pour	T-N - Tentative
X - Day Schedule	N - Night
NC - Night Time Confirmed	D-PILE Delivery
C - Confirmed or Cure	



Phillips
Crossing

Rosen Inn
International





Agenda — Future Project Status

- **Past Project Status — FDOT to review past 7 days**
 - Jack and bore (Areas 2 and 3)
 - Bridge deck installation (Areas 1, 2, and 3)
 - Place lime rock (Areas 2 and 3)
 - Maintaining existing and installing new Wrong-Way Vehicle Detection Systems (Areas 3, 6, and 7)
 - Lighting (Areas 2, 3, 5, 6, and 7)
 - Turkey Lake median widening
 - Continue installing MSE walls (Area 1)
 - Utility relocation
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Jack and Bore





Agenda — Future Project Status

- **Future Project Status — FDOT to review next 7 days**
 - Jack and bore (Areas 2 and 3)
 - Embankment work (Areas 6 and 7)
 - Bridge deck installation (Areas 1, 2, and 3)
 - Place lime rock (Areas 2 and 3)
 - Continue installing MSE walls (Area 1)
 - Maintaining existing and installing new Wrong-Way Vehicle Detection Systems (Areas 3, 6, and 7)
 - Turkey Lake median widening
 - Lighting (Areas 6 and 7)
 - Utility relocation
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Future Project Status

- **Future Project Status — FDOT to review next 14 – 21 days**
 - Jack and bore (Areas 2 and 3)
 - Bridge deck installation (Areas 1, 2, and 3)
 - Continue installing MSE walls (Area 1)
 - Place lime rock (Areas 2 and 3)
 - Maintaining existing and installing new Wrong-Way Vehicle Detection Systems (Areas 3, 6, and 7)
 - Turkey Lake median widening
 - Utility relocation
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Cleanliness Review

- **Cleanliness Review**
 - Committee's observations over past 7 days
- **Condition Review**
 - Committee's observations over past 7 days
(fencing, wraps, barricades, temporary signage)




Agenda — Old Business

- **Public Input or Comments**
- **Commitments Update**
 - Fencing and screening
 - Mowing and cleaning
 - Clean Team
 - Ponds



Agenda — New Business

- **Sidewalk diversion**
 - Overnight Thursday, April 3
 - Diverting pedestrian traffic from the north side to the south side

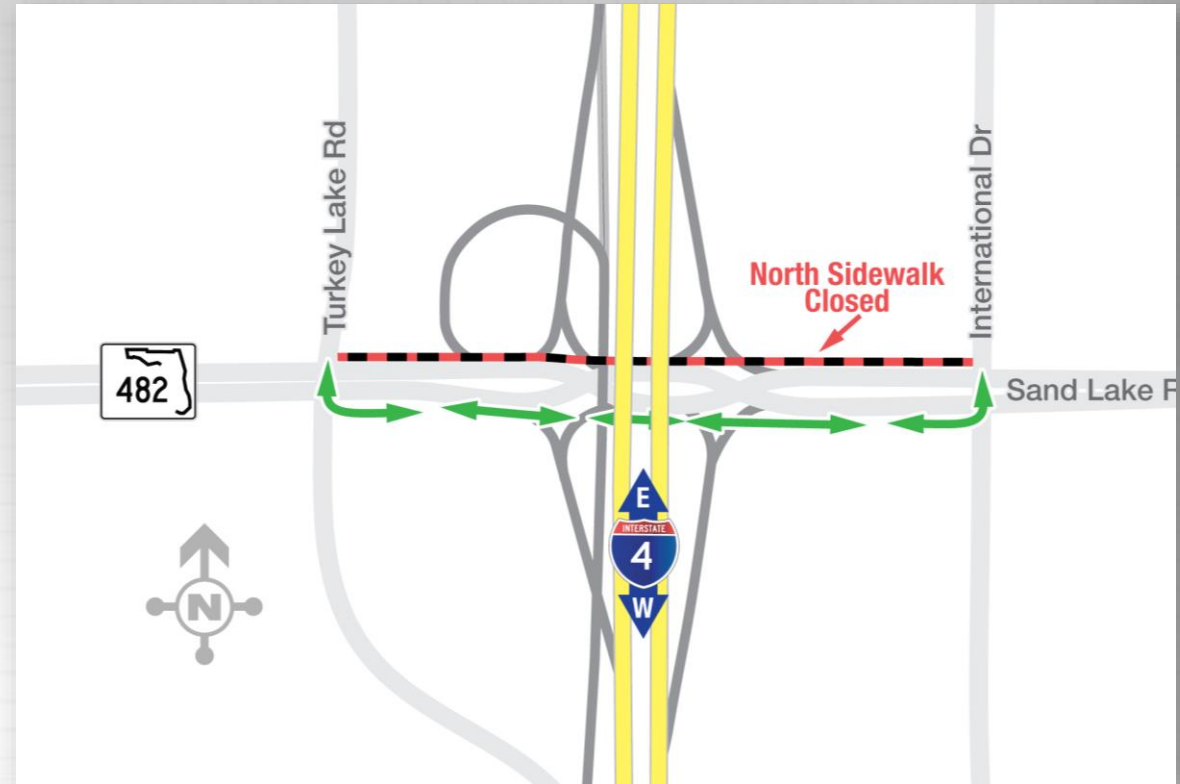



Safety Diversions

- Bridge deck pour over Sand Lake Road
 - Bridge 1
 - North side
 - Thursday, April 3
 - Overnight safety diversions





Safety Diversions

- Westbound I-4 entrance ramp from Sand Lake Road
 - April 3 – 5
 - 10 p.m. – 5 a.m.





Agenda — New Business

- Next meeting: 04/09/25
