



I-4 and Sand Lake Road Interchange Design-Build

11/05/2025



Status as of November 3, 2025

Days Used	Total Days	% Days Complete	Last Contract Day
946	1,732	54.6%	12/29/2027

Sand Lake 3470				Current Week								Week 1								Week 2							
Activity ID	Activity Description	Foreman / Sub	Supt	3-Nov	4-Nov	5-Nov	6-Nov	7-Nov	8-Nov	9-Nov	10-Nov	11-Nov	12-Nov	13-Nov	14-Nov	15-Nov	16-Nov	17-Nov	18-Nov	19-Nov	20-Nov	21-Nov	22-Nov	23-Nov			
				MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN			
	Roadway																										
MSE280	Demo/Exc. MSE wall RW3-2	Marcos C.	Tyler								X	X	X	X	X												
MSE270	Demo/Exc. MSE wall RW3-1	Marcos C.	Tyler								X	X	X	X	X			X	X	X	X	X					
EW510/EW520	Place Embankment I4 XL's (South)	Marcos C.	Tyler	X	X	X	X	X			X	X	X	X	X												
BW380	Grade for Median Barrier I4 EBXL (North)	Marcos C.	Tyler	X	X	X	X	X										X	X	X	X	X					
DEMO160	Rmv Laggng TW1-1	Marcos C.	Tyler															X		X		X					
TW150	Subsoil Excavation (north median)	Stephanie C	Tyler	X	X	X	X	X																			
EW530	Place Embankment Ramp M2	Stephanie C	Tyler								X	X															
EW370	Exc/Grade Pond 206B	Stephanie C	Tyler								X	X	X	X	X			X	X								
EW360	Exc/Grade Pond 206	Stephanie C	Tyler																	X	X	X					
BASE160/200	Fin Limerock Ramp M2/M3	Jessie Wilson	Tyler	X	X	X	X																				
STAB280	Sweeten Ramp M2 (RW6-2)	Jessie Wilson	Tyler					X	X																		
STAB280	Box Subgrade Ramp M2 (RW6-2)	Jessie Wilson	Tyler								LBR	LBR	LBR	LBR	LBR												
BASE330	Plc Limerock Ramp M2 (RW6-2)	Jessie Wilson	Tyler															X	X	X							
BASE330	Fin Limerock Ramp M2 (RW6-2)	Jessie Wilson	Tyler																	X	X	X					
STAB330	Balance/Sweetener/Mix I4 XL's 1454-1477	Jessie Wilson	Tyler								X	X	X	X	X			LBR	LBR	LBR	LBR	LBR					
	Sand Lake off and on ramps to I-4 - Trash pickup and Mowing	Billy Worles	Greg L				X	X													X	X					
	Turkey Lake Sidewalks, Trash pickup and Mowing	Billy Worles	Greg L								X	X	X														
	Kirkman ramp - Trash pickup and Mowing	Billy Worles	Greg L											X	X												
FLAT120	Turkey Lake Assist Jvd	Larry Rapp	Greg L					X				X	X														
BASE140	Excavate,place in lieu of,base and asphalt for separator TL Rd	Larry Rapp	Greg L									X	X	X	X	X		X	X	X	X	X	X				
BASE140	Excavate place lime rock in lieu of and base for E-curb TL Rd	Larry Rapp	Greg L	X	X	X	X	X	X		X																
	Drainage / Utilities																										
DRG290	Install CS-160 to S-82 (24")	Jose Castro C.	Greg L	X	X	X												X	X	X							
DRG290	Install S-82 to S-82OF (24")	Jose Castro C.	Greg L				X	X	X		X	X									X	X	X				
DRG290	Install S-81 S-81A (42")	Jose Castro C.	Greg L										X	X	X	X											
DRG290	Install S-81OF to S-81A (42")	Jose Castro C.	Greg L															X	X	X							
DRG290	Install S-80 to S-81 (42")	Jose Castro C.	Greg L																			X	X				
DRG290	Pave temp sidewalk for S-80	Jose Castro C.																			X						
DRG220	Install Trench Box for Jack and Bore	Isalas Barcenas	Greg L	X	X																						
DRG220	Install CS-206 (36") pipe	Isalas Barcenas	Greg L			X	X																				
DRG220	Install CS-206A (36")	Isalas Barcenas	Greg L					X	X		X																
DRG220	Install S-806B connect to S-806A run	Isalas Barcenas	Greg L									X	X	X													
DRG220	Install S-2000 to S-2001 (36")	Isalas Barcenas	Greg L												X	X											
DRG430	Install WM casing SL @ Whole Foods	Isalas Barcenas	Greg L															X	X	X							
DRG430	Excavete and Prep CIP S-506	Isalas Barcenas	Greg L																		X	X	X				
DRG430	Install S-545 to S-549 (18")	Edward Benitez	Greg L	X																							
DRG430	Install S-545 to S-544 (18")	Edward Benitez	Greg L		X	X																					
DRG430	Install S-544 to S-540 (18")	Edward Benitez	Greg L				X	X	X	N	N	N	N	N													
DRG430	Install S-590 to S-591 (15")	Edward Benitez	Greg L															X	X								
DRG430	Install S-592 to S-593 (15")	Edward Benitez	Greg L																	X	X	X	X				
	Structures																										
	<u>Pylons</u>																										
SUBS280	form top section pylon 1-1	Victor Medina	Jose Perez	P	C	C	C	C	C	C																	
SUBS280	remove forms/ready for shipment pylon 1-1 top	Victor Medina	Jose Perez								X	X	X	X	X												
SUBS280	rub and patch pylons	Raffel Nunez/victor	Jose Perez		X	X	X	X																			

Sand Lake 3470				Current Week								Week 1								Week 2							
Activity ID	Activity Description	Foreman / Sub	Supt	3-Nov	4-Nov	5-Nov	6-Nov	7-Nov	8-Nov	9-Nov	10-Nov	11-Nov	12-Nov	13-Nov	14-Nov	15-Nov	16-Nov	17-Nov	18-Nov	19-Nov	20-Nov	21-Nov	22-Nov	23-Nov			
				MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN			
	<u>Bridge #3</u>																										
PILE230	Drive pile endbent 1	Juan Pinero	James O'Neill	D	D	X	X	X	X																		
PILE240	Cut Pile pier 2 WB/Excavate WB	Jaime/Victor	Jose Perez																								
SUBS160	Form WB/EB Footers	Francisco/Eusiabo	Jose perez	E/B	W/B	C	C	C	C	C																	
SUBS170	Pre Form columns	Jaime/Eusiabo	James O'Neill								X	X	X	X	X												
SUBS160	Strip/backfill/remove trench boxes	Jaime/Eusiabo	Jose Perez				X	X	X		X	X	X	X	X	X		X									
SUBS690	Pre Form caps	Jaime/Eusiabo	James O'Neill											X	X	X		X	X	X	X	X	X	P			
SUBS660	Form EB 1	Victor/Eusiabo	Jose Perez															X	X	X	X	X	X				
	Subcontractor																										
FLAT120	Form/Pour separator TL Rd	JVD	Roberto								X	X	X	X													
FLAT160	Form/Pour E curb TL Rd	JVD	Roberto												X			X	X	X	X						
BW290	Median Barrier I4 XL's (622S - 6239)	Blount Sanford	Roberto	X	X	X	X	X			X	X	X	X	X												
TW130/150	Install TW 4-1 and 4-2	Maylor	Nate	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X					
MSE280	Construct Wall 3-2 (Wirewall 4-2)	RWH	Nate								X	X	X	X	X			X	X	X	X	X					
	Refreash Skip markers on I-4 WB	McShea	Nate	N																							
AREA 3	Install 36" J&B S-500 - S500A	CFU	Greg	X	X	X	X	X																			
AREA 3	Install 36" J&B S-500A - S500B	CFU	Greg								X	X	X	X	X												
AREA 3	Install 36" J&B S-456 - S83	CFU	Greg															X	X	X	X	X					
	<u>Lighting</u>																										
LGHT110	Light Pole Install I4WB North of SLR	Conti	Rainer	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X					
	<u>ITS</u>																										
ITS120	ITS Pole 73.6 WB-B Conduit	Conti	Rainer								X	X	X														
	<u>Toll Plaza</u>																										
TOLL200	Slab Pour	Conti	Rainer				X																				
	Utilities	UTILITY OWNER	STA																								
	Gas Line Relocation (SLR/TLR Intersect Field Meet)	Teco	SLR	N	N	N	N	N																			
	Sand Lake Road Closures / Sidewalk																										
	<u>Sand Lake Rd & Ramps</u>																										
	Sand Lake WB Contra flow (Bridge Demo)	James	Jamey	X	X	X	X			X	X	X	X	X			X	X	X	X	X						
	Sand Lake EB Contra flow (Bridge Demo)	James	Jamey	X	X	X	X			X	X	X	X	X			X	X	X	X	X						
	Turekylake Rd North & South direcsctions for drainage	Lane	Jamey							X	X	X	X	X			X	X	X	X	X						
	<u>I-4 EB</u>																										
	I-4 Single Lane Closures EB	Lane	Jamey	X	X	X	X			X	X	X	X	X			X	X	X	X	X						
	<u>I-4 WB</u>																										
	I-4 Single Lane Closures WB	Lane	Jamey	X	X	X	X			X	X	X	X	X			X	X	X	X	X						



Phillips
Crossing

Rosen Inn
International





Agenda — Current Project Status

- **Past Project Status — FDOT to review past 7 days**
 - Jack and bore (Areas 1 and 3)
 - Pile set checks (Area 8)
 - Pylon work (Areas 2 and 3)
 - Signal and sign foundation work
 - Install lighting on westbound I-4 (Areas 3 and 4)
 - Old westbound I-4 lanes demolition
 - MSE wall demolition (Areas 2 and 3)
 - Embankment work (Area 3)
 - Turkey Lake Road median widening
 - Finish lime rock (Area 3)
 - Drainage work (Areas 1, 2, and 3)
 - Utility relocation
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**









Agenda — Future Project Status

- **Future Project Status — FDOT to review next 7 days**
 - Storm drainage work on Sand Lake Road (Area 7)
 - Pile set checks (Area 8)
 - Signal and sign foundation work
 - Install lighting on westbound I-4 (Areas 3 and 4)
 - Old westbound I-4 lanes demolition
 - Excavate and grade ponds
 - Install MSE walls (Areas 2 and 3)
 - Embankment work (Area 2)
 - Drainage work (Areas 1, 2, and 3)
 - Utility relocation
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Future Project Status

- **Future Project Status — FDOT to review next 14 – 21 days**
 - Planter wall work (Areas 2 and 3)
 - Signal and sign foundation work
 - Install lighting on westbound I-4 (Areas 3 and 4)
 - Excavate and grade ponds
 - Install MSE walls (Areas 2 and 3)
 - Embankment work (Area 2)
 - Drainage work (Areas 1, 2, and 3)
 - Place lime rock (Area 3)
 - Install watermain casing (Area 1)
 - Utility relocation
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Cleanliness Review

- **Cleanliness Review**
 - Committee's observations over past 7 days
- **Condition Review**
 - Committee's observations over past 7 days
(fencing, wraps, barricades, temporary signage)




Agenda — Old Business

- **Public Input or Comments**
- **Commitments Update**
 - Fencing and screening
 - Mowing and cleaning
 - Clean Team
 - Ponds



Safety Diversions

- November 5 and 6
 - Westbound I-4 exit ramp to eastbound S.R. 528
 - 10 p.m. – 6 a.m.

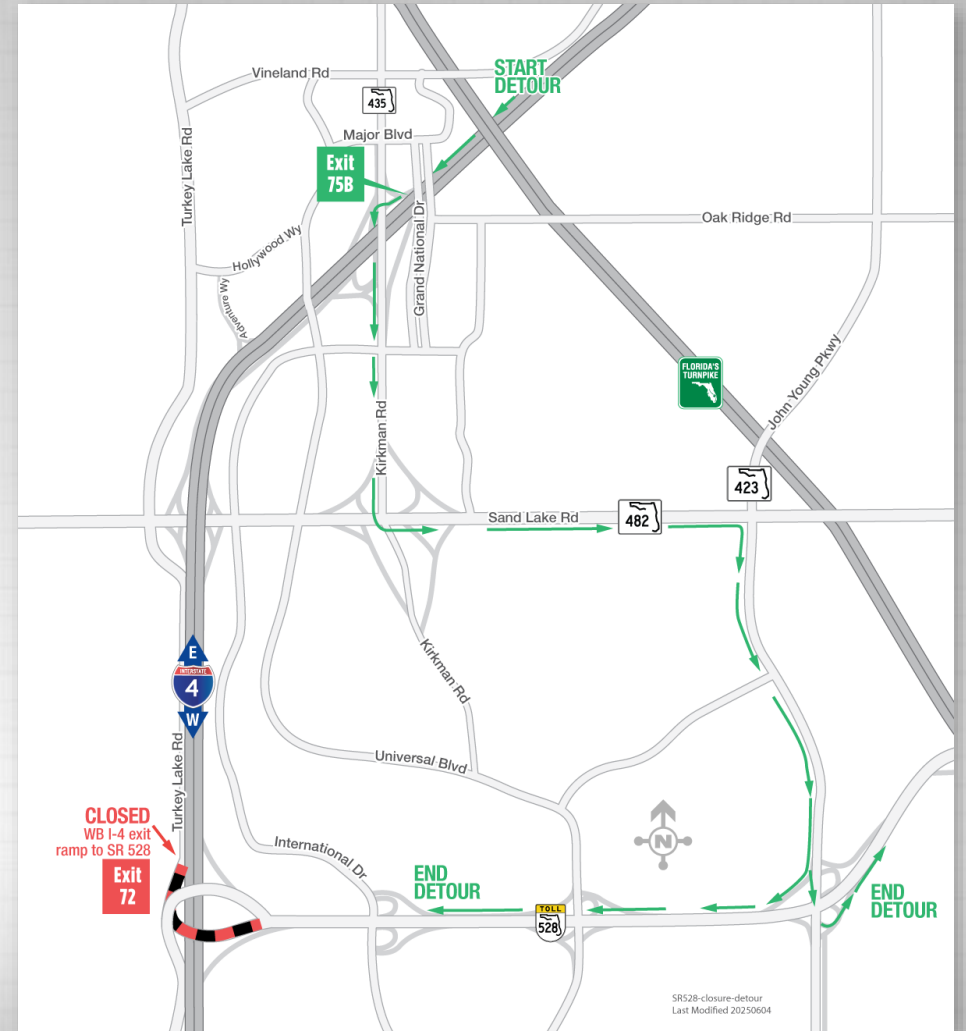



Agenda — New Business

Next meeting: 11/12/25
