



# I-4 and Sand Lake Road Interchange Design-Build

**11/19/2025**

[I4Beyond.com](http://I4Beyond.com)



# Status as of November 17, 2025

Days Used	Total Days	% Days Complete	Last Contract Day
960	1,734	55.4%	12/31/2027

Sand Lake 3470				Current Week								Week 1								Week 2							
Activity ID	Activity Description	Foreman / Sub	Supt	17-Nov	18-Nov	19-Nov	20-Nov	21-Nov	22-Nov	23-Nov	24-Nov	25-Nov	26-Nov	27-Nov	28-Nov	29-Nov	30-Nov	1-Dec	2-Dec	3-Dec	4-Dec	5-Dec	6-Dec	7-Dec			
				MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN			
	Roadway																										
MSE270	Demo/Exc. MSE wall RW3-1	Marcos C.	Tyler	X	X	X	X	X			X	X	X														
	Exc/Grade Pond 206/206B	Marcos C.	Tyler	X	X	X	X	X			X	X	X					X	X	X	X	X					
BW380	Grade for Median Barrier I4 EBXL (North)	Marcos C.	Tyler	X	X	X	X	X																			
	Place Embankment North/South XL's	Stephanie C	Tyler	X	X	X	X	X			X	X	X					X	X	X							
	Backfill B7 & B8 Backwalls	Stephanie C	Tyler																		X	X	X				
BASE330	Plc Limerock Ramp M2 (RW6-2)	Jessie Wilson	Tyler	X	X	X																					
BASE330	Fin Limerock Ramp M2 (RW6-2)	Jessie Wilson	Tyler			X	X	X			V	V	V					X	X	X							
STAB330	Balance/Sweetener/Mix I4 XL's 1454-1477	Jessie Wilson	Tyler	LBR	LBR	LBR	LBR	LBR																			
STAB330	Box Subgrade I4 XL's 1454-1477	Jessie Wilson	Tyler								X	X	X					X	X	X							
BASE380	Plc/Fin Limerock I4 XL's 1454-1477																				X	X	X				
	Clean Team Sandlake Sidewalks, Trash pickup and Mowing	Billy Worles	Greg L	X	X	X																					
	Snad lake off and on ramps to I-4 - Trash pickup and Mowing	Billy Worles	Greg L				X	X												X	X	X					
	Turkey Lake Sidewalks, Trash pickup and Mowing	Billy Worles	Greg L								X	X	X														
	Kirkman ramp - Trash pickup and Mowing	Billy Worles	Greg L															X	X								
BASE140	Excavate place lime rock in lieu of base/asphalt for separator TL Rd	Larry Rapp	Greg L	X	X	X	X	X	x		X	X	X														
BASE140	Excavate place lime rock in lieu of and base for E-curb TL Rd	Larry Rapp	Greg L															X	X	X	X	X					
	Drainage / Utilities																										
DRG290	Pour S-820F Miter	Jose Castro C.	Greg L	X																							
	Place S-820F Rip Rap	Jose Castro C.	Greg L		X																						
DRG290	Install S-81 S-81A (42")	Jose Castro C.	Greg L								X	X	X														
DRG290	Install S-810F to S-81A (42")	Jose Castro C.	Greg L			X	X	X	X																		
DRG290	Install S-80 to S-81 (42")	Jose Castro C.	Greg L																	X	X	X					
DRG290	Pave temp sidewalk for S-80	Jose Castro C.	Greg L															X	X								
DRG220	Install CS-206 (36") pipe	Isalas Barcenas	Greg L	X	X	X																					
DRG220	Install CS-206 to CS-206A (36")	Isalas Barcenas	Greg L				X	X	X																		
DRG220	Install S-806B connect to S-806A run (54")	Isalas Barcenas	Greg L								X	X	X					X	X								
DRG220	Install S-2000 to S-2001 (36")	Isalas Barcenas	Greg L																	X	X	X	X				
DRG430	Excavate and Prep CIP S-506	Isalas Barcenas	Greg L				X	X	X																		
DRG430	Install S-590 to S-591 (15")	Edward Benitez	Greg L	X	X																						
DRG430	Install S-592 to S-593 (15")	Edward Benitez	Greg L			X	X	X	X																		
DRG430	Install S-549 to S-550 With conlfit box(s)	Edward Benitez	Greg L								X	X	X						X	X							
	Install FM Valves @ Whole Foods	Edward Benitez	Greg L															X									
	Structures																										
	<u>Pylons</u>																										
SUBS280	remove forms/ready for shipment pylon 1-1 top	Victor Medina	Jose Perez	x	x	x	x	x			x	x	x														
SUBS280	rub and patch pylons	Raffel Nunez/victor	Jose Perez															x	x	x	x	x					
	<u>Planter wall</u>																										
CIP120	Form planter wall 1-1	Jalme Castillo /Felepe	Jose Perez	x	x	x	x	x			x	x	x					x	P								
	rub and patch planter wall 1-2	Fransico	Jose Perez																x	x	x	x					
	<u>Bridge #3</u>																										
SUBS180	Pour columns	Eusebio Perez	James O'Neill	N/P	c	C	C	C	C	C	c	c															
SUBS180	Strip/backfill/remove trench boxes	Eusebio Perez	Jose Perez		N	N	N			N	N																
SUBS660	Form EB 1	Victor/Eusiabo	Jose Perez			N	N	N			x	X	X					X	x	x	x	x					
SUBS660	Form caps	Jalme/Eusiabo	James O'Neill															N	N	N	N			N			
SUBS670	Form EB 3	Victor/Eusiabo	Jose Perez								X	X	X														
	Subcontractor																										
FLAT120	Form/Pour separator TL Rd	JVD	Roberto		X	X	X																				
FLAT160	Form/Pour E curb TL Rd	JVD	Roberto		X	X	X																				



Sand Lake 3470				Current Week								Week 1								Week 2							
Activity ID	Activity Description	Foreman / Sub	Supt	17-Nov	18-Nov	19-Nov	20-Nov	21-Nov	22-Nov	23-Nov	24-Nov	25-Nov	26-Nov	27-Nov	28-Nov	29-Nov	30-Nov	1-Dec	2-Dec	3-Dec	4-Dec	5-Dec	6-Dec	7-Dec			
				MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN			
BW190	Half Wall Ramp M2	JVD	Roberto		X	X	X																				
BW290	Median Barrier I4 XL's (6226 - 6239)	Blount Sanford	Roberto		X	X	X																				
TW130/150	Install TW 4-1 and 4-2	Maylor	Nate	X	X	X	X	X			X	X	X														
MSE280	Construct Wall 3-2 (Wirewall 4-2)	RWH	Nate	X	X	X	X	X			X	X	X														
MSE270	Construct Wall 3-1 (Wirewall 4-1)	RWH	Nate																	X	X	X					
PAVE350/210	Pave Ramps M, M2, & M3	Hubbard	Nate														X	X	X	X	X			X			
	<u>Lighting</u>																										
	Light Pole Install I4WB North of SLR	Conti	Rainer	X	X	X	X	X																			
	<u>SPM</u>																										
	Drill Shaft OHC 5	Conti/Reliable	Rainer														X	X									
	Drill Shaft OHC 6	Conti/Reliable	Rainer								X	X															
	Drill Shaft OHC 8	Conti/Reliable	Rainer				X	X																			
	Drill Shaft OHC 11	Conti/Reliable	Rainer		X	X																					
	Drill Shaft OHC 16	Conti/Reliable	Rainer																	X	X						
	<u>Utilities</u>	UTILITY OWNER	STA																								
	SLR Bore across I-4	Summit	SLR	X	X	X																					
	Sand Lake Road Closures / Sidewalk																										
	<u>Upcoming Milestones</u>																										
	Finish Ramp M2/M3 Construction - Open to Final Configuration	3/6/2026																									
	<u>Sand Lake Rd &amp; Ramps</u>																										
	Sand Lake WB Contra flow (Bridge Demo)	James	Jamey	X	X	X	X			X	X	X	X				X	X	X	X	X						
	Sand Lake EB Contra flow (Bridge Demo)	James	Jamey	X	X	X	X			X	X	X	X				X	X	X	X	X						
	Turekylake Rd North & South directions for drainage	Lane	Jamey	X	X	X	X			X	X	X	X				X	X	X	X	X						
	<u>I-4 EB</u>																										
	I-4 Single Lane Closures EB	Lane	Jamey	X	X	X	X			X	X	X	X				X	X	X	X	X						
	<u>I-4 WB</u>																										
	I-4 Single Lane Closures WB	Lane	Jamey	X	X	X	X			X	X	X	X				X	X	X	X	X						





Phillips  
Crossing

Rosen Inn  
International







# Agenda — Current Project Status

- **Past Project Status — FDOT to review past 7 days**
  - Jack and bore (Area 3)
  - Pylon and planter wall work (Areas 2 and 3)
  - Signal and sign foundation work
  - Install lighting on westbound I-4 (Areas 3 and 4)
  - Old westbound I-4 lanes demolition
  - Excavate and grade ponds
  - MSE wall demolition (Areas 2 and 3)
  - Embankment work (Area 3)
  - Turkey Lake Road median widening
  - Place/finish lime rock (Area 3)
  - Drainage work (Areas 1, 2, and 3)
  - Utility relocation
  - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**






















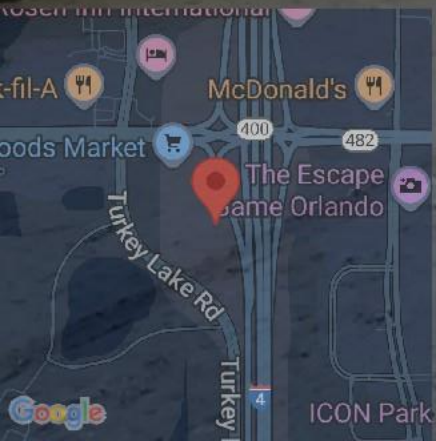

Nov 17, 2025 9:43:53 AM  
8015 Turkey Lake Road  
Orlando  
Orange County  
Florida









# Agenda — Future Project Status

- **Future Project Status — FDOT to review next 7 days**
  - MSE wall demolition (Areas 2 and 3)
  - Pylon and planter wall work (Areas 2 and 3)
  - Storm drainage work on Sand Lake Road (Area 7)
  - Pile set checks (Area 8)
  - Signal and sign foundation work
  - Old westbound I-4 lanes demolition
  - Excavate and grade ponds
  - Place/finish lime rock (Area 3)
  - Embankment work (Area 2)
  - Drainage work (Areas 1, 2, and 3)
  - Utility relocation
  - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**





# Agenda — Future Project Status

- **Future Project Status — FDOT to review next 14 – 21 days**
  - Install watermain casing (Area 1)
  - Pylon and planter wall work (Areas 2 and 3)
  - Signal and sign foundation work
  - Pile set checks (Area 8)
  - Embankment work (Area 2)
  - Drainage work (Areas 1, 2, and 3)
  - Place/finish lime rock (Area 3)
  - Excavate and grade ponds
  - Utility relocation
  - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**





# Agenda — Cleanliness Review

- **Cleanliness Review**
  - Committee's observations over past 7 days
- **Condition Review**
  - Committee's observations over past 7 days  
(fencing, wraps, barricades, temporary signage)





# Agenda — Old Business


- **Public Input or Comments**
- **Commitments Update**
  - Fencing and screening
  - Mowing and cleaning
  - Clean Team
  - Ponds





# Safety Diversions

- November 19 and 20
  - Westbound I-4 exit ramp to eastbound S.R. 528
  - 10 p.m. – 6 a.m.

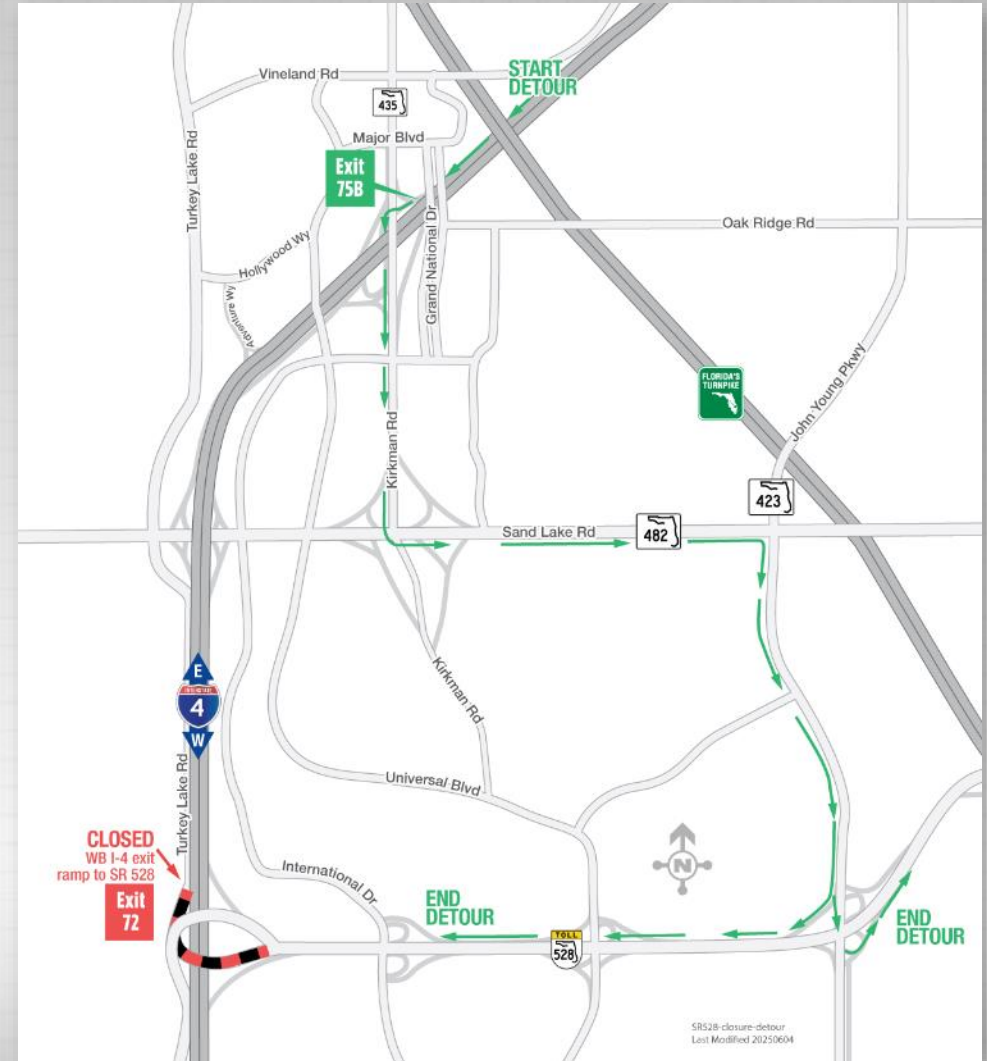





# Agenda — New Business

**Next meeting: 12/03/25**
