



I-4 and Sand Lake Road Interchange Design-Build

12/03/2025

I4Beyond.com



Status as of December 1, 2025

Days Used	Total Days	% Days Complete	Last Contract Day
974	1,734	56.2%	12/31/2027


Sand Lake 3470				Current Week							Week 1							Week 2						
Activity ID	Activity Description	Foreman / Sub	Supt	1-Dec	2-Dec	3-Dec	4-Dec	5-Dec	6-Dec	7-Dec	8-Dec	9-Dec	10-Dec	11-Dec	12-Dec	13-Dec	14-Dec	15-Dec	16-Dec	17-Dec	18-Dec	19-Dec	20-Dec	21-Dec
				MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN
	Roadway																							
MSE270	Demo/Exc. MSE wall RW3-1	Marcos C.	Tyler	X	X	X	X	X																
	Exc/Grade Pond 206/206B	Marcos C.	Tyler	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X		
	Grade for Median Barrier I4 EBXL (South)	Marcos C.	Tyler								X	X	X	X	X			X	X	X	X	X		
EW530	Place Embankment North/South XL's	Stephanie C	Tyler	X	X	X	X	X																
BW380	Grade for Median Barrier I4 EBXL (North)	Stephanie C	Tyler								X	X	X											
	Backfill B7 & B8 Backwalls	Stephanie C	Tyler											X	X	X								
FLAT220	Sand Lake Rd. Widening/Base/Flatwork 318 - 323	Stephanie C	Tyler															X	X	X	X	X		
BASE330	Fin Limerock Ramp M2 (RW6-2)	Jessie Wilson	Tyler	X	X	X																		
STAB330	Balance/Sweetener/Mix I4 XL's 1454-1477	Jessie W./Ian P.	Tyler	X	LBR	LBR	LBR	LBR																
STAB330	Box Subgrade I4 XL's 1454-1477	Jessie W./Ian P.	Tyler						X		X	X	X	X	X			X	X	X	X	X		
BASE380	Plc/Fin Limerock I4 XL's 1454-1477	Jessie W./Ian P.	Tyler											X	X	X		X	X	X	X	X		
	Night Mot \ Erosion Deficiency Items	Dennis Scott	Greg L	X	X	X	X	X																
	Temp Driveway - Checkers	Dennis Scott	Tyler								X	X	X	X	X									
	Clean Team Sandlake Sidewalks,Trash pickup and Mowing	Billy Wortes	Greg L										X	X	X									
	Sand lake off and on ramps to I-4 - Trash pickup and Mowing	Billy Wortes	Greg L			X	X	X										X	X					
	Turkey lake Sidewalks,Trash pickup and Mowing	Billy Wortes	Greg L								X	X								X	X	X		
	Kirkman ramp - Trash pickup and Mowing	Billy Wortes	Greg L	X	X													X	X					
FLAT120	Turkey Lake Assist Jvd	Larry Rapp	Greg L															X	X	X	X	X		
BASE140	Excavate place lime rock in lieu of base/asphalt for separator TL Rd	Larry Rapp	Greg L									X	X	X	X									
BASE140	Excavate place lime rock in lieu of and base for E-curb TL Rd	Larry Rapp	Greg L			X	X	X			X							X	X	X	X	X		
	Install FM Valves @ Whole Foods	Larry Rapp	Greg L	X	N																			
	Drainage / Utilities																							
DRG290	Install S-81 S-81A (42")	Jose Castro C.	Greg L															V	V	V	V	V		
DRG290	Install S-80 to S-81 (42")	Jose Castro C.	Greg L			X	X	X			X	X												
DRG290	Pave temp sidewalk for S-80	Jose Castro C.	Greg L										X	X										
	Install FM Valves @ Whole Foods	Jose Castro C.	Greg L	X	N																			
DRG220	Install CS-206 to CS-206A (36")	Isaias Barcenas	Greg L															V	V	V	V	V		
DRG220	Install S-2000 to S-2001 (36")	Isaias Barcenas	Greg L			X	X	X	X															
DRG430	Install WM casing SL @ Whole Foods	Isaias Barcenas	Greg L								X	X	X	X										
DRG430	Excavate and Prep CIP S-506	Isaias Barcenas	Greg L													X								
	Install FM Valves @ Whole Foods	Isaias Barcenas	Greg L	X	N																			
DRG430	Install S-549 to S-550 With conflict box(s)	Edward Benitez	Greg L			X																		
	Install FM Valves @ Whole Foods	Edward Benitez	Greg L	X	N						V	V	V	V	V			V	V	V	V	V		
	Structures																							
	<u>Pylon</u>																							
SUBS280	rub and patch pylons	Raffel Nunez/victor	Jose Perez	x	x	x	x	x			x	x	x	x	x									
	<u>Planter wall</u>																							
CIP120	Form planter wall 1-1	Jaime Castillo /Felepe	Jose Perez	x	x	P		x			x	x	x	x	x									
	rub and patch planter wall 1-1	Fransico	Jose Perez															x	x	x	x	x		
	<u>Bridge #3</u>																							
SUBS660	Form EB 1	Victor/Eusiabo	Jose Perez	X	x	x	x	x			x	x	x	P	x			x	x	x	P	x		
SUBS660	Form caps	Jaime/Eusiabo	James O'Neill	x	x	x	x	x			x	x	x	x	x			x	x	x	x	x		

Sand Lake 3470				Current Week							Week 1							Week 2						
Activity ID	Activity Description	Foreman / Sub	Supt	1-Dec	2-Dec	3-Dec	4-Dec	5-Dec	6-Dec	7-Dec	8-Dec	9-Dec	10-Dec	11-Dec	12-Dec	13-Dec	14-Dec	15-Dec	16-Dec	17-Dec	18-Dec	19-Dec	20-Dec	21-Dec
				MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN
	Subcontractor																							
FLAT160	Form/Pour E curb TL Rd	JVD	Roberto			X	X	X																
BW290	Median Barrier I4 WB (5245 - 5252)	Blount Sanford	Roberto								X	X	X	X	X			X	X	X	X	X		
BW290	Median Barrier I4 XL's (6225 - 6239)	Blount Sanford	Roberto								X	X	X	X	X			X	X	X	X	X		
TW130/150	Install TW 4-1 and 4-2	Maylor	Nate	X	X	X	X	X																
MSE270	Construct Wall 3-1 (Wirewall 4-1)	RWH	Nate					X			X	X	X	X	X			X	X	X	X	X		
PAVE350/210	Pave Ramps M, M2, & M3	Hubbard	Nate			N	N	N		N	N	N	N	N				N	N	N				
	Storm Drain Ramp M Grout Repair S-320A to S-320 48"	APS	Greg															N	N	N				
	B3 endbent 3 & pier 2 caps	Shelby	Harry	x	x	x	x	x			x	x	x	x	x			x	x	x	x	x		
	Maintain Whole Foods lift station/Clean FM line 2 Trucks	Badger	Harry		N																			
	<u>Lighting</u>																							
	Light Pole Install I4WB South of SLR	Conti	Rainer								x	x	x	x	x			x	x	x	x	x		
	Lighting Load Center B (Ramp K)	Conti	Rainer			X							X							X				
	Lighting Load Center C (Ramp J)	Conti	Rainer				X							X							X			
	<u>ITS</u>																							
	ITS Load Center B (Ramp K)	Conti	Rainer					X							X							X		
	<u>Signals</u>																							
	SLR Mast Arms Drill Shaft Pole 5	Conti/Reliable	Rainer																			X		
	<u>SPM</u>																							
	Drill Shaft OHC 5	Conti/Reliable	Rainer				X	X																
	Drill Shaft OHC 6	Conti/Reliable	Rainer								X	X												
	Drill Shaft OHC 18	Conti/Reliable	Rainer																	X	X			
	Drill Shaft OHS 2 LT	Conti/Reliable	Rainer										X	X										
	Drill Shaft OHS 3 LT	Conti/Reliable	Rainer															X	X					
	<u>Toll Plaza</u>																							
TOLL200	Slab Pour	Conti	Rainer					P																
	Sand Lake Road Closures / Sidewalk																							
	<u>Sand Lake Rd & Ramps</u>																							
	Sand Lake WB Contra flow (Bridge Demo)	James	Jamey	X	X	X	X				X	X	X	X				X	X	X	X			
	Sand Lake EB Contra flow (Bridge Demo)	James	Jamey	X	X	X	X				X	X	X	X				X	X	X	X			
	Turkey Lake Rd North & South direction for drainage	Lane	Jamey	X	X	X	X				X	X	X	X				X	X	X	X			
	<u>I-4 EB</u>																							
	I-4 Single Lane Closures EB	Lane	Jamey	X	X	X	X				X	X	X	X				X	X	X	X			
	<u>I-4 WB</u>																							
	I-4 Single Lane Closures WB	Lane	Jamey	X	X	X	X				X	X	X	X				X	X	X	X			



Phillips
Crossing

Rosen Inn
International





Agenda — Current Project Status

- **Past Project Status — FDOT to review past 7 days**
 - MSE wall demolition (Area 8)
 - Pylon and planter wall work (Areas 2 and 3)
 - Storm drainage work on Sand Lake Road (Area 7)
 - Pile set checks (Area 8)
 - Signal and sign foundation work
 - Old westbound I-4 lanes demolition
 - Excavate and grade ponds
 - Place/finish lime rock (Area 3)
 - Embankment work (Area 2)
 - Drainage work (Areas 1, 2, and 3)
 - Utility relocation
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**















Agenda — Future Project Status

- **Future Project Status — FDOT to review next 7 days**
 - Ramp paving (Area 3)
 - Bridge cap and end bent work (Area 8)
 - Place lime rock (Area 8)
 - Placing embankments (Area 8)
 - Force main work (Area 1)
 - Storm drainage work on Sand Lake Road (Area 7)
 - MSE wall demolition (Areas 2 and 3)
 - Pylon and planter wall work (Areas 2 and 3)
 - Signal and sign foundation work
 - Excavate and grade ponds
 - Drainage work (Areas 1, 2, and 3)
 - Utility relocation
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Future Project Status

- **Future Project Status — FDOT to review next 14 – 21 days**
 - Ramp paving (Area 3)
 - Place lime rock (Area 8)
 - Pylon and planter wall work (Areas 2 and 3)
 - Signal and sign foundation work
 - Force main work (Area 1)
 - Placing embankments (Areas 2 and 8)
 - Drainage work (Areas 1, 2, and 3)
 - Excavate and grade ponds
 - Utility relocation
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Cleanliness Review

- **Cleanliness Review**
 - Committee's observations over past 7 days
- **Condition Review**
 - Committee's observations over past 7 days
(fencing, wraps, barricades, temporary signage)



Agenda — Old Business

- **Public Input or Comments**
- **Commitments Update**
 - Fencing and screening
 - Mowing and cleaning
 - Clean Team
 - Ponds



Safety Diversions


- December 3 and 4
 - Westbound I-4 exit ramp to Sand Lake Road
 - 10 p.m. – 6 a.m.





Safety Diversions

- **December 1 – 4**
 - Westbound I-4 exit ramp to eastbound S.R. 528
 - 10 p.m. – 6 a.m.

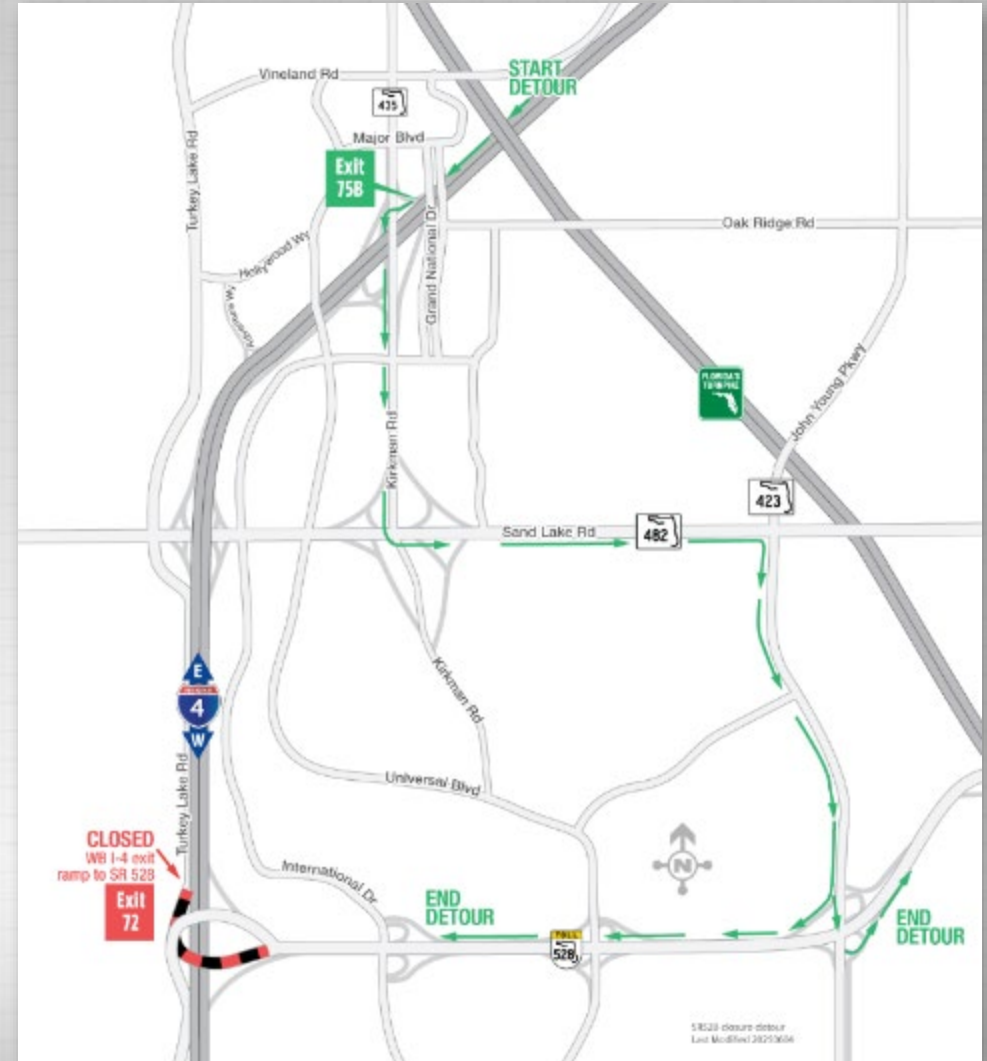



Agenda — New Business

Next meeting: 12/10/25

Future meetings 12/24 and 12/31?
