



I-4 and Sand Lake Road Interchange Design-Build

12/10/2025

I4Beyond.com



Status as of December 8, 2025

Days Used	Total Days	% Days Complete	Last Contract Day
981	1,740	56.4%	1/6/2028

FLOAT	Activity ID	Sand Lake 3470				Current Week								Week 1								Week 2							
		Activity Description	Foreman / Sub	Supt	8-Dec	9-Dec	10-Dec	11-Dec	12-Dec	13-Dec	14-Dec	15-Dec	16-Dec	17-Dec	18-Dec	19-Dec	20-Dec	21-Dec	22-Dec	23-Dec	24-Dec	25-Dec	26-Dec	27-Dec	28-Dec				
					MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN				
		Roadway																											
20	MSE270	Demo/Exc. MSE wall RW3-1	Marcos C.	Tyler	X																								
	EW360/370	Exc/Grade Pond 206/206B	Marcos C.	Tyler	X	X	X	X	X			X	X	X	X	X			X	X									
20	EW510/520	Grade for Median Barrier I4 EBXL (South)	Marcos C.	Tyler	X	X	X	X	X			X	X	X	X	X			X	X									
25	BW290	Grade for Median Barrier I4 EBXL (North)	Stephanie C	Tyler	X	X	X																						
		Backfill B7 & B8 Backwalls	Stephanie C	Tyler				X	X	X																			
169	FLAT220	Sand Lake Rd. Widening/Base/Flatwork 318 - 323	Stephanie C	Tyler								X	X	X	X	X													
20	STAB330	Box Subgrade I4 XL's 1454-1477	Jessie W./Ian P.	Tyler	X	X	X	X	X			X	X	X	X	X			X	X									
20	BASE380	Plc/Fin Limerock I4 XL's 1454-1477	Jessie W./Ian P.	Tyler				X	X	X		X	X	X	X	X			X	X									
		Night Mot \ Erosion Deficiency Items	Dennis Scott	Greg L	X	X	X	X	X			X	X	X	X	X			X	X									
		Temp Driveway - Checkers	Dennis Scott	Tyler	X	X	X	X	X																				
		Clean Team Sandlake Sidewalks, Trash pickup and Mowing	Billy Worles	Greg L			X	X	X																				
		Snad lake off and on ramps to I-4 - Trash pickup and Mowing	Billy Worles	Greg L								X	X						X	X									
		Turkey lake Sidewalks, Trash pickup and Mowing	Billy Worles	Greg L	X	X								X	X	X													
		Kirkman ramp - Trash pickup and Mowing	Billy Worles	Greg L								X	X																
323	FLAT120	Turkey Lake Assist Jvd	Larry Rapp	Greg L								X	X	X	X	X													
323	BASE140	Excavate place lime rock in lieu of base/asphalt for separator TL Rd	Larry Rapp	Greg L		X	X	X	X	X				X	X	X													
323	BASE140	Excavate place lime rock in lieu of and base for E-curb TL Rd	Larry Rapp	Greg L	X							X	X	X	X	X													
		Drainage / Utilities																											
636	DRG290	Install S-81 S-81A (42")	Jose Castro C.	Greg L								V	V	V	V	V			V	V			V						
636	DRG290	Install S-80 to S-81 (42")	Jose Castro C.	Greg L	X	X																							
636	DRG290	Pave temp sidewalk for S-80	Jose Castro C.	Greg L			X	X																					
384	DRG220	Install CS-206 to CS-206A (36")	Isalas Barcenas	Greg L								V	V	V	V	V			V	V			V						
60	DRG430	Install WM casing SL @ Whole Foods	Isalas Barcenas	Greg L	X	X	X	X																					
60	DRG430	Excavate and Prep CIP S-506	Isalas Barcenas	Greg L					X																				
		Install FM Valves @ Whole Foods	Edward Benitez	Greg L	V	V	V	V	V	V		V	V	V	V	V			V	V			V						
		Structures																											
		Pylon																											
	SUBS280	rub and patch pylons	Raffel Nunez/victor	Jose Perez	X	X	X	X	X																				
		Planter wall																											
494	CIP120	Form planter wall 1-1	Jaime Castillo /Felepe	Jose Perez	X	X	X	X	X																				
494	CIP130	rub and patch planter wall 1-1	Francisco	Jose Perez								X	X	X	X	X													
		Bridge #3																											
20	SUBS660	Form EB 1	Victor/Eusebio	Jose Perez	X	X	X	X	X			X	X	X	X	X			X	X									
20	SUBS660	Form caps	Jaime/Eusebio	James O'Neill	X	X	X	X	X			X	X	X	X	X			X	X									
		Subcontractor																											
323	FLAT120	Form/Pour separator TL Rd	JVD	Roberto	X	X	X																						
545	FLAT160	Form/Pour E curb TL Rd	JVD	Roberto			X	X	X																				
25	BW290	Median Barrier I4 WB (5245 - 5252)	Blount Sanford	Roberto	X	X	X	X	X			X	X	X	X	X			X	X									
25	BW290	Median Barrier I4 XL's (6225 - 6239)	Blount Sanford	Roberto	X	X	X	X	X			X	X	X	X	X			X	X									
20/20	TW130/150	Install TW 4-1	Maylor	Nate	X	X																							
20	MSE270	Construct Wall 3-1 (Wirewall 4-1)	RWH	Nate		X	X	X	X			X	X	X	X	X													
		Storm Drain Ramp M Grout Repair S-320A to S-320 48"	APS	Greg					X																				
46	SUBS690	B3 endbent 3 & pier 2 caps	Shelby	Harry	X	X	X	X	X			X	X	X	X	X													
		Lighting																											
	LGHT110	Light Pole Install I4WB South of SLR	Conti	Ralner	X	X	X	X	X			X	X	X	X	X													
	LGHT110	Lighting Load Center B (Ramp K)	Conti	Ralner			X							X															
	LGHT110	Lighting Load Center C (Ramp J)	Conti	Ralner				X							X														

N/P - Night Poor NC - Night Time Confirmed T-N - Tentative D-File Delivery
 X - Day Schedule TS-Traffic Shift N - Night

	Sand Lake 3470				Current Week								Week 1								Week 2							
FLOAT	Activity ID	Activity Description	Foreman / Sub	Supt	8-Dec	9-Dec	10-Dec	11-Dec	12-Dec	13-Dec	14-Dec	15-Dec	16-Dec	17-Dec	18-Dec	19-Dec	20-Dec	21-Dec	22-Dec	23-Dec	24-Dec	25-Dec	26-Dec	27-Dec	28-Dec			
					MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN			
		<u>ITS</u>																										
541	ITS100	ITS Load Center B (Ramp K)	Contl	Rainer					X							X												
		<u>Signals</u>																										
323	SGNL220	TLR Mast Arms Drill Shaft Pole 3	Contl/Reliable	Rainer											X	X												
		<u>SPM</u>																										
		Drill Shaft OHC 5	Contl/Reliable	Rainer			X	X																				
		Drill Shaft OHC 6	Contl/Reliable	Rainer					X																			
		Drill Shaft OHC 16	Contl/Reliable	Rainer								X	X															
		Sand Lake Road Closures / Sidewalk																										
		<u>Sand Lake Rd & Ramps</u>																										
		Sand Lake WB Contra flow (Structure Pours)	James	Jamey	X	X	X	X			X	X	X	X	X			X	X	X								
		Sand Lake EB Contra flow (Structure Pours)	James	Jamey	X	X	X	X			X	X	X	X	X			X	X	X								
		Ramp M Full Closure	Lane	Jamey	X	X	X	X																				
		<u>I-4 EB</u>																										
		I-4 Single Lane Closures EB	Lane	Jamey	X	X	X	X			X	X	X	X	X			X	X	X								
		<u>I-4 WB</u>																										
		I-4 Single Lane Closures WB	Lane	Jamey	X	X	X	X			X	X	X	X	X			X	X	X								

N/P - Night Pour	NC - Night Time Confirmed	T-N - Tentative	D-File Delivery
X - Day Schedule	TS-Traffic Shift	N - Night	



Phillips Crossing

Rosen Inn International





Agenda — Current Project Status

- **Past Project Status — FDOT to review past 7 days**
 - Ramp paving (Area 3)
 - Bridge cap and end bent work (Area 8)
 - Place lime rock (Area 8)
 - Placing embankments (Area 8)
 - Force main work (Area 1)
 - Storm drainage work on Sand Lake Road (Area 7)
 - MSE wall demolition (Areas 2 and 3)
 - Pylon and planter wall work (Areas 2 and 3)
 - Signal and sign foundation work
 - Excavate and grade ponds
 - Drainage work (Areas 1, 2, and 3)
 - Utility relocation
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**





















Agenda — Future Project Status

- **Future Project Status — FDOT to review next 7 days**
 - Median barrier wall grading (Area 8)
 - Bridge cap work (Area 8)
 - Place lime rock (Area 8)
 - Force main work (Area 1)
 - Storm drainage work on Sand Lake Road (Area 7)
 - MSE wall demolition (Areas 2 and 3)
 - Pylon and planter wall work (Areas 2 and 3)
 - Signal and sign foundation work
 - Excavate and grade ponds
 - Drainage work (Areas 1, 2, and 3)
 - Utility relocation
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Future Project Status

- **Future Project Status — FDOT to review next 14 – 21 days**
 - Sand Lake Road widening work (Area 7)
 - Median barrier wall grading (Area 8)
 - Bridge cap work (Area 8)
 - Place lime rock (Area 8)
 - Force main work (Area 1)
 - Storm drainage work on Sand Lake Road (Area 7)
 - Planter wall work (Areas 2 and 3)
 - Signal and sign foundation work
 - Excavate and grade ponds
 - Drainage work (Areas 1, 2, and 3)
 - Utility relocation
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Cleanliness Review

- **Cleanliness Review**
 - Committee's observations over past 7 days
- **Condition Review**
 - Committee's observations over past 7 days
(fencing, wraps, barricades, temporary signage)






Agenda — Old Business

- **Public Input or Comments**
- **Commitments Update**
 - Fencing and screening
 - Mowing and cleaning
 - Clean Team
 - Ponds



Safety Diversions

- **December 10 and 11**
 - Westbound I-4 exit ramp to eastbound S.R. 528
 - 10 p.m. – 6 a.m.

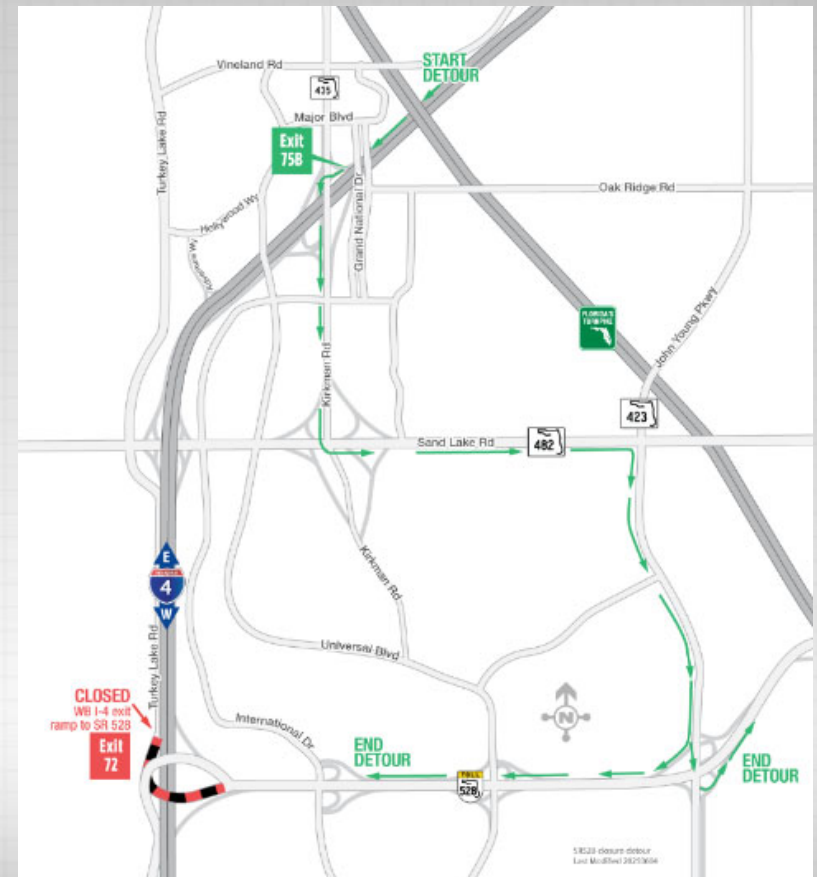



Agenda — New Business

Next meeting: **12/17/25**
