



I-4 and Sand Lake Road Interchange Design-Build

12/17/2025

I4Beyond.com



Status as of December 15, 2025

Days Used	Total Days	% Days Complete	Last Contract Day
988	1,740	56.8%	1/6/2028

Activity ID	Activity Description	Foreman / Sub	Supt	Current Week							Week 1							Week 2						
				15-Dec	16-Dec	17-Dec	18-Dec	19-Dec	20-Dec	21-Dec	22-Dec	23-Dec	24-Dec	25-Dec	26-Dec	27-Dec	28-Dec	29-Dec	30-Dec	31-Dec	1-Jan	2-Jan	3-Jan	4-Jan
	Roadway																							
EW360/370	Exc/Grade Pond 206/206B	Marcos C.	Tyler	X	X	X	X	X			X	X												
BW300	Grade for Median Barrier I4 EBXL (South)	Marcos C.	Tyler								X	X												
FLAT200/110/180	Grade Flatwork Ramp M/M2/SLR	Marcos C.	Tyler	X	X	X	X	X																
	Assist RWH Construct MSE Wall 3-1	Marcos C.	Tyler												X			X	X					
	Backfill B7 & B8 Backwalls	Stephanie C	Tyler	V	V	V	V	V			V	V										X		
STAB330	Box Subgrade I4 XL's 1454-1477	Jessie W./Ian P.	Tyler	X	X	X	X	X			X	X												
BASE380	Pic/Fin Limerock I4 XL's 1454-1477	Jessie W./Ian P.	Tyler	X	X	X	X	X			X	X												
	Sand lake off and on ramps to I-4 - Trash pickup and Mowing	Billy Worles	Greg L	X	X						X	X												
	Turkey Lake Sidewalks, Trash pickup and Mowing	Billy Worles	Greg L			X	X	X																
	Kirkman ramp - Trash pickup and Mowing	Billy Worles	Greg L	X	X																			
FLAT120	Turkey Lake Assist Jvd	Larry Rapp	Greg L	X	X	X	X	X																
BASE140	Excavate place lime rock in lieu of and base for E-curb TL Rd	Larry Rapp	Greg L	X	X	X	X	X																
	Excavate, place, grade limerock Turkey Lake	Larry Rapp	Greg L								X	X												
	Drainage / Utilities																							
DRG290	Install S-81 S-81A (42")	Jose Castro C.	Greg L	V	V	V	V	V			V	V			V			V	V			V		
DRG220	Install CS-206 to CS-206A (36")	Isalas Barcenas	Greg L	V	V	V	V	V			V	V			V			V	V			V		
	Install FM Valves @ Whole Foods	Edward Benitez	Greg L	V	V	V	V	V			V	V			V			V	V			V		
	Structures																							
	Planter wall																							
CIP130	rub and patch planter wall 1-1	Jose Perez		x	x	x	x	x																
	Bridge #3																							
SUBS700	strip EB 3 back wall	Jose Perez		x	x	x	x	x			x	x												
SUBS690	Form pier caps	James O'Neill		N/P	x	x	x	x	x		x	x												
	Subcontractor																							
FLAT160	Form/Pour E curb TL Rd	JVD	Roberto	X	X	X	X	X			X	X												
MSE270	Construct Wall 3-1 (Wirewall 4-1)	RWH	Nate	X	X	X	X	X	X		X	X			X			X	X			X	X	
SUBS690	B3 endbent 3 & pier 2 caps	shelby	Harry	x	x	x	x	x																
	Signals																							
SGNL220	TLR Mast Arms Drill Shaft Pole 3	Conti/Reliable	Rainer				T-N	T-N																
	SPM																							
	Drill Shaft OHC 6	Conti/Reliable	Rainer	X																				
	Drill Shaft OHC 18	Conti/Reliable	Rainer			T-N																		
	Utilities	UTILITY OWNER	STA																					
	Bore in front of 7/11 for Cell Pole Relocation	Duke	SLR	X	X	X																		
	Sand Lake Road Closures / Sidewalk																							
	Sand Lake Rd & Ramps																							
	Sand Lake WB Contra flow (Structure Pours)	James	Jamey	X	X	X	X			X	X	X												
	Sand Lake EB Contra flow (Structure Pours)	James	Jamey	X	X	X	X			X	X	X												
	I-4 EB																							
	I-4 Single Lane Closures EB	Lane	Jamey	X	X	X	X			X	X	X												
	I-4 WB																							
	I-4 Single Lane Closures WB	Lane	Jamey	X	X	X	X			X	X	X												



Phillips
Crossing

Rosen Inn
International





Agenda — Current Project Status

- **Past Project Status — FDOT to review past 7 days**
 - Median barrier wall grading (Area 8)
 - Bridge cap work (Area 8)
 - Place lime rock (Area 8)
 - Force main work (Area 1)
 - Storm drainage work on Sand Lake Road (Area 7)
 - MSE wall demolition (Areas 2 and 3)
 - Pylon and planter wall work (Areas 2 and 3)
 - Signal and sign foundation work
 - Excavate and grade ponds
 - Drainage work (Areas 1, 2, and 3)
 - Utility relocation
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**











Agenda — Future Project Status

- **Future Project Status — FDOT to review next 7 days**
 - MSE wall construction (Area 8)
 - Ramp grading work (Area 3)
 - Subgrade work (Area 8)
 - Bridge cap and end bent work (Area 8)
 - Place lime rock (Area 8)
 - Force main work (Area 1)
 - Storm drainage work on Sand Lake Road (Area 7)
 - Planter wall work (Areas 2 and 3)
 - Signal and sign foundation work
 - Excavate and grade ponds
 - Drainage work (Areas 1, 2, and 3)
 - Utility relocation
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Future Project Status

- **Future Project Status — FDOT to review next 14 – 21 days**
 - MSE wall construction (Area 8)
 - Ramp grading work (Area 3)
 - Subgrade and lime rock base work (Area 8)
 - Median barrier wall grading (Area 8)
 - Storm drainage work on Sand Lake Road (Area 7)
 - Excavate and grade ponds
 - Drainage work (Areas 1, 2, and 3)
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Cleanliness Review

- **Cleanliness Review**
 - Committee's observations over past 7 days
- **Condition Review**
 - Committee's observations over past 7 days
(fencing, wraps, barricades, temporary signage)




Agenda — Old Business

- **Public Input or Comments**
- **Commitments Update**
 - Fencing and screening
 - Mowing and cleaning
 - Clean Team
 - Ponds



Safety Diversions

- **December 21**
 - Westbound I-4 exit ramp to eastbound S.R. 528
 - 10 p.m. – 6 a.m.

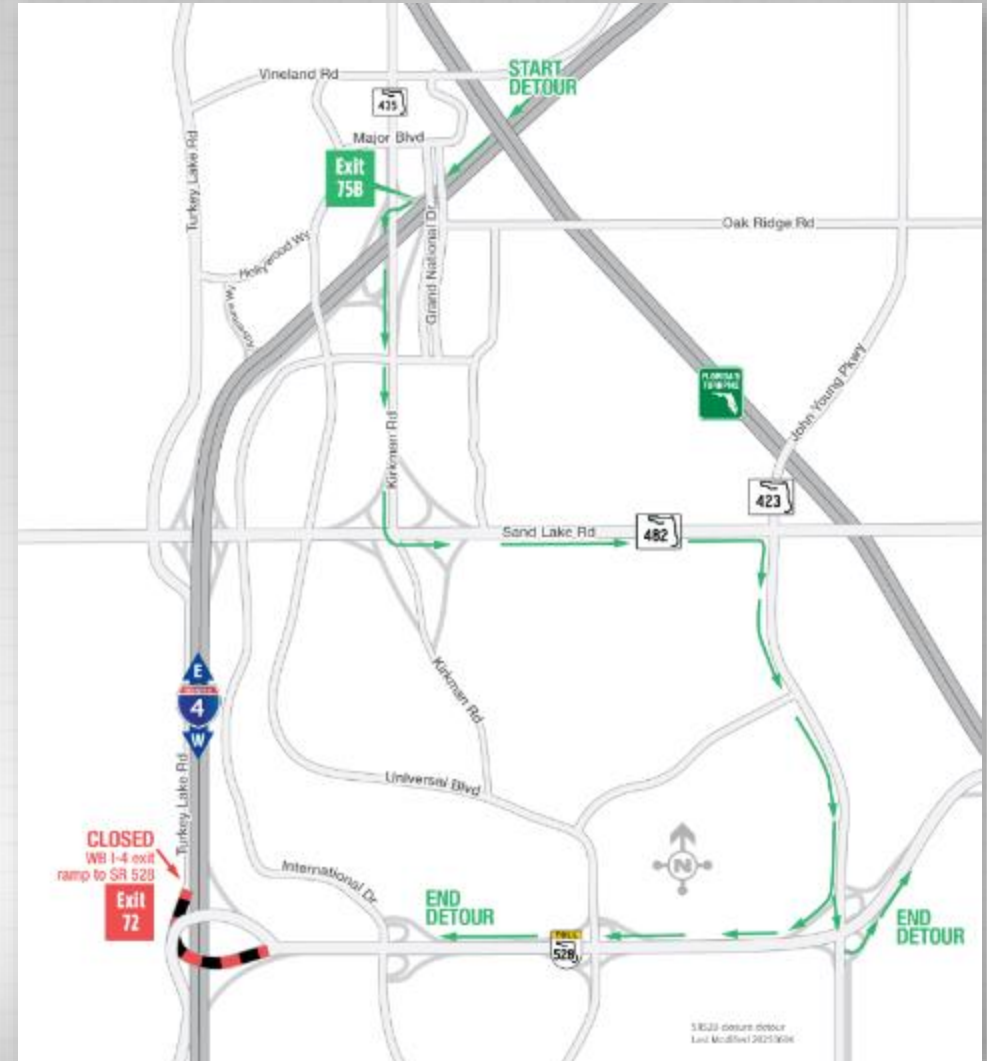



Agenda — New Business

Next meeting: 01/07/26
