



# I-4 and Sand Lake Road Interchange Design-Build

02/11/2026

[I4Beyond.com](http://I4Beyond.com)



# Status as of February 9, 2026

Days Used	Total Days	% Days Complete	Last Contract Day
1,044	1,751	59.6%	1/17/2028

Sand Lake 3470				Current Week							Week 1							Week 2						
Activity ID	Activity Description	Foreman / Sub	Supt	9-Feb	10-Feb	11-Feb	12-Feb	13-Feb	14-Feb	15-Feb	16-Feb	17-Feb	18-Feb	19-Feb	20-Feb	21-Feb	22-Feb	23-Feb	24-Feb	25-Feb	26-Feb	27-Feb	28-Feb	1-Mar
				MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN
	Roadway																							
FLAT260	Sand Lake Rd. Widening/Base/Flatwork (Sta.318 - 323 Checkers)	Marcos C.	Tyler	X	X	X	X	X	X															
	Grade for Sod behind sidewalk/curb (Sta.318 - 323 Checkers)	Marcos C.	Tyler			X	X	X	X															
PAVE280/290	Sand Lake Rd. South Side Sidewalk Repairs	Marcos C.	Tyler								X	X	X	X	X	X								
	Swap Peds to South side Sand Lake																N							
FLAT200/110/180	Ramp M/M2/SLR Widening/Base/Flatwork (Sta.105-110)	Marcos C.	Tyler															X	X	X	X	X	X	
BW290	Grade/backfill Median Barrier I4 EBXL	Stephanie C	Tyler	X	X	X	X	X	X		X	X	X	X	X	X		X	X	X	X	X		
	FG behind Med. Barrier for temp sod (South)	Stephanie C	Tyler	X	X	X	X	X																
BASE380	Ptc/Fin Limerock I4 XL's 1454-1477	Jessie W./Ian P.	Tyler	X	X	X	X	X	X															
BASE370	Ptc/Fin Limerock I4 XL's 1487-1500	Jessie W./Ian P.	Tyler								X	X	X	X	X	X		X	X	X				
	Temp Base (XL tie-ins) 1497+00 - 1505+50	Jessie W./Ian P.	Tyler																		X	X		
	Clean Team Sand Lake Sidewalks, Trash pickup and Mowing	Billy Worles	Greg L															x	x	x	x	x		
	Sand Lake off and on ramps to I-4 - Trash pickup and Mowing	Billy Worles	Greg L	x	x	x	x	x			x	x	x	x	x									
	Turkey Lake Sidewalks, Trash pickup and Mowing	Billy Worles	Greg L								x	x	x											
	Kirkman ramp - Trash pickup and Mowing	Billy Worles	Greg L											x	x	X								
FLAT120	Turkey Lake Assist OPC	Larry Rapp	Greg L	N	N	N	N																	
BASE140	Excavate place lime rock in lieu of and base for E-curb TL Rd	Larry Rapp	Greg L			N	N			N	N													
BASE140	Excavate,place,grade limerock Turkey Lake	Larry Rapp	Greg L								N	N	N	N										
	Demo Traffic Sep. SLR Median (Sta.119 - 122 McDonald's)	Larry Rapp	Greg L																					N
	Assist FM Install Ramp M/SLR	Larry Rapp	Greg L							N	N	N	N	N			N	N	N	N	N			
	Drainage / Utilities																							
DRG340	Install S-279A to S-281A (18")	Jose Castro C.	Greg L	X																				
DRG340	Install S-283A to S-281A (18")	Jose Castro C.	Greg L		X	X	X	X	X															
DRG340	Install S-284	Jose Castro C.	Greg L		X																			
	Link Seal/Split Casing Install S-269A	Jose Castro C.	Greg L								X	X	X											
	Pond 201A Underdrain	Jose Castro C.	Greg L											X	X	X		X	X	X	X	X	X	
DRG430	Install S-506 Dog house box	Isalas Barcenas	Greg L															X	X	X	X	X		
DRG430	Install S-506A top @ Whole food entrance	Isalas Barcenas	Greg L																			X	X	
DRG430	Excavate and verify utilities for S-506	Isalas Barcenas	Greg L												X									
	Install trench drain checkers and Circle K	Isalas Barcenas	Greg L	X	X	X																		
	Dewater/Video Drainage @ Pond 205D	Isalas Barcenas	Greg L				X	X	X		X	X	X	X										
U-OCU1520	Install FM Sand Lake ramp M	Edward Benitez	Greg L	N	N	N	N			N	N	N	N	N										
U-OCU1520	Install FM across sidewalk on South side SL	Edward Benitez	Greg L														N	N	N	N	N			
	Structures																							
	Bridge #3																							
	C.I.P coping plain under bridge	Victor Medina	Jose Perez			x	x	x			x													
SIP170	S.I.P.	Shelby /Eusebio	Jose Perez	X	X	X	X	X																
	place concrete on bridge deck span 2	Jalme/Felepe	James O'Neill											P										
	Install railing for Bidwell	Jalme/Felepe	James O'Neill	x	x	x																		
	Form bulk heads	Eusebio	James O'Neill				x	x																
REINF240	Rebar(shelby)	Shelby	Jose Perez	X	X	X	X				X	X	X	X	X			X	X	X	X	X		
	Form approach slab edge/Bidwell runoff	Eusebio Perez	Jose Perez				x	x	x															
	Set Bidwell	Jalme Castillo	Jose Perez				x	x	x															
DECK170	Set up dry run	Jaime Castillo	James O'Neill								x	x	x	x										

N/P - Night Pour	
X - Day Schedule	T-N - Tentative
NC - Night Time Confirmed	N - Night
TS-Traffic Shift	D-Pile Delivery



Sand Lake 3470				Current Week							Week 1							Week 2						
Activity ID	Activity Description	Foreman / Sub	Supt	9-Feb	10-Feb	11-Feb	12-Feb	13-Feb	14-Feb	15-Feb	16-Feb	17-Feb	18-Feb	19-Feb	20-Feb	21-Feb	22-Feb	23-Feb	24-Feb	25-Feb	26-Feb	27-Feb	28-Feb	1-Mar
				MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN
	Subcontractor																							
FLAT160	Form/Pour E curb TL Rd	JVD	Roberto	X	X	X	X	X			X	X	X	X	X									
BW290	Median Barrier I4 WB (5245 - 5252)	Blount Sanford	Roberto	X	X	X	X	X			X	X	X	X	X									
BW290	Median Barrier I4 XL's (6225 - 6239)	Blount Sanford	Roberto	X	X	X	X	X			X	X	X	X	X									
EW280	Mill and Fill Turkey Lake Rd	Hubbard	Nate	N	N	N	N					N	N	N	N									
	Checkers along Sand Lake	Hubbard	Nate					N																
	EB Express Lanes	Hubbard	Nate														N	N	N	N	N			N
	Shift Turkey Lake Phase 1B Step 2 to Phase 1B Step 3	McShea	Nate				N																	
DRG1240	Install 30" J&B S-55 - S4040F (Tube Area 3)	CFU	Greg								X	X	X	X	X									
DRG1240	Install 30" J&B S-56 - S422A (Tube Area 3)	CFU	Greg															X	X	X	X	X		
SIP170	B3 SIP	Shelby	Harry	X	X	X	X	X																
REINF240	B3 Rebar	Shelby	Harry	X	X	X	X	X																
	Lighting																							
	Service Conduit Lighting Load Center C (Ramp J)	Conti/Vasi	Rainer								X	X	X	X	X									
	Signals																							
SGL130	TLR/SLS Signal Cabinet & Conduit	Conti/Duke	Rainer								X	X	X	X	X									
SGN110	SLR Mast Arms Drill Shaft Pole 6	Conti/Reliable	Rainer				X																	
SGN110	SLR Mast Arms Drill Shaft Pole 7	Conti/Reliable	Rainer					X																
	SPM																							
SIGN100	Drill Shaft OHC 16	Conti/Reliable	Rainer		X	X																		
	Toll Plaza																							
TOLL240	Gantries Anchor Bolts & Loop Boxes	Conti/Vasi	Rainer			X	X	X			X	X	X	X	X									
	Sand Lake Road Closures / Sidewalk																							
	Sand Lake Rd & Ramps																							
	Sand Lake WB Contra flow (Bridge Work) & (Forcemain)	James	Dennis	N	N	N	N	N		N	N	N	N	N			N	N	N	N	N			
	Sand Lake EB Contra flow (Bridge Work) & (Forcemain)	James	Dennis	N	N	N	N	N		N	N	N	N	N			N	N	N	N	N			
	Sand Lake Rd WB Double Lane (Forcemain)	Lane	Dennis	N	N	N	N	N																
	Sand Lake Rd EB Single Lane Outside	Lane	Dennis				N	N																
	Ramp M Full Closure (Forcemain)	Lane	Dennis	N	N	N	N	N																
	Single Outside Right Lane Closure Ramp K	Lane	Dennis				N	N																
	Turkey Lake NB Contra-Flow for Paving (Segment 3)	Lane	Dennis									N	N	N	N									
	Turkey Lake SB Detour for Paving	Lane	Dennis	N	N	N	N	N																
	I-4 EB																							
	I-4 Single Lane Closures EB	Lane	Dennis	N	N	N	N			N	N	N	N	N			N	N	N	N	N			
	I-4 WB																							
	I-4 Single Lane Closures WB	Lane	Dennis	N	N	N	N			N	N	N	N	N			N	N	N	N	N			


N/P - Night Pour	
X - Day Schedule	T-N - Tentative
NC - Night Time Confirmed	N - Night
TS-Traffic Shift	D-Pile Delivery





Phillips  
Crossing

Rosen Inn  
International

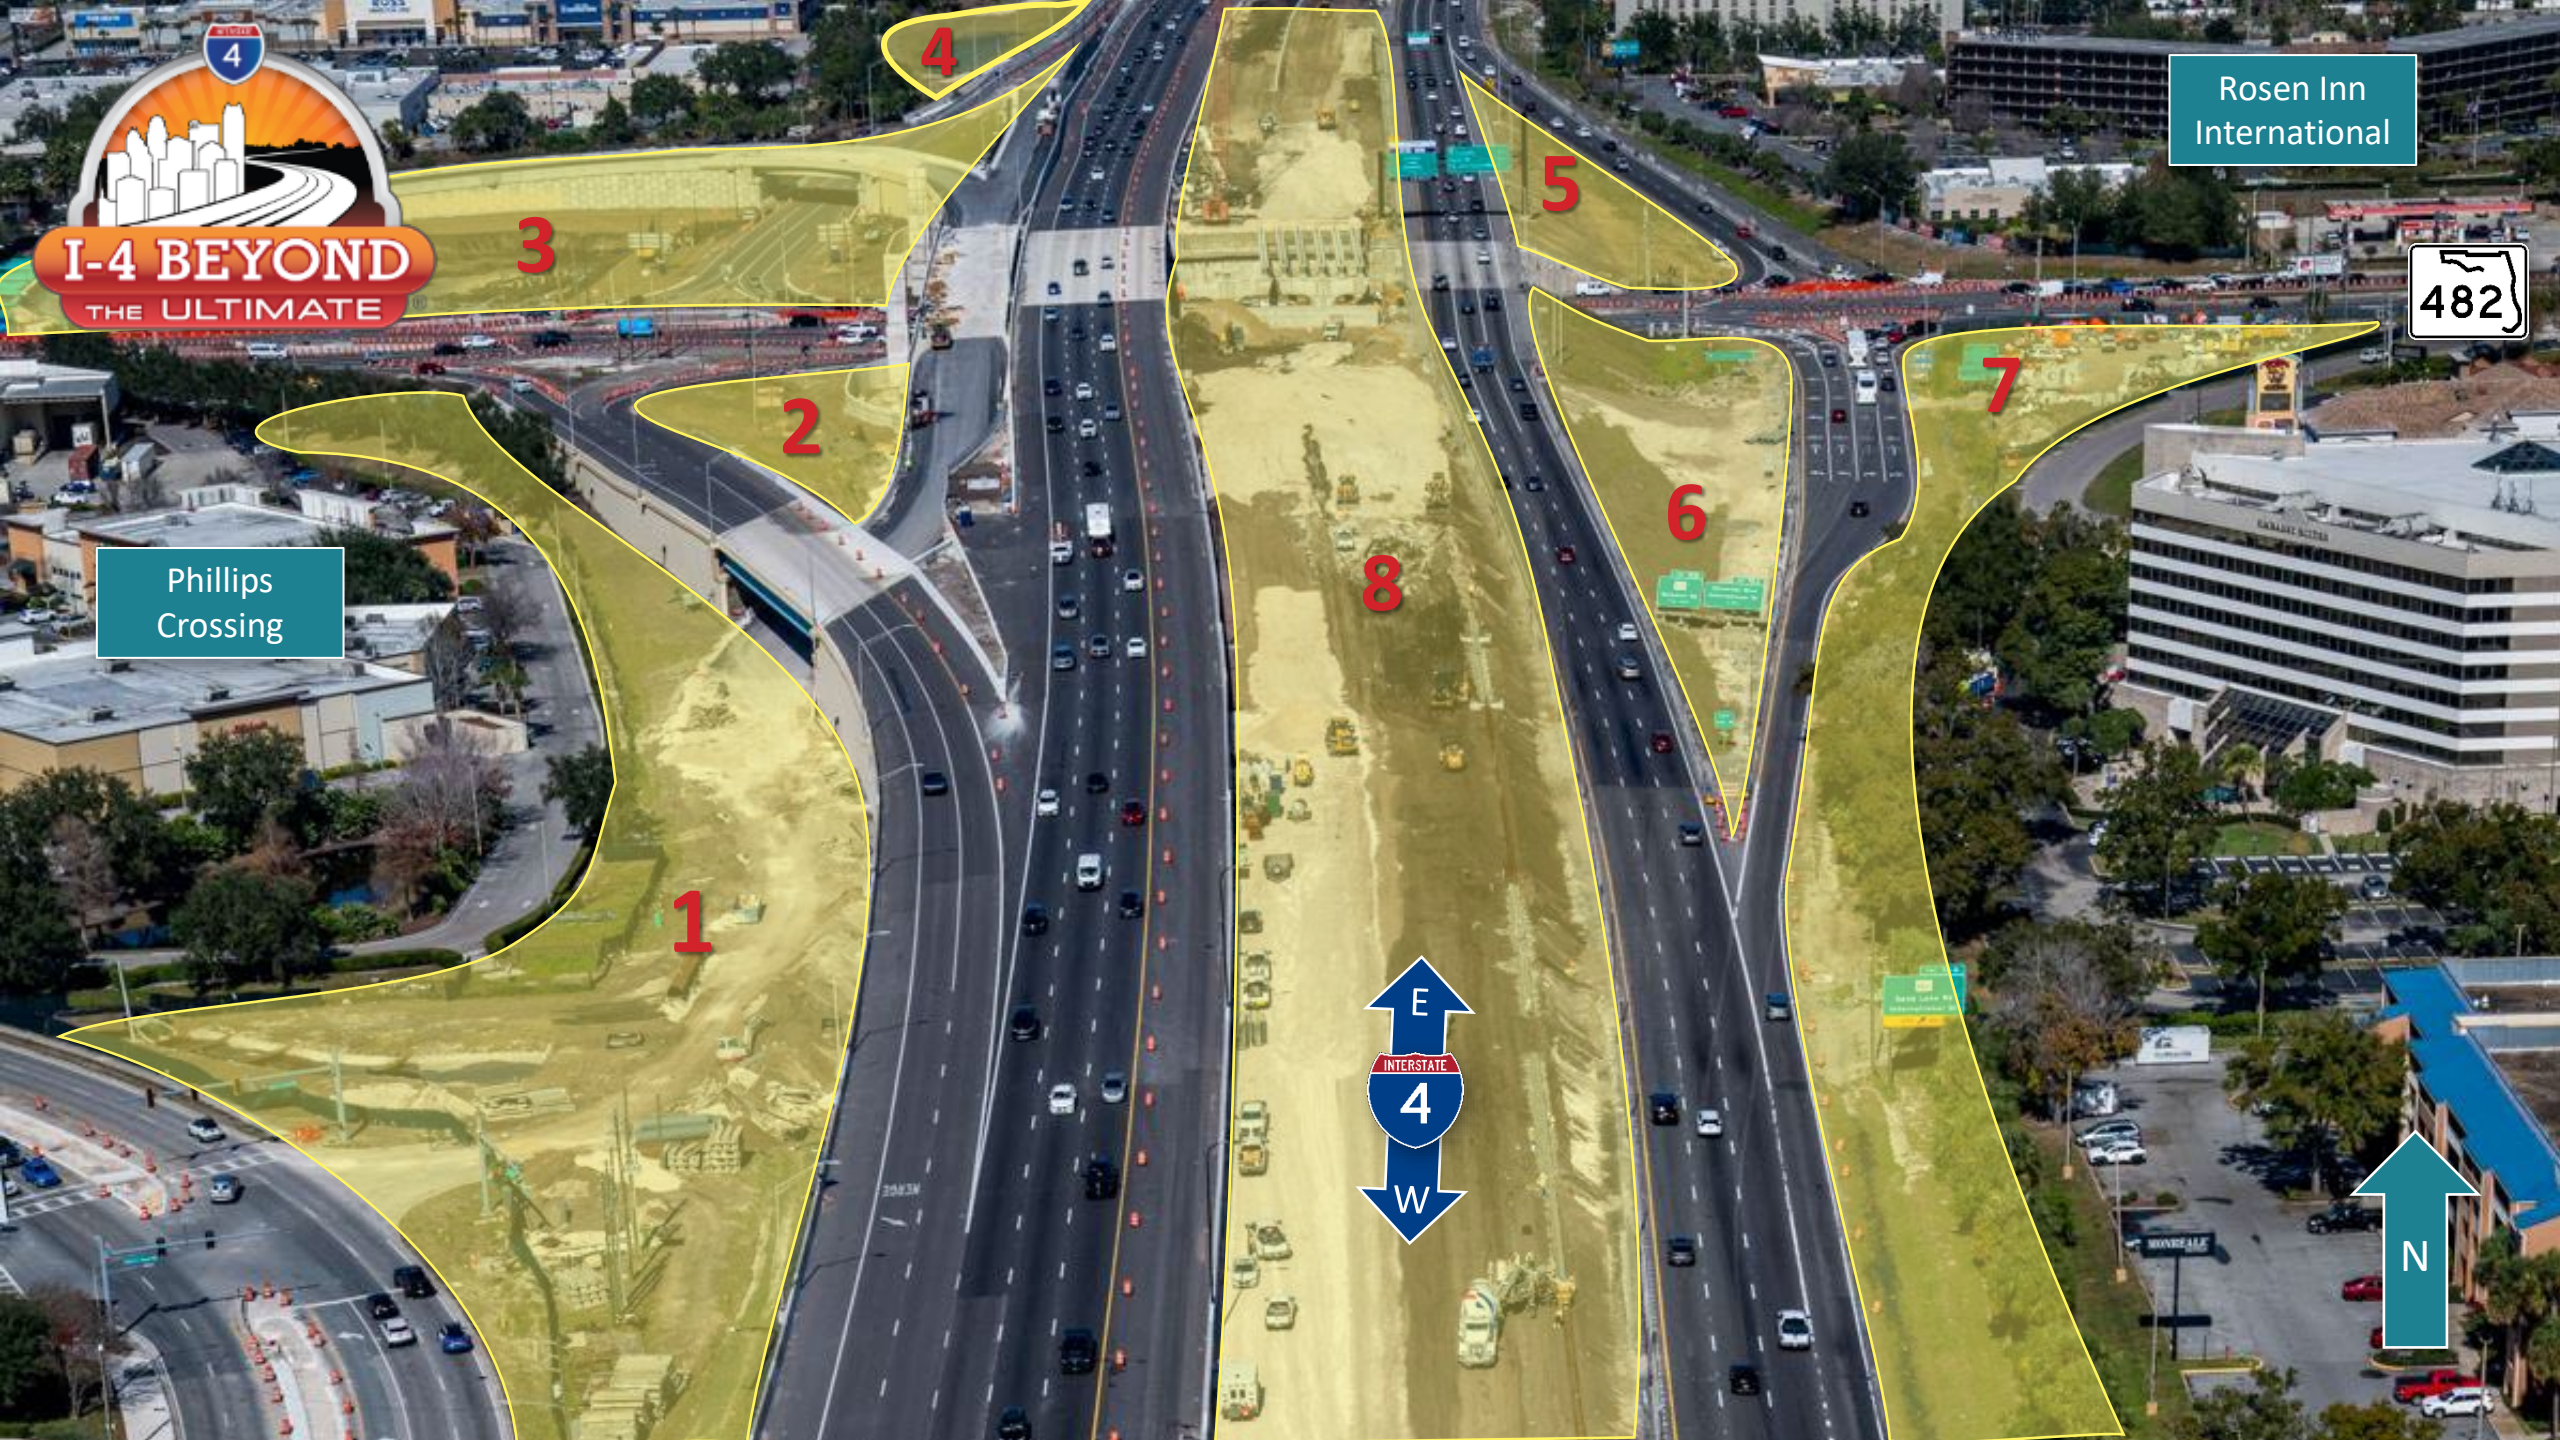





# Agenda — Current Project Status

- **Past Project Status — FDOT to review past 7 days**
  - Bridge beam setting over Sand Lake Road (Area 8)
  - Sand Lake Road widening and grading (Area 7)
  - Turkey Lake Road paving
  - Force main installation (Areas 3 and 5)
  - Place and compact lime rock (Area 8)
  - MSE wall construction (Area 8)
  - Median barrier wall grading (Area 8)
  - Excavate and grade ponds
  - Utility relocation
  - Drainage installation (Areas 1, 2, and 3)
  - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**









Feb 7, 2026 at 7:49:14 AM  
8250 Jamaican Ct  
Orlando FL 32819  
United States





# Agenda — Future Project Status

- **Future Project Status — FDOT to review next 7 days**
  - Bridge structure installation over Sand Lake Road (Area 8)
  - Sand Lake Road widening and grading (Area 7)
  - Turkey Lake Road paving
  - Force main installation (Area 3)
  - Sign structure installation (Area 3)
  - Place and compact lime rock (Area 8)
  - Median barrier wall grading (Area 8)
  - Excavate and grade ponds
  - Drainage installation (Areas 1, 2, and 3)
  - Utility relocation
  - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**





# Agenda — Future Project Status

- **Future Project Status — FDOT to review next 14 – 21 days**
  - Sand Lake Road bridge structure installation (Area 8)
  - Turkey Lake Road paving
  - Sidewalk side swap
  - Force main installation (Area 3)
  - Place and compact lime rock (Area 8)
  - Median barrier wall grading (Area 8)
  - Excavate and grade ponds
  - Utility relocation
  - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



# Agenda — Cleanliness Review

- **Cleanliness Review**
  - Committee's observations over past 7 days
- **Condition Review**
  - Committee's observations over past 7 days  
(fencing, wraps, barricades, temporary signage)





# Agenda — Old Business


- **Public Input or Comments**
- **Commitments Update**
  - Fencing and screening
  - Mowing and cleaning
  - Clean Team
  - Ponds
  - Express lanes signage/access
  - Hardscaping and aesthetics



# Safety Diversions

- **February 9 – 12 (nightly)**
  - Southbound Turkey Lake Road paving
  - Traffic will be diverted onto westbound I-4 to Daryl Carter Parkway
  - 10 p.m. – 6 a.m.
  - Weather permitting

<https://fdot.tips/TurkeyLakeRoad>

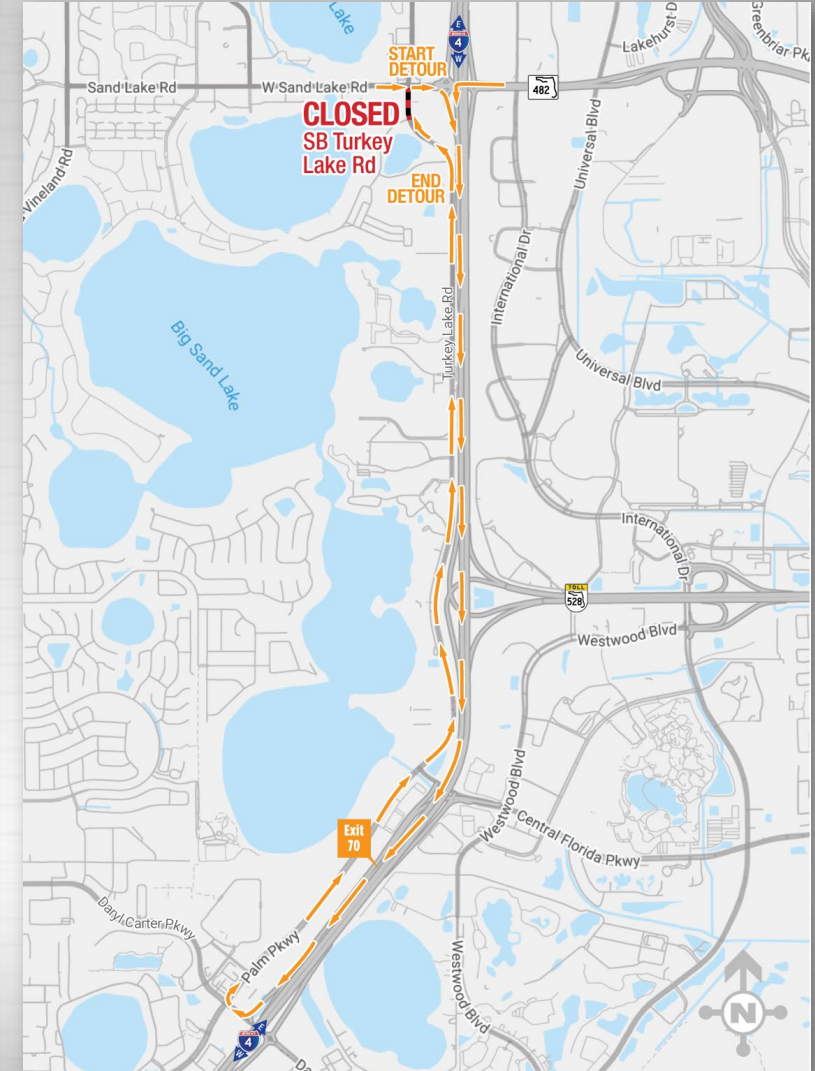






# Safety Diversions

- February 9 – 11 (nightly)
  - Ramp from westbound I-4 to Sand Lake Road for force main installation
    - 10 p.m. – 6 a.m.
  - Eastbound and westbound Sand Lake Road for bridge work
    - Traffic will be shifted and reduced to one lane in each direction
    - 11:00 p.m. – 6:30 a.m.

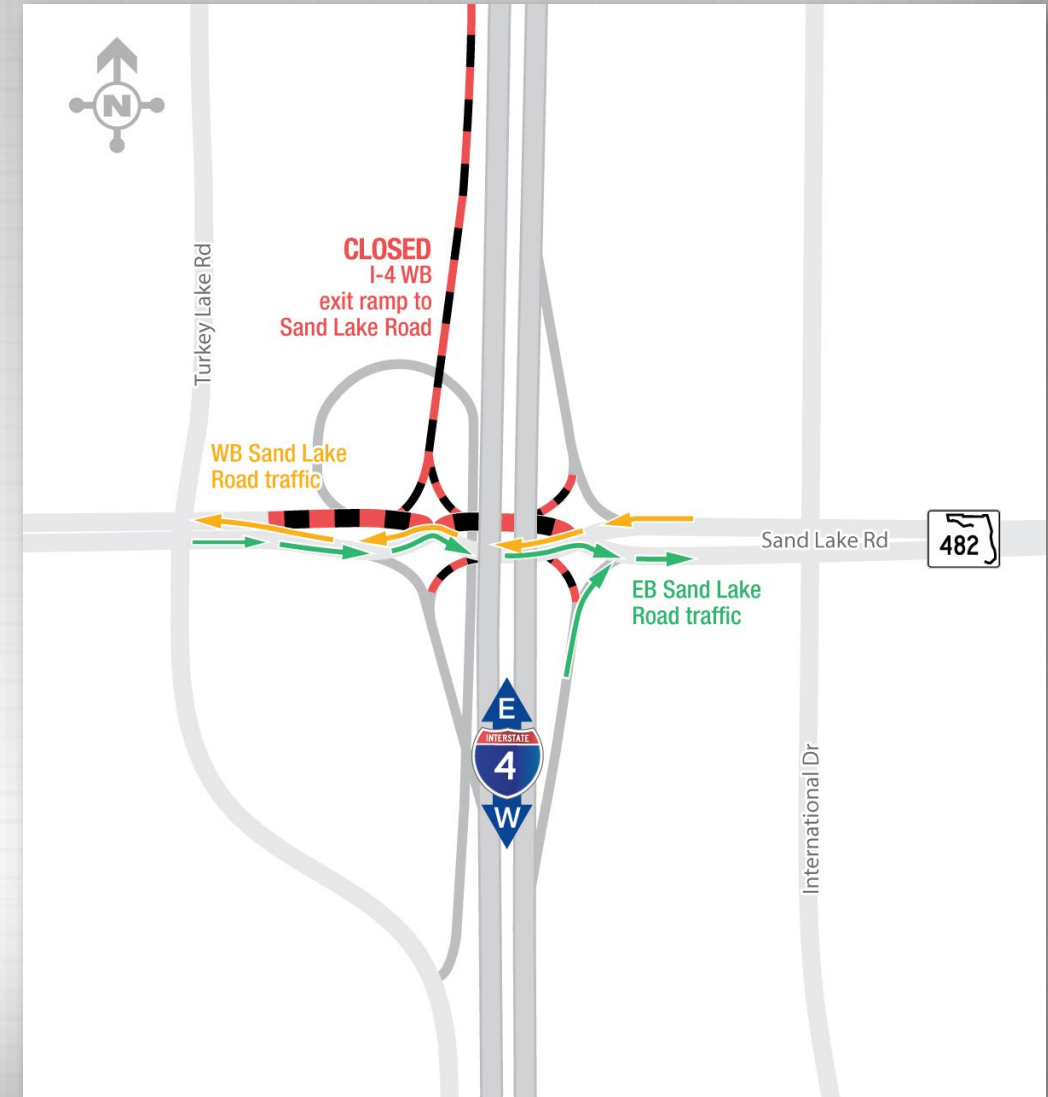



# Agenda — New Business

**Next meeting: 02/18/26**
