



I-4 and Sand Lake Road Interchange Design-Build

04/29/2026

I4Beyond.com



Status as of April 27, 2026

Days Used	Total Days	% Days Complete	Last Contract Day
1,121	1,753	63.9%	1/19/2028

Sand Lake 3470				Current Week							Week 1								Week 2							
Activity ID	Activity Description	Foreman / Sub	Supt	27-Apr	28-Apr	29-Apr	30-Apr	1-May	2-May	3-May	4-May	5-May	6-May	7-May	8-May	9-May	10-May	11-May	12-May	13-May	14-May	15-May	16-May	17-May		
				MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN		
	Roadway																									
TW130	Exc/Grade Wall 4-1	Marcos C.	Tyler	X	X	X	X	X	X		X	X	X	X	X	X										
TW150	Exc/Grade Wall 4-2	Marcos C.	Tyler															X	X	X	X	X				
EW490	Place Embankment Ramp K	Stephanie C	Tyler	X	X	X	X	X	X		X	X	X	X	X	X										
EW530	Place Embankment EB XL 6239 - 6275	Stephanie C	Tyler															X	X	X	X	X				
BASE370	WB XL Plc/Fin Limerock 5230 - 5265	Jessie W	Tyler	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X				
STAB320	WB XL Mix/Plc/Fin Stab 5230 - 5265	Jessie W	Tyler	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X				
STAB300	I4 WB Tube 1430 - 1340	Ian Palasz	Tyler	X																						
	FG Ditch WB Tube 1430 - 1340	Ian Palasz	Tyler								X	X	X	X	X	X		X	X	X	X	X				
	Ramp L Temp Limerock (tie-in)	Ian Palasz	Tyler		X	X	X	X	X	X																
	Clean Team Sand Lake Sidewalks, Trash pickup and Mowing	Billy Worles	Greg L	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X				
	Sand Lake off and on ramps to I-4 - Trash pickup and Mowing	Billy Worles	Greg L	X	X	X												X	X	X	X	X				
	Turkey Lake Sidewalks, Trash pickup and Mowing	Billy Worles	Greg L				X	X			X									X	X					
	Kirkman ramp - Trash pickup and Mowing	Billy Worles	Greg L									X	X	X								X				
FLAT120	Turkey Lake Assist OPC on Mill Lime rock operation	Isaias Barcenas	Greg L	N																						
	Ramp M2 Opening																									
	CB Top complete Turkey Lake																									
	Signage	Conti	Greg L	X	X	X	X																			
	Traffic signals	Conti	Greg L	X	X	X	X	N																		
	Traffic Swap	Jacob L	Dennis Scott					N																		
	Install Lane Signs Support M switch	Edward Benitez	Greg L					N																		
	Drainage / Utilities																									
	S-526 to S-530	Jose Castro C.	Greg L															X	X							
DRG280	S-531 to S-526 (18")	Jose Castro C.	Greg L								X	X	X	X												
DRG280	S-533	Jose Castro C.	Greg L												X	X										
DRG280	S-534 to S535	Jose Castro C.	Greg L					X	X																	
DRG280	S-536 to S-537	Jose Castro C.	Greg L	X	X	X																				
	S-542 and S-543	Jose Castro C.	Greg L				X																			
DRG450	S-2000 to S-2004 6" under drain	Isaias Barcenas	Greg L								X	X	X	X												
DRG450	S-2004 to S-2007 6" under drain	Isaias Barcenas	Greg L												X	X										
DRG450	S-2007 to S-2009 6" under drain	Isaias Barcenas	Greg L															X	X							
DRG450	S-2009 to S-2006 6"under drain	Isaias Barcenas	Greg L																	X	X	X				
DRG450	S-2006 to S-2002 6" under drain	Isaias Barcenas	Greg L																				X			
DRG380	Install S-244 to S-245 (18")	Isaias Barcenas	Greg L	X	X	X	X																			
DRG380	Install S-245 to S-243 (18")	Isaias Barcenas	Greg L								X	X	X	X												
DRG340	Install S-263 to S-266	Isaias Barcenas	Greg L												X	X		X	X							
U-OCU1540	FM N SL @ McDonald's	Edward Benitez	Greg L	N	N	N				N	N	N	N	N			N	N	N	N	N				N	
U-OCU1540	Flush/Pressure Test FM	Edward Benitez	Greg L				N																			
	Structures																									
	Bridge #7 & 8																									
	set up concrete screed/dry run	Felipe Perez	James O'Neill					X	X		X	X	X	X												
	Bridge #4																									
DEMO180	demo existing abutment 1 and mse wall	Victor /Eusebio	Jose Perez	N	N	N	N																		N	
DEMO180	cut beams to be load out	Juan/Victor	James O'Neill	X																						

N/P - Night Pour	
X - Day Schedule	T-N - Tentative
NC - Night Time Confirmed	N - Night
TS-Traffic Shift	D-Pile Delivery

Sand Lake 3470				Current Week								Week 1								Week 2							
Activity ID	Activity Description	Foreman / Sub	Supt	27-Apr	28-Apr	29-Apr	30-Apr	1-May	2-May	3-May	4-May	5-May	6-May	7-May	8-May	9-May	10-May	11-May	12-May	13-May	14-May	15-May	16-May	17-May			
				MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN			
PILE250	postion crane on pier 2	Juan	James O'Neill		N									N													
	Pile equipment and assembly	Juan	James O'Neill			N												D	X								
	template/drive pier 2 pile	Juan	James O'Neill												X	X					X	X					
	Build Temp and Crane	Juan pinero	James O'Neill	X	X	X	X	X													X						
	NATT (prpopsd pile delivery)	Juan Pinero	James O'Neill									ND		ND						ND		ND					
	excavate pylon footer	victor Medina	Jose Perez								X	X	X														
	Form Pylon footer	victor Medina	Jose Perez											X	X												
	Subcontractor																										
BW290	Median Barrier I4 WB 5230 - 5265	Blount Sanford	Rainer	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X					
BW290	Median Barrier I4 XL's (6225 - 6239)	Blount Sanford	Rainer															X	X	X	X	X					
BW290	Guardrail Removal I4 EB GUL	ACME Guardrail	Nate								X	X	X	X	X												
GR120	Guardrail Ramp M2-M3	ACME Guardrail	Nate	N	N	N	N																				
STRP260	Stripe M-2	McShea	Nate					N																			
EW230	Mill and Fill Turkey Lake Rd Inside	Hubbard	Nate	N																							
	Misc Asphalt Under Bridge 5	Hubbard	Nate		N																						
	Asphalt Repair Forcemain trench	Hubbard	Nate		N																						
	Temp Overbuild on South End of Project	Hubbard	Nate			N																					
	Traffic Swap Ramp M2 & Turkey Lake rd Phase 1C	McShea	Nate			N	N	N																			
	Restripe and shift South end P-1 Step 3	McShea	Nate			N	N																				
	WB Tube	Hubbard	Nate				N			N																	
	Cover Temp Pavement marking/ place RPM's on TLR	McShea	Nate			N	N																				
PAVE340	Paving on WB Tube	Hubbard	Nate	N	N	N	N																				
	Conti																										
LGHT130	Bridge 3 Underdeck	Conti	Rainer															X	X	X	X	X					
ITS120	ITS Conduit I-4 EB Sta: 1433 - 1480	Conti/Vasi/KDI	Rainer	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X					
	Signal Pole 3 (SLR/TLR)	Conti/Reliable	Rainer	N																							
SIGN100	Drill Shaft OHS 5 RT	Conti/Reliable	Rainer		N	N	N																				
TOLL110	Bore Service Conduit	Conti/Vasi/KDI	Rainer															X	X	X	X	X					
	Ramp M2 Opening																										
	WWD Test	Conti	Rainer			X	X																				
	Signals Temp	Conti	Rainer	N	N			N																			
	Lighting Temp	Conti	Rainer					N																			
	Existing Ped Signals	Conti	Rainer					N																			
	OHC 10 & MP 5 Install	Conti	Rainer			N	N																				
	OHC 16 Install	Conti	Rainer			N	N																				
	Temp Signs SLR (Two TLR Sign)	Conti	Rainer			X	X																				
	Temp Signs TLR/SLS Ground Mounts	Conti	Rainer		X	X	X																				
	Temp Signs TLR/SLS Overhead	Conti	Rainer	N	N			N																			
	Temp Signs TLR/SLR Overhead	Conti	Rainer					N																			
	SLR/TLR Signal Head Adjustment	Conti	Rainer					N																			
	Sand Lake Road Closures / Sidewalk																										
	Sand Lake Rd & Ramps																										
	Sand Lake WB Contra flow (Bridge Work)	James	Dennis	N	N	N	N			N	N	N	N	N			N	N	N	N	N						
	Sand Lake EB Contra flow (Bridge Work)	James	Dennis	N	N	N	N			N	N	N	N	N			N	N	N	N	N						
	Sand Lake Rd EB Double Lane	Lane	Dennis					N	N																		
	Ramp M Full Closure (Overhead Sign Installtion)	Lane	Dennis			N	N																				
	Ramp M Closure (Ramp Opening)	Lane	Dennis					N	N																		
	Turkey Lake Rd North & South (Single Outside Lanes)	Lane	Dennis	N	N	N	N			N	N	N	N	N			N	N	N	N	N						
	I-4 Single Lane Closures EB	Lane	Dennis	N	N	N	N			N	N	N	N	N			N	N	N	N	N						
	I-4 Single Lane Closures WB	Lane	Dennis	N	N	N	N			N	N	N	N	N			N	N	N	N	N						

N/P - Night Pour

X - Day Schedule


NC - Night Time Confirmed

TS-Traffic Shift

T-N - Tentative

N - Night

D-Pile Delivery

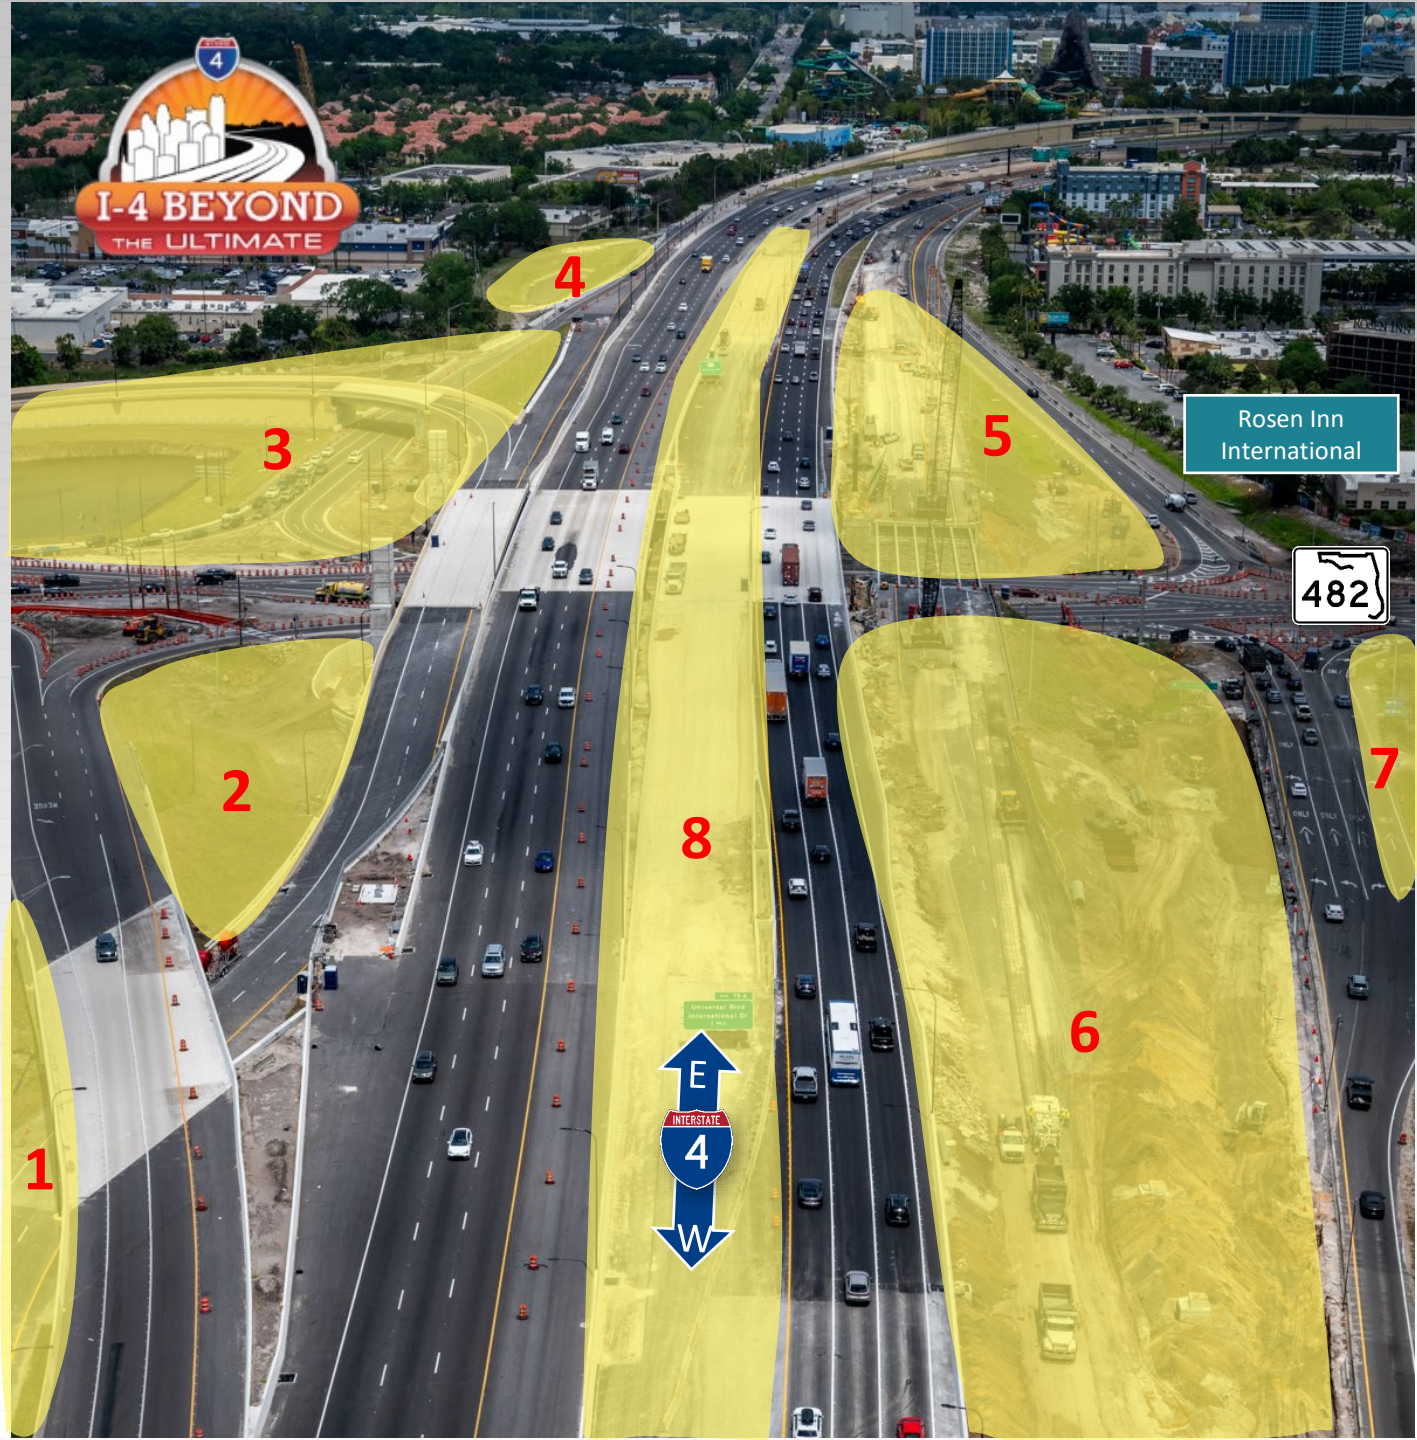



Agenda — Current Project Status

- **Past Project Status — FDOT to review past 7 days**
 - Bridge demolition and beam removal over Sand Lake Road (Area 8)
 - Force main installation and testing (Areas 3 and 5)
 - Sand Lake Road loop ramp tie-in (Areas 1 and 3)
 - Turkey Lake Road median grading and paving
 - Place and compact limerock (Area 8)
 - Median barrier wall installation (Area 8)
 - Signal and sign structure installation (Areas 1 and 3)
 - Excavate and grade ponds
 - Utility relocation
 - Drainage installation (Areas 1, 2, and 3)
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**









Agenda — Future Project Status

- **Future Project Status — FDOT to review next 7 days**
 - Sand Lake Road loop ramp opening
 - Miscellaneous bridge work at Sand Lake Road (Area 8)
 - Sand Lake Road pile deliveries (Area 8)
 - Miscellaneous work at Sand Lake Road loop ramp tie-in (Areas 1 and 3)
 - Force main installation (Area 5)
 - Signal and sign structure installation (Areas 1, 3, and 8)
 - Paving (Area 8)
 - Turkey Lake Road outside widening
 - Median barrier wall concrete placement (Area 8)
 - Excavate and grade ponds
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Future Project Status


- **Future Project Status — FDOT to review next 14 – 21 days**
 - Miscellaneous bridge work at Sand Lake Road (Area 8)
 - Pile driving at I-4 bridge at Sand Lake Road (Area 8)
 - Bridge work over Central Florida Parkway
 - Force main installation and testing (Areas 3 and 5)
 - Sign and signal structure installation (Areas 1, 3 and 8)
 - Place and compact limerock (Area 8)
 - Median barrier wall grading (Area 8)
 - Turkey Lake Road outside grading
 - Excavate and grade ponds
 - Drainage installation (Areas 1, 2, and 3)
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Loop Ramp Outreach Plans

In-person “Good Neighbor Outreach”

- Two days of outreach completed for the ramp opening (April 22, 23)
- Distributed handouts as well as digital outreach to HOAs of gated communities
 - 4/22 In-person – 246 handouts, 150 businesses/residential areas reached
 - 4/23 In-person – 224 handouts, 148 businesses/residential areas reached

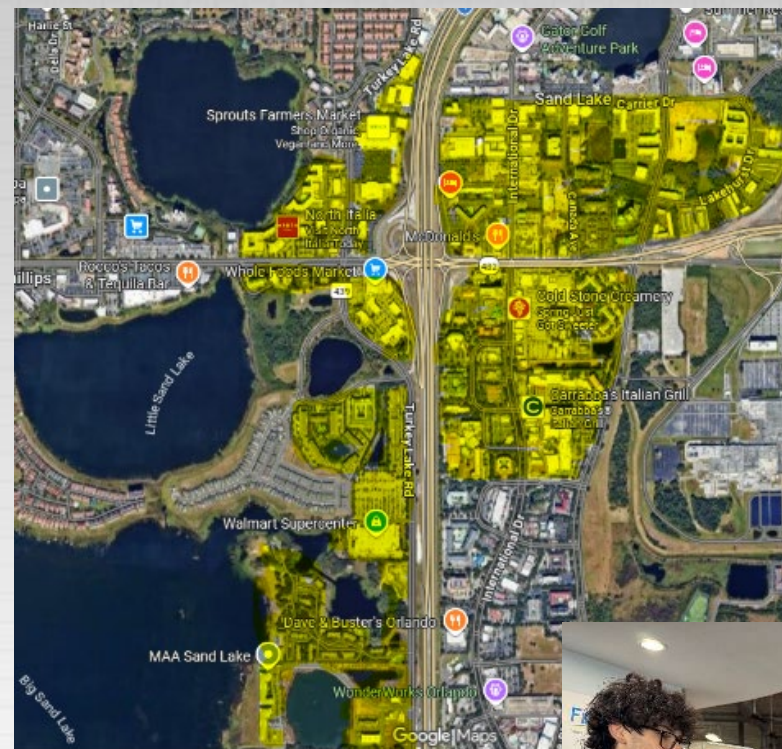



Loop Ramp Outreach Plans

Fence Banner Designs

- Approved banners have been printed
- To be placed along Sand Lake Road the day of opening

Loop Ramp Videos

- Videos have been approved by PIO and are now live.
- Began geo-fenced boosted social campaign on Thursday, April 23.





115K
VEHICLES DAILY



Agenda — Cleanliness Review

- **Cleanliness Review**
 - Committee's observations over past 7 days
- **Condition Review**
 - Committee's observations over past 7 days
(fencing, wraps, barricades, temporary signage)



Agenda — Old Business

- **Public Input or Comments**
- **Commitments Update**
 - Fencing and screening
 - Mowing and cleaning
 - Clean Team
 - Express lanes signage/access
 - Hardscaping and aesthetics
 - Ponds



Safety Diversions

- **April 29 – May 1 (nightly)**
 - Westbound I-4 exit ramp to Sand Lake Road for sign installation
 - 10 p.m. to 6 a.m.





Agenda — New Business

Next meeting: 05/06/2026
