



I-4 and Sand Lake Road Interchange Design-Build

05/13/2026



Status as of May 11, 2026

Days Used	Total Days	% Days Complete	Last Contract Day
1,135	1,754	64.7%	1/20/2028

Sand Lake 3470				Current Week								Week 1								Week 2							
Activity ID	Activity Description	Foreman / Sub	Supt	11-May	12-May	13-May	14-May	15-May	16-May	17-May	18-May	19-May	20-May	21-May	22-May	23-May	24-May	25-May	26-May	27-May	28-May	29-May	30-May				
				MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT				
	Roadway																										
TW130/EW580	Exc/Grade Wall 4-1	Marcos C.	Tyler	X	X	X	X	X																			
TW150	Exc/Grade Wall 4-2	Marcos C.	Tyler								X	X	X	X	X	X			X	X	X	X					
EW490	Place Embankment EB/Ramp K	Stephanie C	Tyler	X	X	X	X	X	X		X	X	X														
EW530	Place Embankment EB XL 6239 - 6275	Stephanie C	Tyler											X	X												
BW290	Grade for Med. Barrier 5239 - 5252	Stephanie C	Tyler															X	X	X	X						
BASE370	WB XL Plc/Fin Limerock 5230 - 5265	Jessie W	Tyler	X	X	X	X	X			X	X	X	X	X												
STAB320	WB XL Mix/Plc/Fin Stab 5230 - 5265	Jessie W	Tyler	X	X	X	X	X			X	X	X	X	X												
STAB300	I4 WB Tube 1430 - 1340	Ian Palasz	Tyler								X	X	X	X	X												
	FG Ditch WB Tube 1430 - 1340	Ian Palasz	Tyler	X	X	X	X	X																			
	Night Mot \ Erosion Deficiency Items	Dennis Scott	Greg L	N	N	N	N			N	N	N	N	N													
	Clean Team Sand Lake Sidewalks, Trash pickup and Mowing	Billy Worles	Greg L	X	X	X	X	X			X	X	X	X	X			X	X	X	X						
	Sand Lake off and on ramps to I-4 - Trash pickup and Mowing	Billy Worles	Greg L	X	X	X	X	X	X									X	X	X	X						
	Turkey Lake Sidewalks, Trash pickup and Mowing	Billy Worles	Greg L			X	X				X								X	X							
	Kirkman ramp - Trash pickup and Mowing	Billy Worles	Greg L					X				X	X	X								X					
	Place Grade Limerock on Turkey Lake for Curb and Gutter	Victor Castro	Jose Castro	X	X	X																					
	Drainage / Utilities																										
	Install S-232 To S-233	Isaias Barcenas	Greg L					X	X		X																
DRC350	Install S-230 to S-239 (30")	Isaias Barcenas	Greg L	X	X	X	X																				
	Install S-226 to S-227 (18")	Isaias Barcenas	Greg L								X	X	X														
	Pipe Repair ramp J and Sand Lake	Isaias Barcenas	Greg L											X	X	X											
	S-2009 to S-2006 6" under drain	Mark Gregory	Greg L	X	X	X	X	X																			
	S-2006 to S-2002 6" under drain	Mark Gregory	Greg L								X	X	X	X	X	X											
	S-2002 to S-2001 6" under drain	Mark Gregory	Greg L															X	X	X	X	X	X				
U-OCU1540/1560	FM N SL @ McDonald's	Edward Benitez	Greg L	N	N	N	N			N	N	N	N	N													
	Structures																										
	Bridge #7 & 8																										
	set up concrete screed/dry run	Felipe Perez/Jaime	Jose Perez	x	x																						
	place concrete on B8	Felipe Perez	Jose Perez			P	B/P																				
	Bridge #4																										
	demo existing mse wall north side	Victor /Eusebio	Jose Perez	x	x	x	x	x			x	x	x	x	x												
EXC200	excaavate pier 2 b4 footer install trench box	Eusebio/Victor	Jose Perez							N	N	N	N	N													
	move Pile equipment	Juan	James O'Neill					x	x																		
PILE250	template/drive pier 2 pile	Juan/Eusebio	James O'Neill	x	x	x	x	x	x		x	x	x	x	X			x	X	x	X						
	cut Pile	Juan	James O'Neill					x	x																		
	Build Temp and Crane pier 1	Juan pinero	James O'Neil								x	x	x	x	x												
	Pile Delivery (Pier)	Juan Pinero	James O'Neil	ND		ND												ND		ND							
	Pite Delivery (EB1)	Juan Pinero	James O'Neil								ND			ND													
	C.I.P under b2 & B3 endbent 1 vertical	Victor	Jose Perez	x	x	x	x	x																			
	Subcontractor																										
BW300	Median Barrier EB 7195 - 7199	Blount Sanford	Rainer															X	X	X	X						
BW290	Median Barrier I4 WB 5230 - 5265	Blount Sanford	Rainer			X	X	X																			
BW290	Median Barrier I4 XL's (6225 - 6239)	Blount Sanford	Rainer			X	X	X																			
	Restripe and shift South end P-1 Step 3	McShea	Nate															N	N								
PAVE340	Paving on WB Tube	Hubbard	Nate															N	N	N							
LGHT130	Bridge 3 Underdeck	Conti	Rainer								X	X	X	X	X												
	ITS																										
ITS120	ITS Conduit I-4 EB Sta: 1433 - 1480	Conti/Vasi/KDI	Rainer	X	X	X	X	X			X	X	X	X	X			X	X	X	X						

N/P - Night Pour

X - Day Schedule

NC - Night Time Confirmed

TS-Traffic Shift


T-N - Tentative

N - Night

D-Pile Delivery

Sand Lake 3470				Current Week								Week 1								Week 2							
Activity ID	Activity Description	Foreman / Sub	Supt	11-May	12-May	13-May	14-May	15-May	16-May	17-May	18-May	19-May	20-May	21-May	22-May	23-May	24-May	25-May	26-May	27-May	28-May	29-May	30-May				
				MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT				
	<u>Toll Plaza</u>																										
TOLL110	Bore Service Conduit	Conti/Vasi/KDI	Rainer								X	X	X	X	X												
TOLL140	Set Building	Conti	Rainer																	N	N						
	Sand Lake Road Closures / Sidewalk																										
	<u>Sand Lake Rd & Ramps</u>																										
	Sand Lake WB Contra flow (Bridge Work)	James	Dennis	N	N	N	N			N	N	N	N	N				N	N	N	N						
	Sand Lake EB Contra flow (Bridge Work)	James	Dennis	N	N	N	N			N	N	N	N	N				N	N	N	N						
	Turkey Lake Rd North & South (Single Outside Lanes)	Lane	Dennis	N	N	N	N			N	N	N	N	N				N	N	N	N						
	<u>I-4 EB</u>																										
	I-4 Single Lane Closures EB	Lane	Dennis	N	N	N	N			N	N	N	N	N				N	N	N	N						
	<u>I-4 WB</u>																										
	I-4 Single Lane Closures WB	Lane	Dennis	N	N	N	N			N	N	N	N	N				N	N	N	N						

N/P - Night Pour	
X - Day Schedule	T-N - Tentative
NC - Night Time Confirmed	N - Night
TS-Traffic Shift	D-Pile Delivery

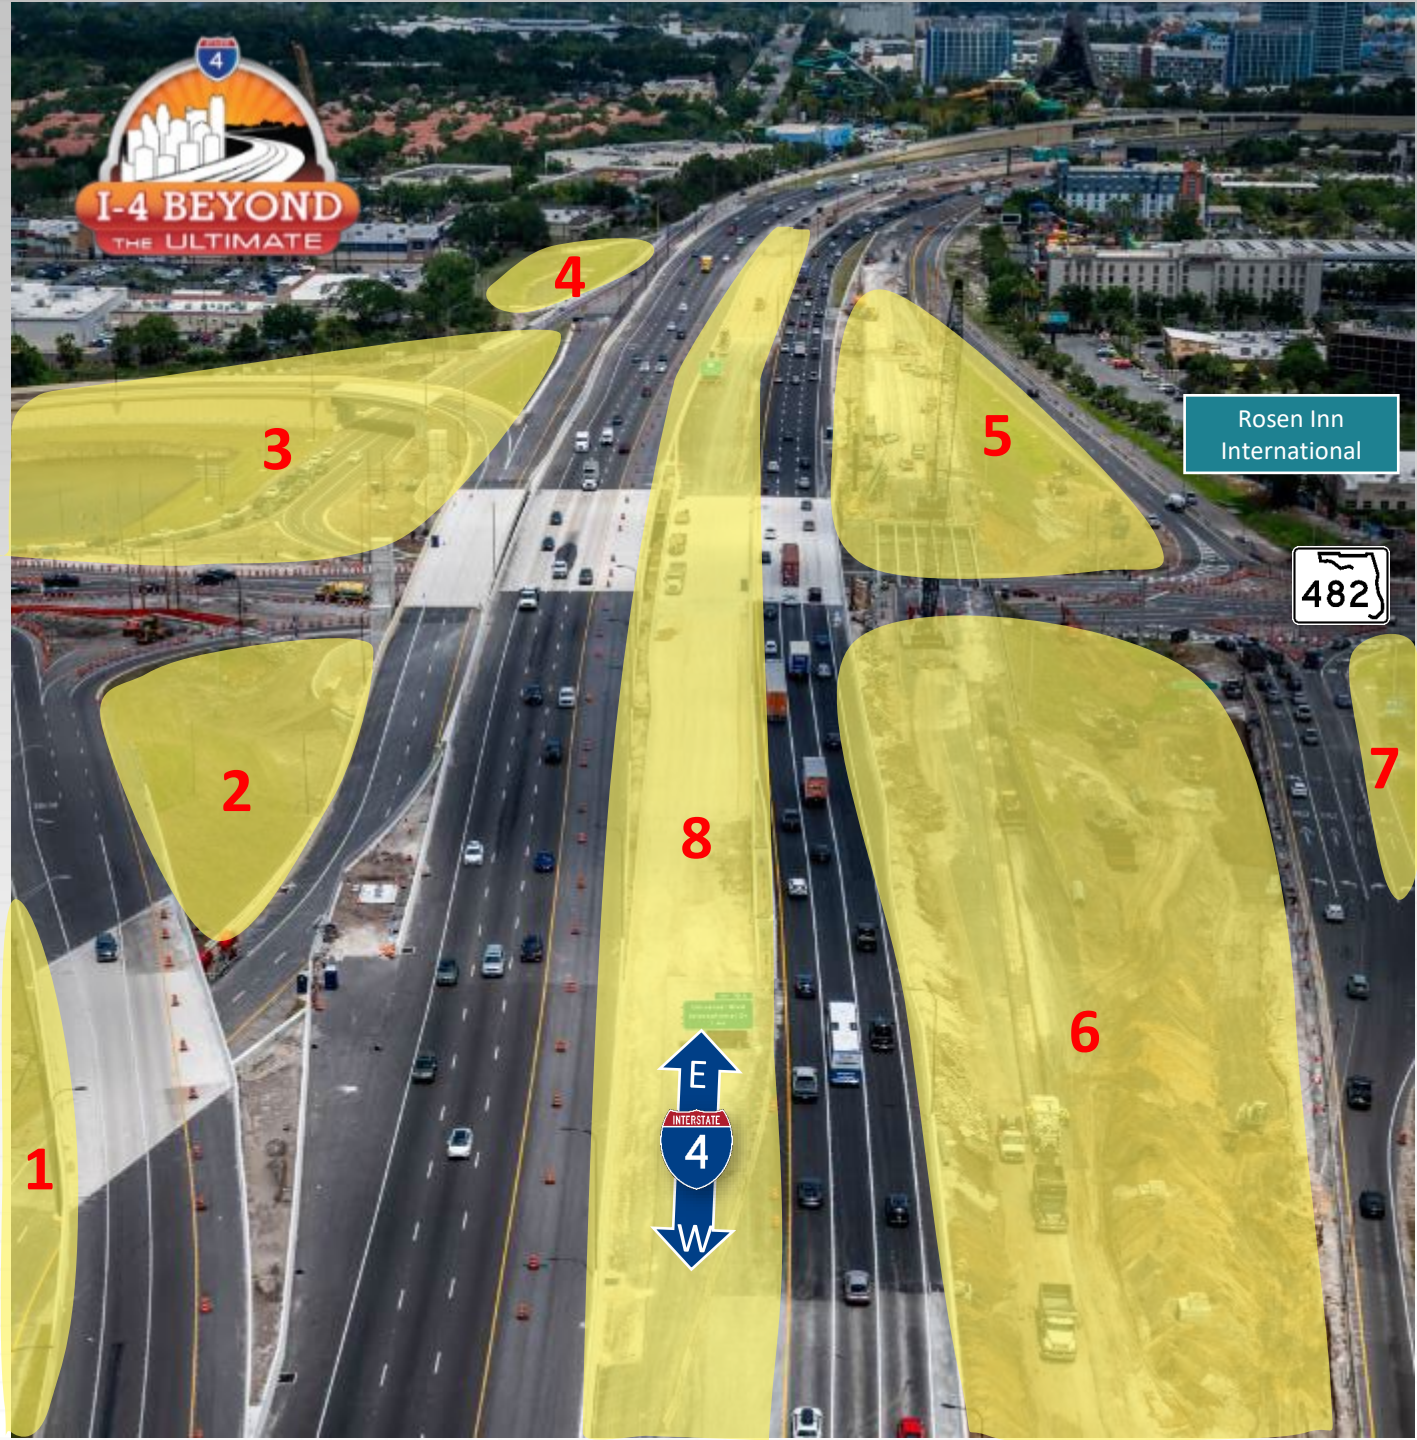



Agenda — Current Project Status

- **Past Project Status — FDOT to review past 7 days**
 - Loop ramp system opening – May 2
 - Bridge demolition and pile driving at Sand Lake Road (Area 8)
 - Bridge work over Central Florida Parkway
 - Force main installation and testing (Area 5)
 - Turkey Lake Road outside grading and widening
 - Place and compact limerock (Area 8)
 - Median barrier wall installation (Area 8)
 - Signal and sign structure installation
 - Excavate and grade ponds
 - Utility relocation
 - Drainage installation (Areas 1, 2, and 3)
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**










Agenda — Future Project Status

- **Future Project Status — FDOT to review next 7 days**
 - Miscellaneous bridge demolition work and pile driving at Sand Lake Road (Area 8)
 - Bridge work over Central Florida Parkway
 - Sand Lake Road pile deliveries (Area 8)
 - Force main installation (Area 5)
 - Signal and sign structure installation (Areas 1, 3, and 8)
 - Turkey Lake Road outside widening
 - Median barrier wall concrete placement (Area 8)
 - Excavate and grade ponds
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**




Agenda — Future Project Status

- **Future Project Status — FDOT to review next 14 – 21 days**
 - Miscellaneous bridge demolition work and pile driving at Sand Lake Road (Area 8)
 - Force main installation and testing (Areas 3 and 5)
 - Sign and signal structure installation
 - Place and compact limerock (Area 8)
 - Median barrier wall grading (Area 8)
 - Turkey Lake Road outside grading and widening
 - Excavate and grade ponds
 - Paving (Area 8)
 - Drainage installation (Areas 1, 2, and 3)
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**

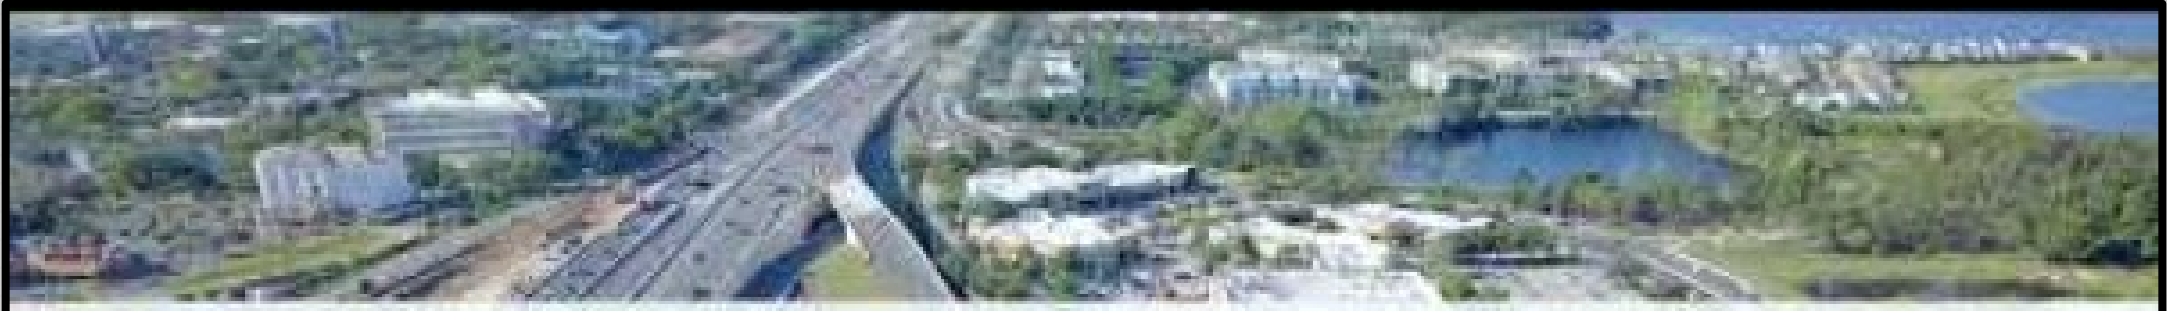

NOW OPEN

New Ramp System at I-4 and Sand Lake Road

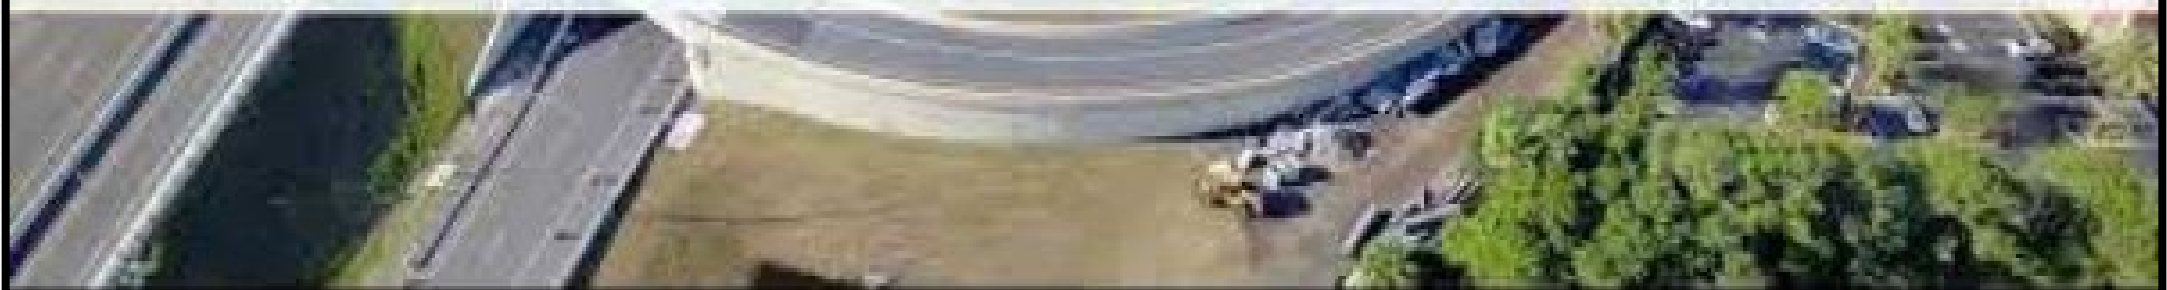



Agenda — Cleanliness Review

- **Cleanliness Review**
 - Committee's observations over past 7 days
- **Condition Review**
 - Committee's observations over past 7 days
(fencing, wraps, barricades, temporary signage)




Agenda — Old Business

- **Public Input or Comments**
- **Commitments Update**
 - Fencing and screening
 - Mowing and cleaning
 - Clean Team
 - Express lanes signage/access
 - Hardscaping and aesthetics
 - Ponds



Safety Diversions

- **May 14 (overnight)**
 - Eastbound/westbound Central Florida Parkway under I-4
 - 12 a.m. to 5 a.m.

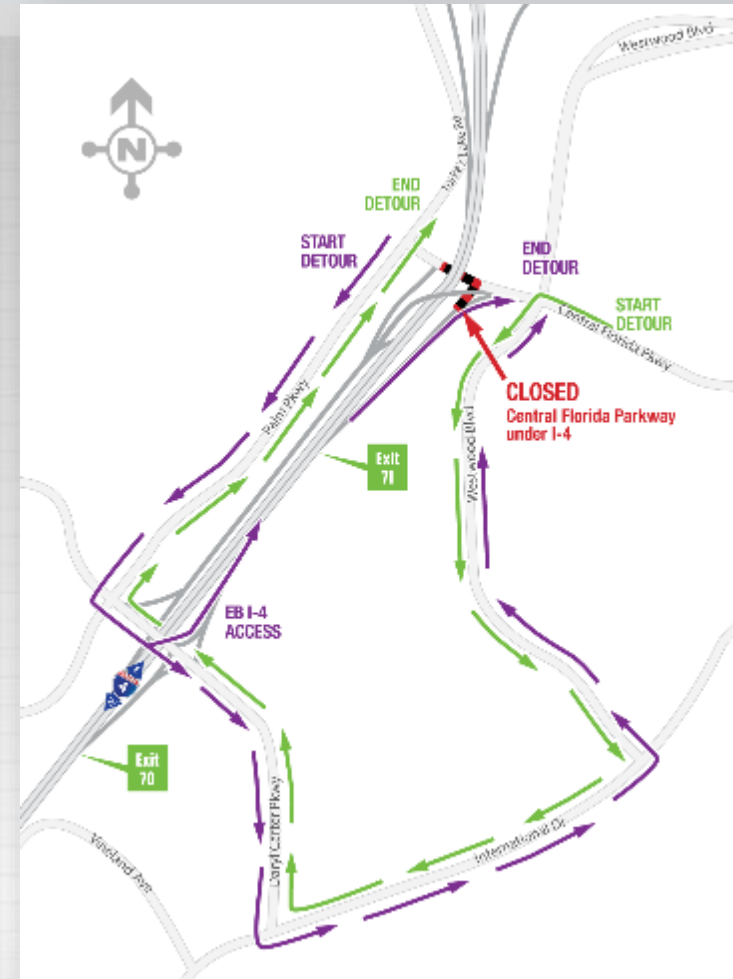



Agenda — New Business

Next meeting: 05/20/2026
