



I-4 and Sand Lake Road Interchange Design-Build

06/01/2026

I4Beyond.com



Status as of June 1, 2026

Days Used	Total Days	% Days Complete	Last Contract Day
1,156	1,754	65.9%	1/20/2028

Sand Lake 3470						Current Week							Week 1							Week 2						
Show/Hide	FLOAT	Activity ID	Activity Description	Foreman / Sub	Supt	1-Jun	2-Jun	3-Jun	4-Jun	5-Jun	6-Jun	7-Jun	8-Jun	9-Jun	10-Jun	11-Jun	12-Jun	13-Jun	14-Jun	15-Jun	16-Jun	17-Jun	18-Jun	19-Jun	20-Jun	21-Jun
						MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN
X			Roadway																							
	84	MSE310	Exc/Grade Wall 4-1	Marcos C.	Tyler	X				X	X		X	X	X	X	X	X		X	X	X	X		X	
	203	SUBS320	Excavate/Grade Pylon Footing 4-1	Marcos C.	Tyler		X		X																	
	6	EW710	Place Embankment EB XL 6239 - 6275	Marcos C.	Tyler	X	X	X	X	X																
	-	BASE370/390	WB XL Plc/Fin Limerock 5238 - 5252	Jessie W	Tyler	X	X																			
	63	EW570	Ph. 2C - EB Widening 1440 - 1450	Jessie W	Tyler			X	X	X	X		X	LBR	LBR	LBR	LBR	LBR			X	X	X	X		
	126	STAB390	Ph. 2C - EB Reconstruct - Mix/Plc/Fin stab (1437 - 1465)	Jessie W	Tyler								X	X	X	X	X	X			LBR	LBR	LBR	LBR		
	-	EW500	I4 WB Tube 1430 - 1340	Ian Palasz	Tyler	X	X	X																		
	344	STAB300	I4 WB Tube - Balance/Mix 1355 - 1335 (bridge 7)	Ian Palasz	Tyler				X	X			X	LBR	LBR	LBR	LBR	LBR								
	364	BASE360	I4 WB Tube - Plc/Fin Lime Rock 1355 - 1335 (bridge 7)	Ian Palasz	Tyler																				X	
	126	BASE450	Ph. 2C - EB Reconstruct - Plc/Fin Limerock (1437 - 1465)	Ian Palasz	Tyler									X	X	X	X	X	X		X	X	X	X		
X			Clean Team Sand Lake Sidewalks, Trash pickup and Mowing	Billy Wortes	Greg L	X	X	X	X	X			X	X	X	X	X	X			X	X	X			
			Sand Lake off and on ramps to I-4 - Trash pickup and Mowing	Billy Wortes	Greg L	X	X	X													X	X	X			
			Turkey Lake Sidewalks, Trash pickup and Mowing	Billy Wortes	Greg L				X	X	X														X	
			Kirkman ramp - Trash pickup and Mowing	Billy Wortes	Greg L								X	X	X											
			Remove existing Curb Turkey Lake	Victor Castro	Jose Castro	X	X	X	X	X	X		X	X	X	X	X	X			X	X	X	X		
			Place Grade Limerock on Turkey Lake for Curb and Gutter	Victor Castro	Jose Castro	X	X	X	X	X	X		X	X	X	X	X	X			X	X	X	X		
X			Drainage / UTILITIES																							
	6	DRG1370	Install S-278 to S-278A (18")	Isalas Barcenas	Greg L		X	X	X																	
	6	DRG1380	Install S-278A to S-279A (18")	Isalas Barcenas	Greg L					X	X		X	X	X	X	X									
	492	DRG300	Install S-66 to S-67 (24")	Mark Gregory	Greg L	X	X																			
	492	DRG300	Install S-64 to S-63 (24")	Mark Gregory	Greg L			X	X	X	X		X	X	X	X	X	X		X						
	492	DRG300	Install S-65 to CS-100 (24")	Mark Gregory	Greg L																X	X	X			
	492	DRG300	Install S-84 to S-83 (29"X45")	Mark Gregory	Greg L																				X	
	69	U-OCU1540	Install FM Sand Lake ramp M	Edward Benitez	Greg L	N	N	N	N			N	N	N	N	N			N	N	N	N	N			N
			Structures																							
			Bridge #7 & 8																							
			Rub and patch B7&8	Jaime	Jose Perez	N			N					N	N	N	N	N								
			strip edge forms	Jaime	Jose Perez	N	N	N	N					N	N	N	N	N								
			remove temp deck under b7&8	Jaime	Jose Perez	N	N	N	N																	
			Bridge #4																							
	62	PILE250	template/drive pier 2 pile	Juan Pinero	James O'Neill	X	X	X	X	X			X	X	X	X	X				X	X	X			
	75	PILE270	drive embedment 2 pile	Juan Pinero	James O'Neill									X	X						X	X	X	X		X
			cut Pile	Juan Pinero	James O'Neill									X	X											
	62	SUBS260	dewater & F/G footer	Eusebio	Jose Perez			X	X	X	X		X													
	62	CURE220	Form/pour/remove, footer pier 2	Eusebio	Jose Perez										X	X	X	X		X	X					
			Pile Delivery (Pier)	Juan Pinero	James O'Neill	ND		ND		ND			ND													
			Pile Delivery (EB1)		James O'Neill																					
			Pile Delivery (EB3)		James O'Neill																					
			Pylon Footing North																							
	-	SUBS200	make Forms pylon footer	Victor Medina	Jose Perez	X	X	X																		
	-	SUBS200	Form Pylon footer	Victor Medina	Jose Perez	X	X	X	X	X			X	X	X	X	X	X								
			Subcontractor																							
	-	BW300	Median Barrier EB 7195 - 7199	Blount Sanford	Rainer	X	X	X	X	X																
	-	TW130	Wire Wall 9-1	RWH	Nate	X	X	X	X	X																
	84	MSE310	RW 4-1	RWH	Nate						X		X	X	X	X	X			X	X	X	X			
			Phase 2A-2B Barrier Wall	TCP	Harry																					
	6	DRG1400	Install 36" J&B S-726 - S727 (Tube Area 4)	CFU	Greg	X	X	X	X	X																
	326	DRG310	Install 30" J&B S-55 - S404OF (Tube Area 3)	CFU	Greg								X	X	X	X	X									
	326	DRG310	Install 30" J&B S-56 - S422A (Tube Area 3)	CFU	Greg															X	X	X	X			
			Ramp L Tie in	Hubbard		N																				
	-	PAVE360	Paving on WB Tube	Hubbard		N	N	N	N																	
			Mill & Resurface WB Inside Shld Gut (1499+00 - 1509+00)	Hubbard									N													
			EB Outside Temp Shld Overbuild (1521+00 - 1533+00)	Hubbard																						
	-		WB Express lanes (1499+00 - 1509+00)	Hubbard											N	N	N									
	123	PAVE440	Ramp K paving	Hubbard															N	N	N	N				
			Guardrail Removal (Sta 1336+00 to 1357+50)	Acme		X	X	X	X	X																
			Lighting																							
			Lighting Maintenance (Existing Circle K Sign)	Conti	Rainer			X	X	X																
	404	LGHT130	Bridge 3 Underdeck	Conti	Rainer								X	X	X	X	X	X								
	-	LGHT110	Lighting Load Center C (Ramp J) Conduit	Conti	Rainer	X	X	X	X	X			X	X	X	X	X	X		X	X	X	X			
			Service Conduit Lighting Load Center C (Ramp J)	Conti/Vasi	Rainer	X	X	X	X	X			X	X	X	X	X	X		X	X	X	X			

N/P - Night Pour

X - Day Schedule

NC - Night Time Confirmed

TS-Traffic Shift


T-N - Tentative

N - Night

D-Pile Delivery

Sand Lake 3470																										
Show/Hide	FLOAT	Activity ID	Activity Description	Foreman / Sub	Supt	Current Week							Week 1							Week 2						
						1-Jun	2-Jun	3-Jun	4-Jun	5-Jun	6-Jun	7-Jun	8-Jun	9-Jun	10-Jun	11-Jun	12-Jun	13-Jun	14-Jun	15-Jun	16-Jun	17-Jun	18-Jun	19-Jun	20-Jun	21-Jun
						MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN
			<u>Toll Plaza</u>																							
	605	TOLL110	Bore Service Conduit	Conti/Vasi/KDI	Rainer	X	X	X	X	X			X	X	X	X	X									
	605	TOLL110	Fuel Tank Pad	Conti	Rainer															X	X	X	X			
x			Sand Lake Road Closures / Sidewalk																							
			<u>Sand Lake Rd & Ramps</u>																							
			Sand Lake WB Contra flow (Bridge Work)	James	Dennis	N	N	N	N	N		N	N	N	N	N			N	N	N	N	N			
			Sand Lake EB Contra flow (Bridge Work)	James	Dennis	N	N	N	N	N		N	N	N	N	N			N	N	N	N	N			
			Sand Lake Rd EB Single Lane Inside (Forcemain)	Lane	Dennis	N	N	N	N			N	N	N	N	N			N	N	N	N	N			
			Sand Lake Rd WB Single Lane Inside (Forcemain)	Lane	Dennis	N	N	N	N			N	N	N	N	N			N	N	N	N	N			
			Full Closure of Ramp L	Lane	Dennis																		N			
			Ramp L Single Right Lane	Lane	Dennis	N																				
			<u>I-4 EB</u>																							
			I-4 Single Lane Closures EB	Lane	Dennis	N	N	N	N			N	N	N	N	N			N	N	N	N	N			
			<u>I-4 WB</u>																							
			I-4 Single Lane Closures WB	Lane	Dennis	N	N	N	N			N	N	N	N	N			N	N	N	N	N			
			I-4 Double Lane Closures WB	Lane	Dennis				N																	
			<u>Central Florida PKWY</u>																							
			Full Detour CFP (12:30AM to 5:30AM)	Dennis	Dennis	N	N	N	N			N	N	N	N	N										

N/P - Night Pour	
X - Day Schedule	T-N - Tentative
NC - Night Time Confirmed	N - Night
TS-Traffic Shift	D-Pile Delivery

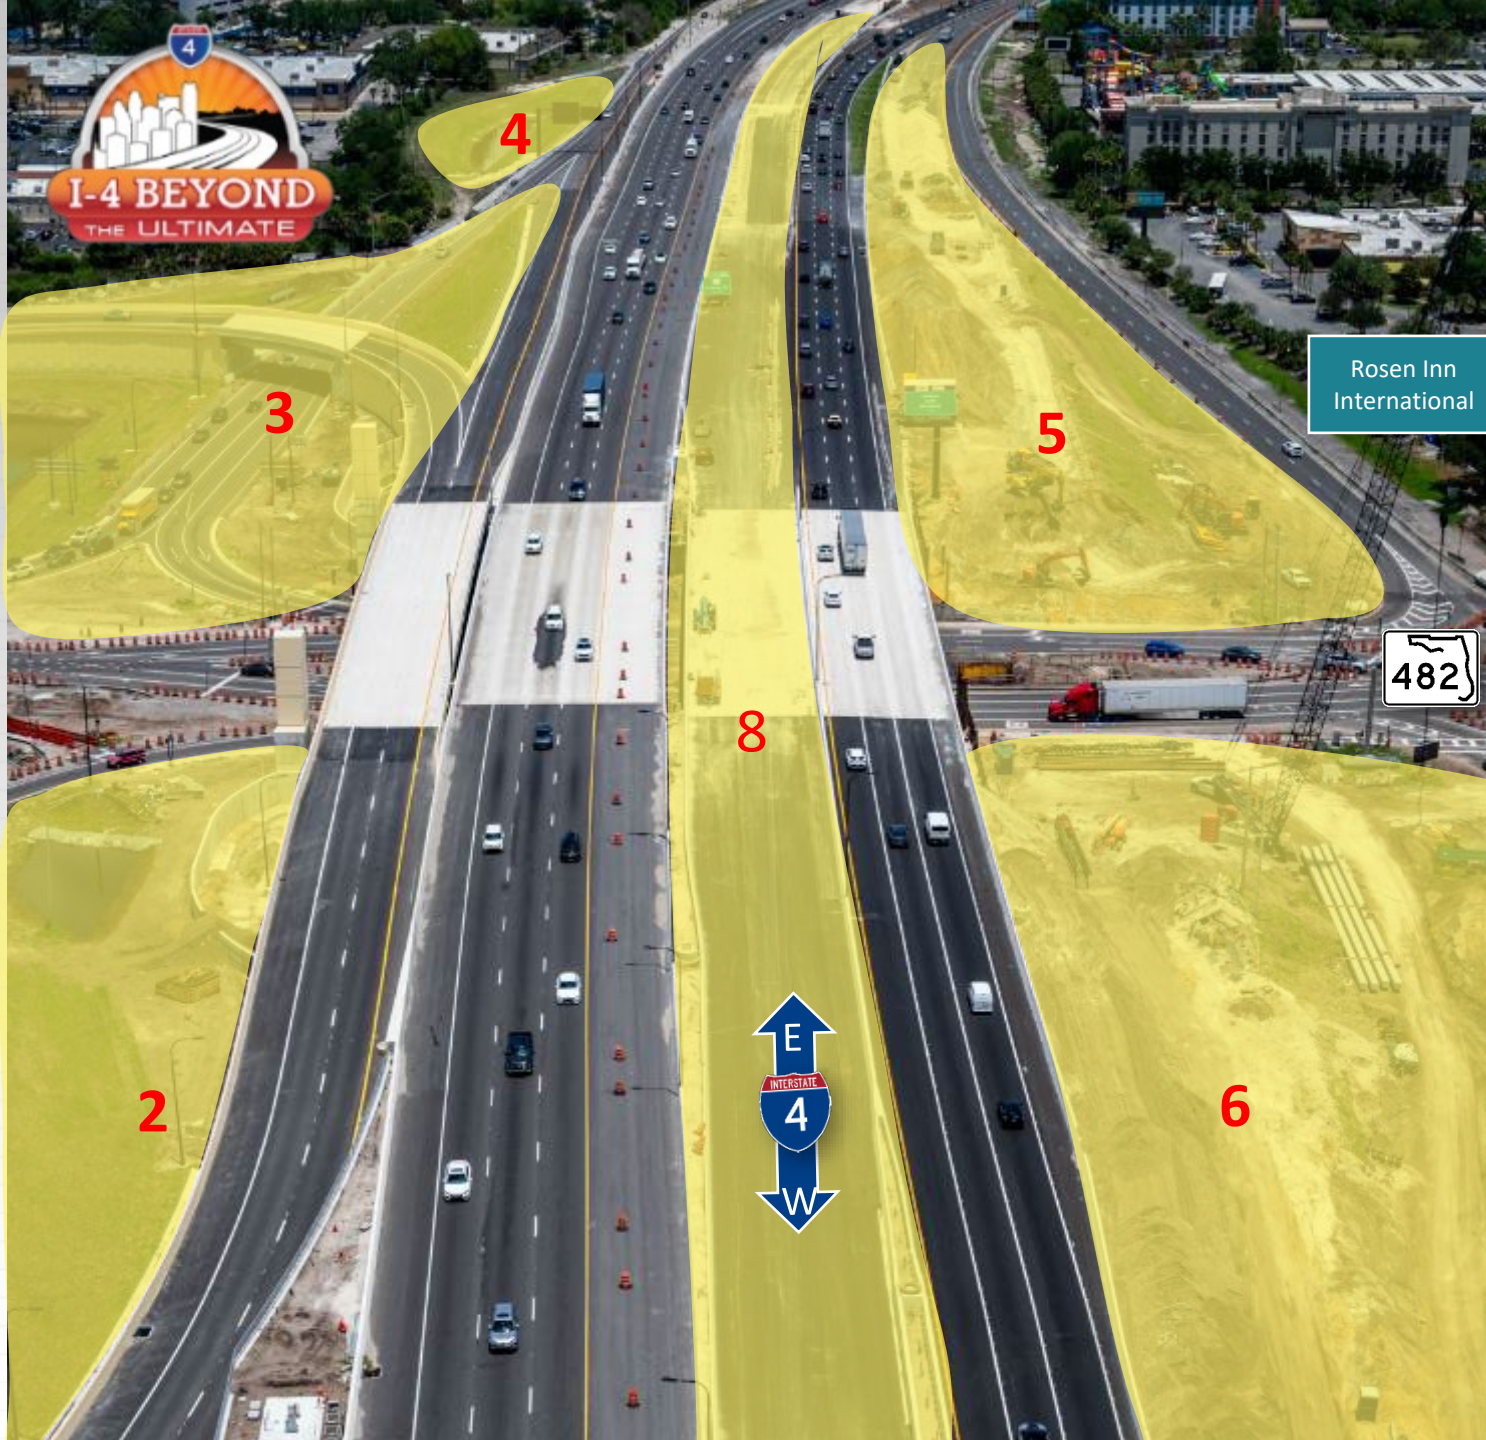



Agenda — Current Project Status

- **Past Project Status — FDOT to review past 7 days**
 - Bridge pile driving at Sand Lake Road (Area 6)
 - Sand Lake Road pile deliveries (Area 6)
 - Bridge work over Central Florida Parkway
 - Force main installation and testing (Areas 3 and 5)
 - I-4 median Paving (Area 8)
 - Turkey Lake Road outside grading and widening
 - Place and compact limerock (Area 8)
 - Embankment material placement (Area 6)
 - Median barrier wall installation (Area 8)
 - Signal and sign structure installation
 - Excavate and grade ponds
 - Utility relocation
 - Drainage installation (Areas 1, 2, and 3)
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**









Agenda — Future Project Status

- **Future Project Status — FDOT to review next 7 days**
 - Bridge pile driving at Sand Lake Road (Area 6)
 - Sand Lake Road pile deliveries (Area 6)
 - Bridge work over Central Florida Parkway
 - Force main installation and testing (Areas 3 and 5)
 - Turkey Lake Road outside grading and widening
 - Place and compact limerock (Area 8)
 - Embankment material placement (Area 6)
 - Median barrier wall installation (Area 8)
 - Signal and sign structure installation
 - Excavate and grade ponds
 - Utility relocation
 - Drainage installation (Areas 1, 2, and 3)
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Future Project Status

- **Future Project Status — FDOT to review next 14 – 21 days**
 - Miscellaneous bridge demolition work and pile driving at Sand Lake Road (Area 6)
 - Sand Lake Road pile deliveries (Area 6)
 - Force main installation and testing (Areas 3 and 5)
 - Embankment material placement (Area 6)
 - Eastbound I-4 entrance ramp shift (Area 5)
 - Paving (Area 6)
 - Place and compact limerock (Area 8)
 - Median barrier wall grading (Area 8)
 - Turkey Lake Road outside grading and widening
 - Excavate and grade ponds
 - Sign and signal structure installation
 - Drainage installation (Areas 1, 2, and 3)
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Cleanliness Review

- **Cleanliness Review**
 - Committee's observations over past 7 days
- **Condition Review**
 - Committee's observations over past 7 days
(fencing, wraps, barricades, temporary signage)




Agenda — Old Business

- **Public Input or Comments**
- **Commitments Update**
 - Fencing and screening
 - Mowing and cleaning
 - Clean Team
 - Express lanes signage/access
 - Hardscaping and aesthetics
 - Ponds



Safety Diversions

- **June 1–5 (overnight)**
 - Eastbound/westbound Central Florida Parkway under I-4 for bridge work
 - 12:30 a.m. to 5:30 a.m.

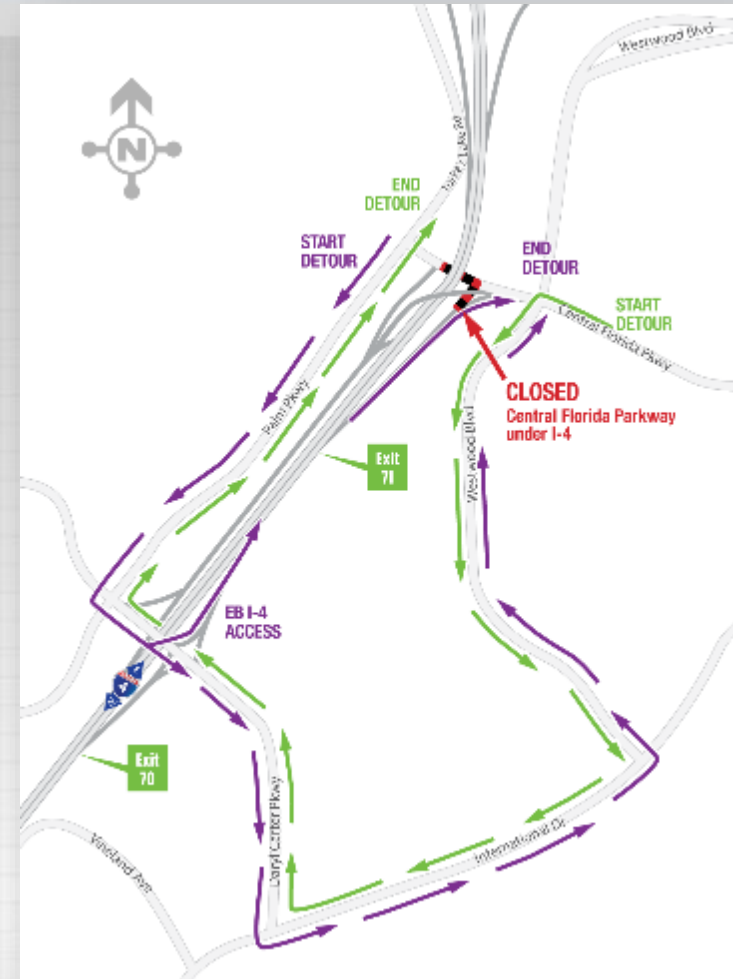



Agenda — New Business

Next meeting: 06/10/2026
