



I-4 and Sand Lake Road Interchange Design-Build

06/10/2026

I4Beyond.com



Status as of June 8, 2026


Days Used	Total Days	% Days Complete	Last Contract Day
1,163	1,757	66.2%	1/23/2028

Sand Lake 3470				Current Week								Week 1								Week 2							
Activity ID	Activity Description	Foreman / Sub	Supt	8-Jun	9-Jun	10-Jun	11-Jun	12-Jun	13-Jun	14-Jun	15-Jun	16-Jun	17-Jun	18-Jun	19-Jun	20-Jun	21-Jun	22-Jun	23-Jun	24-Jun	25-Jun	26-Jun	27-Jun	28-Jun			
				MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN			
	Structures																										
	Bridge #7 & 8																										
	Rub and patch B7&8	Jaime	Jose Perez	N	N	N	N																				
	strip edge forms	Jaime	Jose Perez	N	N	N	N	N																			
	Bridge #4																										
PILE250	template/drive pier 2 pile	Juan Pinero	James O'Neill	X	X	X	X	X																			
PILE270	drive endbent 2 pile	Juan Pinero	James O'Neill								X	X	X	X		*		X	X	X	X	X					
	cut Pile	Juan Pinero	James O'Neill	x	x																						
CURE220	Form/pour/remove, footer pier 2	Eusebio Perez	Jose Perez	x							x	x	x	x													
	assemble cap forms for pier 2	Eusebio Perez												x				x	x	x	x	x	*				
	Pile Delivery (Pier)	Juan Pinero	James O'Neil	ND																							
	Pile Delivery (EB3)	Juan Pinero	James O'Neil			X		X																			
	Pylon Footing North																										
SUBS200	Form Pylon footer	Victor Medina	Jose Perez			x	x	x	*		x	x	x	x				x	x	x	x	x					
	Subcontractor																										
BW300	Median Barrier EB 7195 - 7199	Blount Sanford	Harry	X	X	X	X	X			X	X	X	X				X	X	X	X	X					
	Pylon footer rebar 4-1	Shelby	Harry			x	x	x			x																
MSE310	RW 4-1	RWH	Nate	X	X	X	X	X			X	X	X	X				X	X	X	X	X					
	Ramp L Shift	TCP	Nate											N													
	Barrier Wall Install South End of Project (Phase 1 Step 3)	TCP	Nate																				N				
	Ramp L Shift	McShea	Nate											N													
DRG1400	Install 36" J&B S-726 - S727 (Tube Area 4)	CFU	Greg	X	X	X	X	X			X	X	X	X													
DRG310	Install 30" J&B S-55 - S404OF (Tube Area 3)	CFU	Greg															X	X	X	X	X					
PAVE360	Paving on WB Tube	Hubbard		N																							
	Mill & Resurface WB Inside Shld Gul (1499+00 - 1509+00)	Hubbard																		N	N						
	EB Outside Temp Shld Overbuild (1521+00 - 1533+00)	Hubbard			N																						
	WB Express lanes (1499+00 - 1509+00)	Hubbard															N	N	N								
PAVE440	Ramp K paving	Hubbard																					N				
	Lighting																										
LGHT130	Bridge 3 Underdeck	Conti	Rainer	X	X	X	X	X																			
LGHT110	Lighting Load Center C (Ramp J) Conduit	Conti	Rainer	X	X	X	X	X			X	X	X	X													

N/P - Night Pour	
X - Day Schedule	T-N - Tentative
NC - Night Time Confirmed	N - Night
TS-Traffic Shift	D-Pile Delivery

Sand Lake 3470				Current Week								Week 1								Week 2							
Activity ID	Activity Description	Foreman / Sub	Supt	8-Jun	9-Jun	10-Jun	11-Jun	12-Jun	13-Jun	14-Jun	15-Jun	16-Jun	17-Jun	18-Jun	19-Jun	20-Jun	21-Jun	22-Jun	23-Jun	24-Jun	25-Jun	26-Jun	27-Jun	28-Jun			
				MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN			
LCM110	Lighting Load Center C (Ramp J) Conduit	Conti	Rainer	X	X	X	X	X			X	X	X	X													
	Service Conduit Lighting Load Center C (Ramp J)	Conti/Vasi	Rainer	X	X	X	X	X			X	X	X	X													
ITS100	ITS Load Center B (Ramp K)	Conti	Rainer															X	X	X	X	X					
	<u>Toll Plaza</u>																										
TOLL240	Loop Boxes	Conti/Vasi/KDI	Rainer																								
TOLL110	Bore Service Conduit	Conti/Vasi/KDI	Rainer	X	X	X	X	X																			
TOLL110	Fuel Tank Pad	Conti	Rainer	X	X	X	X	X			X	X	X	X													
TOLL110	Load Center	Conti	Rainer															X	X	X	X	X					
	Sand Lake Road Closures / Sidewalk																										
	<u>Sand Lake Rd & Ramps</u>																										
	Sand Lake WB Contra flow (Bridge Work)	James	Dennis	N	N	N	N			N	N	N	N	N													
	Sand Lake EB Contra flow (Bridge Work)	James	Dennis	N	N	N	N			N	N	N	N	N													
	Sand Lake Rd EB Single Lane Inside (Forcemain)	Lane	Dennis	N	N	N	N			N	N	N	N	N													
	Sand Lake Rd WB Single Lane Inside (Forcemain)	Lane	Dennis	N	N	N	N			N	N	N	N	N													
	Full Closure of Ramp L	Lane	Dennis											N													
	<u>I-4 EB</u>																										
	I-4 Single Lane Closures EB	Lane	Dennis	N	N	N	N			N	N	N	N	N													
	<u>I-4 WB</u>																										
	I-4 Single Lane Closures WB	Lane	Dennis	N	N	N	N			N	N	N	N	N													
	<u>Central Florida PKWY</u>																										
	Full Detour CFP (12:30AM to 5:30AM)	Dennis	Dennis	N	N	N	N																				

N/P - Night Pour	
X - Day Schedule	T-N - Tentative
NC - Night Time Confirmed	N - Night
TS-Traffic Shift	D-Pile Delivery

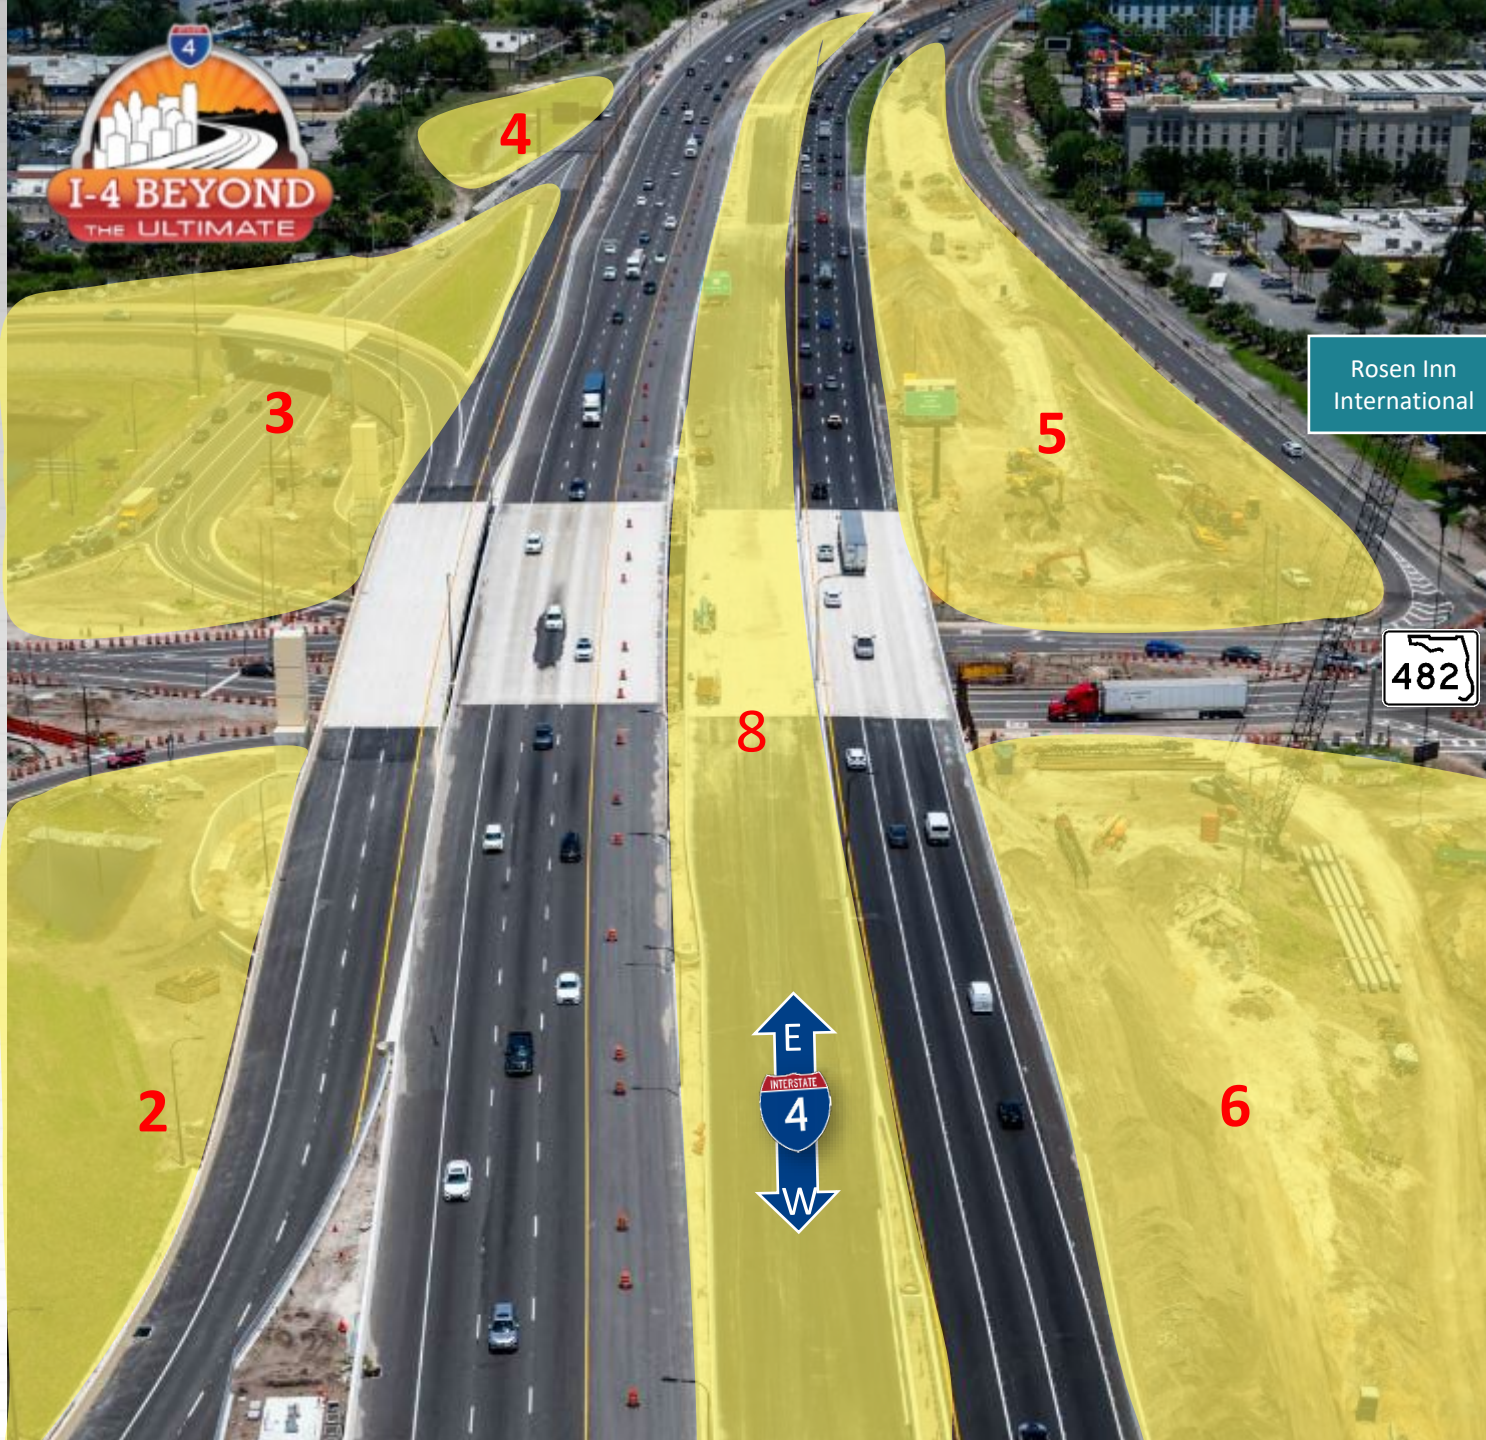




Agenda — Current Project Status


- **Past Project Status — FDOT to review past 7 days**

- Bridge pile driving at Sand Lake Road (Area 6)
- Sand Lake Road pile deliveries (Area 6)
- Bridge work over Central Florida Parkway
- Force main installation and testing (Area 3)
- I-4 median Paving (Area 8)
- Turkey Lake Road outside grading and widening
- Place and compact limerock (Area 8)
- Embankment material placement (Area 6)
- Median barrier wall installation (Area 8)
- Signal and sign structure installation
- Excavate and grade ponds
- Utility relocation
- Drainage installation (Areas 1, 2, and 3)
- Ongoing mowing and litter pickup

- **Committee's Comments & Suggestions**

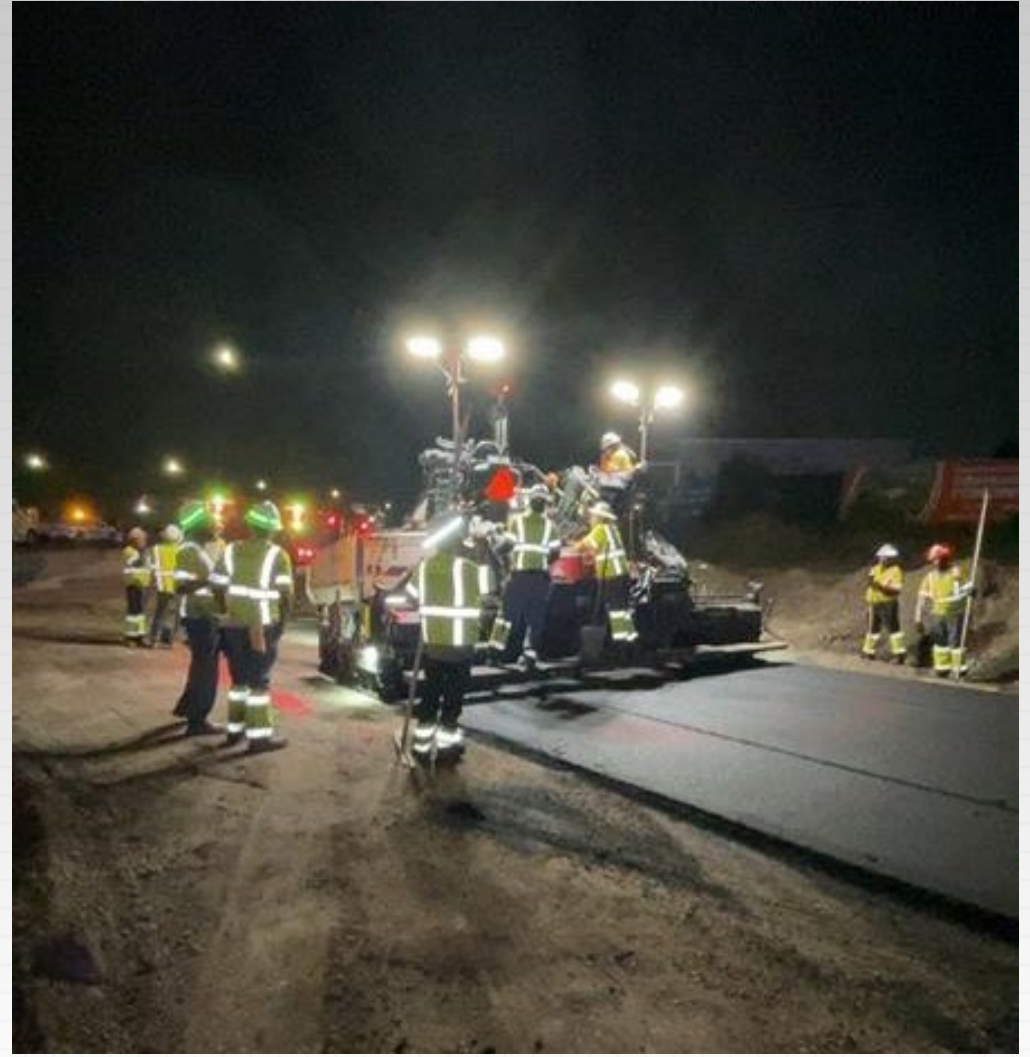



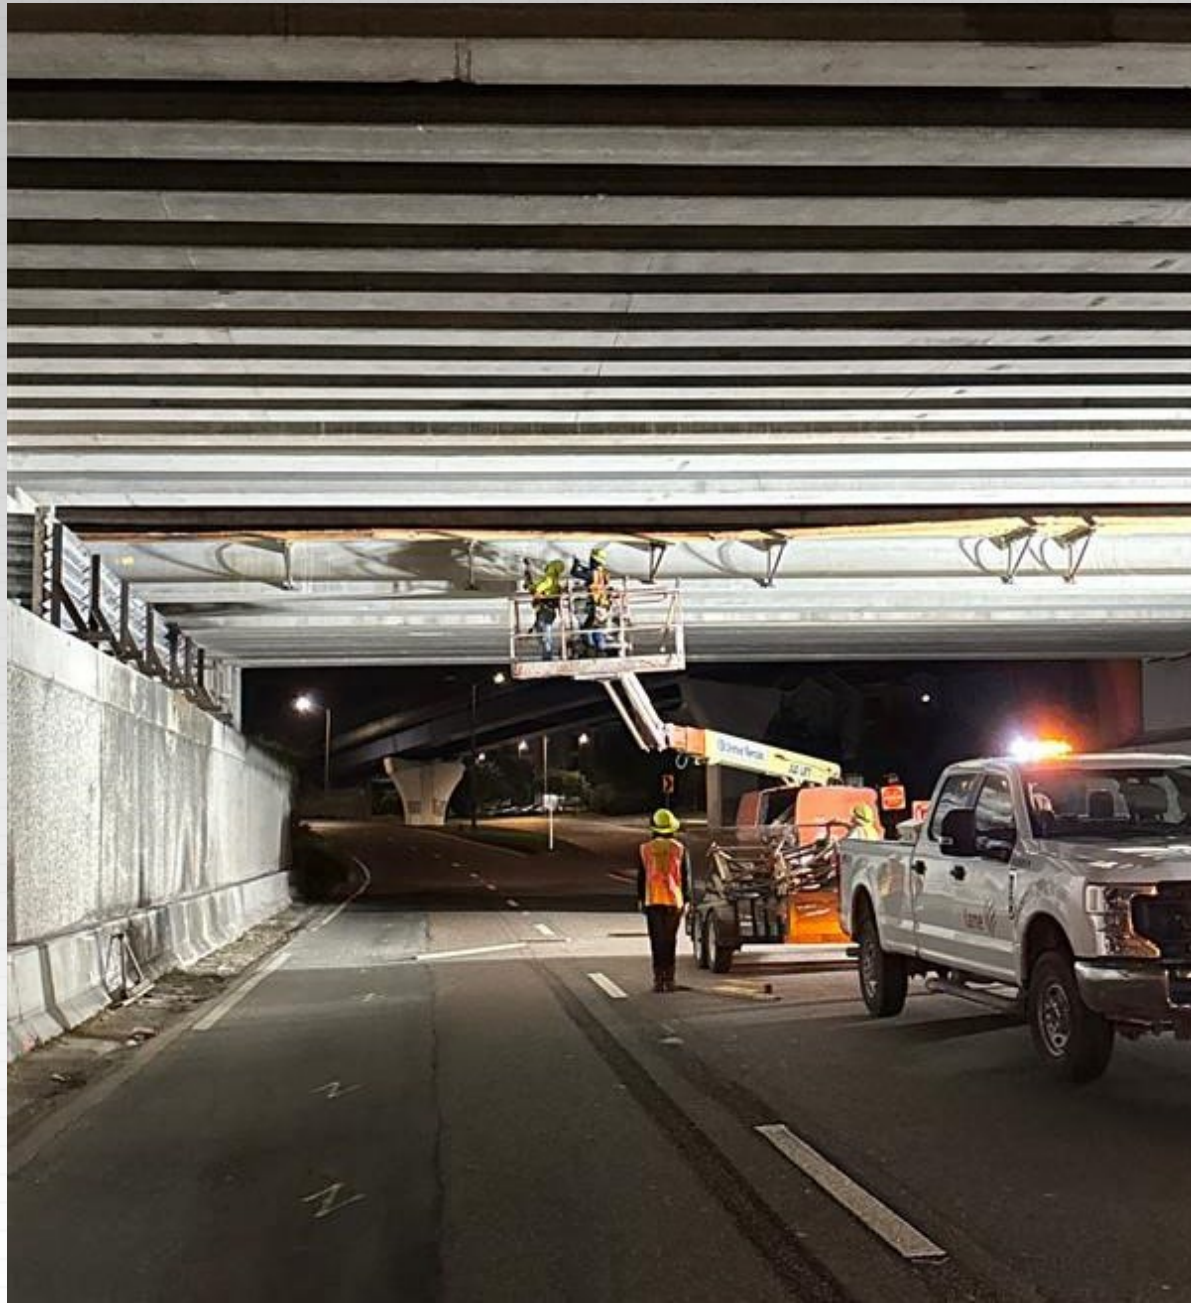



Agenda — Future Project Status

- **Future Project Status — FDOT to review next 7 days**
 - Bridge pile driving at Sand Lake Road (Area 6)
 - Sand Lake Road pile deliveries (Area 6)
 - Eastbound I-4 entrance ramp shift (Area 5)
 - Force main installation and testing (Area 3)
 - Turkey Lake Road outside grading and widening
 - Place and compact limerock (Area 8)
 - Embankment material placement (Area 6)
 - Median barrier wall installation (Area 8)
 - Signal and sign structure installation
 - Excavate and grade ponds
 - Utility relocation
 - Drainage installation (Areas 1, 2, and 3)
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Future Project Status

- **Future Project Status — FDOT to review next 14 – 21 days**
 - Miscellaneous bridge demolition work and pile driving at Sand Lake Road (Area 6)
 - Sand Lake Road pile deliveries (Area 6)
 - Force main installation and testing (Area 3)
 - Embankment material placement (Area 6)
 - Paving (Area 6)
 - Place and compact limerock (Area 8)
 - Median barrier wall grading (Area 8)
 - Turkey Lake Road outside grading and widening
 - Excavate and grade ponds
 - Sign and signal structure installation
 - Drainage installation (Areas 1, 2, and 3)
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Cleanliness Review

- **Cleanliness Review**
 - Committee's observations over past 7 days
- **Condition Review**
 - Committee's observations over past 7 days
(fencing, wraps, barricades, temporary signage)




Agenda — Old Business

- **Public Input or Comments**
- **Commitments Update**
 - Fencing and screening
 - Mowing and cleaning
 - Clean Team
 - Express lanes signage/access
 - Hardscaping and aesthetics
 - Ponds



Safety Diversions

- **June 18 (overnight)**
 - Eastbound I-4 entrance ramp from Sand Lake Road for a ramp shift
 - 10 p.m. to 6 a.m.

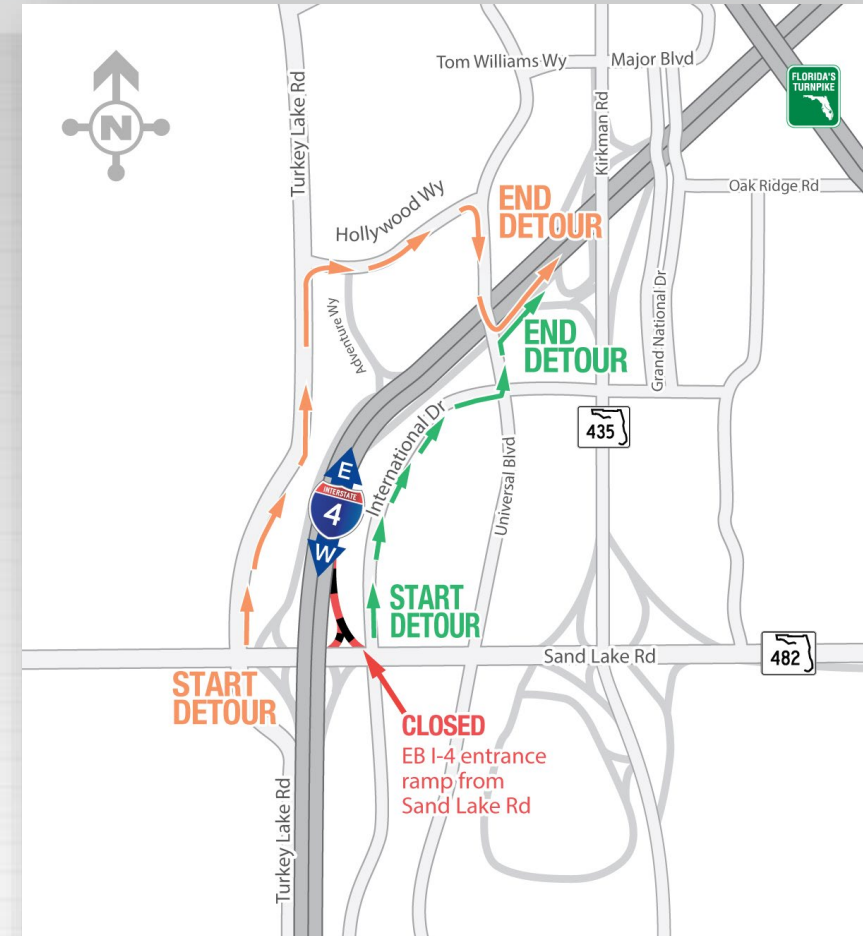



Agenda — New Business

Next meeting: 06/17/2026
