



I-4 and Sand Lake Road Interchange Design-Build

06/24/2026

I4Beyond.com



Status as of June 22, 2026


Days Used	Total Days	% Days Complete	Last Contract Day
1,177	1,779	67.0%	2/14/2028

Sand Lake 3470				Current Week								Week 1								Week 2							
Activity ID	Activity Description	Foreman / Sub	Supt	22-Jun	23-Jun	24-Jun	25-Jun	26-Jun	27-Jun	28-Jun	29-Jun	30-Jun	1-Jul	2-Jul	3-Jul	4-Jul	5-Jul	6-Jul	7-Jul	8-Jul	9-Jul	10-Jul	11-Jul	12-Jul			
				MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN			
	Roadway																										
MSE320	Exc/Grade Wall 4-2	Marcos C.	Tyler	X	X	X	X	X			X	X	X	X				X	X	X	X	X					
	Sand Lake Rd. Widening (North)	Marcos C.	Tyler	X	X	X	X	X			X	X	X	X													
	Sand Lake Rd. Widening (South)	Marcos C.	Tyler															X	X	X	X	X					
	Place Embankment Ramp L	Marcos C.	Tyler								X	X	X	X				X	X	X	X	X					
BASE370/390	WB XL Plc/Fin Limerock 5238 - 5252	Jessie W	Tyler	X	X																						
EW570	Ph. 2C - EB Widening 1440 - 1450	Jessie W	Tyler			X	X	X			X	X	X	X													
STAB390	Ph. 2C - EB/Ramp K - Mix/Plc/Fin stab (7189 - 7210)	Jessie W	Tyler				X	X	X																		
BASE450	Ph. 2C - EB/Ramp K - Plc/Fin Lime Rock (7189 - 7210)	Jessie W	Tyler								X	X	X	X				X	X	X	X	X					
	EB XL - Mix/Plc/Fin stab (6252 - 6262)	Jessie W	Tyler	LBR	LBR	LBR																					
STAB300	I4 WB Tube - Balance/Mix 1355 - 1335 (bridge 7)	Ian Palasz	Tyler	LBR	LBR	X	X	X	X																		
BASE360	I4 WB Tube - Plc/Fin Lime Rock 1355 - 1335 (bridge 7)	Ian Palasz	Tyler								X	X	X	X													
	FG WB Tube Ditch	Ian Palasz	Tyler	X	X																						
BASE450	Finish Lime Rock - Sand Lake Rd. Widening (North)	Ian Palasz	Tyler															X	X	X	X	X					
	Mowing and Litter Pick Up	Billy Worles	Greg L	X	X	X	X	X			X	X	X	X				X	X	X	X	X					
	Clean Team Sand Lake Sidewalks, Trash pickup and Mowing	Billy Worles	Greg L	X	X	X	X	X			X	X	X	X				X	X	X	X	X					
	Sand Lake off and on ramps to I-4 - Trash pickup and Mowing	Billy Worles	Greg L																								
	Turkey Lake Sidewalks, Trash pickup and Mowing	Billy Worles	Greg L																								
	Kirkman ramp - Trash pickup and Mowing	Billy Worles	Greg L	X	X	X																					
	Remove existing Curb Turkey Lake	Michael Bloomfield	Jose Castro	X	X	X	X	X			X	X	X	X				X	X	X	X	X					
	Place Grade Limerock on Turkey Lake for Curb and Gutter	Michael Bloomfield	Jose Castro	X	X	X	X	X			X	X	X	X				X	X	X	X	X					
	Drainage / Utilities																										
	Pipe video pond 206	Isaias Barcenas	Greg L	X																							
DRG1380	Install S-709 to S-715 (24")	Isaias Barcenas	Greg L	X																							
DRG1390	Install S-715 to S-716 (30")	Isaias Barcenas	Greg L		X	X	X	X	X		X	X															
DRG1390	installS-716 to S-717 (30')	Isaias Barcenas	Greg L										X	X				X	X	X	X	X	X				
DRG300	Install S-84 to S-83 (29"X45")	Victor Castro	Greg L	X	X																						
DRG300	Install S-422B To S-422A (24")	Victor Castro	Greg L			X	X																				
DRG300	Install S-422A To S-422OF (24")	Victor Castro	Greg L					X			X																
	Install S-517 To S-521 (18")	Victor Castro	Greg L								X	X	X	X													
	Install S-522 To S-524 (18")	Victor Castro	Greg L															X	X	X							
	Install S-350 to S-350OF (18")	Victor Castro	Greg L																		X	X	X				
	Install S-717 To0 S-722 (30")	Dakota Mooney	Greg L	X	X	X	X	X	X		X																
	Install S-721 To S-722 (30")	Dakota Mooney	Greg L									X	X	X													
U-OCU1540	Install FM Sand Lake ramp M to cross TL	Edward Benitez	Greg L	X	X	X	X			N	N	N	N	N			N	N	N	N	N			N			
	Structures																										
	Bridge #4																										
PILE270	drive endbent 2 pile	Juan Pinero	James O'Neill	X	X	X	X	X	X																		
	cut Pile	Eusebio Perez	Jose Perez	x	N																						
SUBS260	dewater & F/G footer	Eusebio Perez	Jose Perez					x	x																		
CURE220	Form/pour/remove, footer pier 2	Eusebio Perez	Jose Perez	x	x	x	x	x			x	x	x														
	asemble cap forms for pier 2	Eusebio Perez	Jose Perez	x	x	x	x	x	x		x	x	x	x													
	form endbent 1	Jaime Castillo	Jose															x	x	x	x	x	x				
	form columns pier 2	Jaime Castillo	Jose Perez															x	x	x	x	x					
	Pylon Footing																										
SUBS200	install protection forms around pylon rebar	Jaime Castillo	Jose Perez		x																						

N/P - Night Pour	
X - Day Schedule	T-N - Tentative
NC - Night Time Confirmed	N - Night
TS-Traffic Shift	D-Pile Delivery

Sand Lake 3470				Current Week								Week 1								Week 2							
Activity ID	Activity Description	Foreman / Sub	Supt	22-Jun	23-Jun	24-Jun	25-Jun	26-Jun	27-Jun	28-Jun	29-Jun	30-Jun	1-Jul	2-Jul	3-Jul	4-Jul	5-Jul	6-Jul	7-Jul	8-Jul	9-Jul	10-Jul	11-Jul	12-Jul			
				MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN			
SUBS200	remove forms Pylon footer 4-1	Jaime Castillo	Jose Perez	x	x																						
	Subcontractor																										
FLAT160	Turkey Lake Curb and Gutter	JVD	Rainer								X	X	X	X													
BW300	Median Barrier EB 7195 - 7199	Blount Sanford	Harry			X	X	X			X	X	X	X				X	X	X	X	X					
BW290	Median Barrier Ramp K	Blount Sanford	Harry			X	X	X																			
	B4 footer pier 2 rebar	Shelby	Harry	x	x	x																					
	B4 column rebar	Shelby	Harry												N	N											
MSE310	RW 4-1	RWH	Nate	X	X	X	X	X			X	X	X	X				X	X	X	X	X					
	Barrier Wall Install South End of Project (Phase 1 Step 3)	TCP	Nate							N	N	N	N	N													
	Barrier Wall Install Area 4 TTCP's	TCP	Nate														N	N	N	N	N						
	WB Tube - 1339 - 1425	Unlimited Turf	Nate				X	X																			
	Shift Traffic Area 4 TTCP's	McShea													N	N											
DRG310	Install 30" J&B S-55 - S404OF (Tube Area 3)	CFU	Greg	X	X	X	X	X																			
DRG310	Install 30" J&B S-56 - S422A (Tube Area 3)	CFU	Greg								X	X	X	X													
DRG310	Install 36" J&B S-71 - S83 (Tube Area 3)	CFU	Greg															X	X	X	X	X					
	Mill & Resurface WB Inside Shld Gul (1499+00 - 1509+00)	Hubbard																									
	WB Express lanes (1499+00 - 1509+00)	Hubbard								N	N	N															
PAVE440	Ramp K paving	Hubbard																N	N	N	N						
	APS Pipe Videos	APS			X																						
	Lighting																										
LGHT110	Lighting Load Center C (Ramp J) Conduit	Conti	Rainer	X	X	X	X	X																			
	Service Conduit Lighting Load Center C (Ramp J)	Conti/Vasi	Rainer	X	X	X	X	X																			
	ITS																										
ITS100	ITS Load Center B (Ramp K)	Conti	Rainer	X	X	X	X	X			X	X	X	X				X	X	X	X	X					
	Toll Plaza																										
TOLL110	Load Center	Conti	Rainer	X	X	X	X	X			X	X	X	X													
TOLL140	Set Building	Conti	Rainer								N	N															
	Sand Lake Road Closures / Sidewalk																										
	Sand Lake Rd & Ramps																										
	Sand Lake WB Contra flow (Bridge Work)	James	Dennis	N	N	N	N			N	N	N	N	N				N	N	N	N						
	Sand Lake EB Contra flow (Bridge Work)	James	Dennis	N	N	N	N			N	N	N	N	N				N	N	N	N						
	Sand Lake Rd EB Single Lane Inside (Forcemain)	Lane	Dennis	N	N	N	N			N	N	N	N					N	N	N	N						
	Sand Lake Rd WB Single Lane Inside (Forcemain)	Lane	Dennis	N	N	N	N			N	N	N	N					N	N	N	N						
	Turkey Lake & Sandlake Rd Intersection (Detour 12.1A)	Lane	Dennis															N	N	N	N			N			
	Turkey Lake & Sandlake Rd Intersection (Detour 12.1B)	Lane	Dennis								N	N	N					N	N								
	Turkey Lake & Sandlake Rd Intersection (Detour 12.)	Lane	Dennis															N	N	N	N						
	I-4 EB																										
	I-4 Single Lane Closures EB	Lane	Dennis	N	N	N	N			N	N	N	N	N				N	N	N	N						
	I-4 WB																										
	I-4 Single Lane Closures WB	Lane	Dennis	N	N	N	N			N	N	N	N	N				N	N	N	N						

N/P - Night Pour	
X - Day Schedule	T-N - Tentative
NC - Night Time Confirmed	N - Night
TS-Traffic Shift	D-Pile Delivery

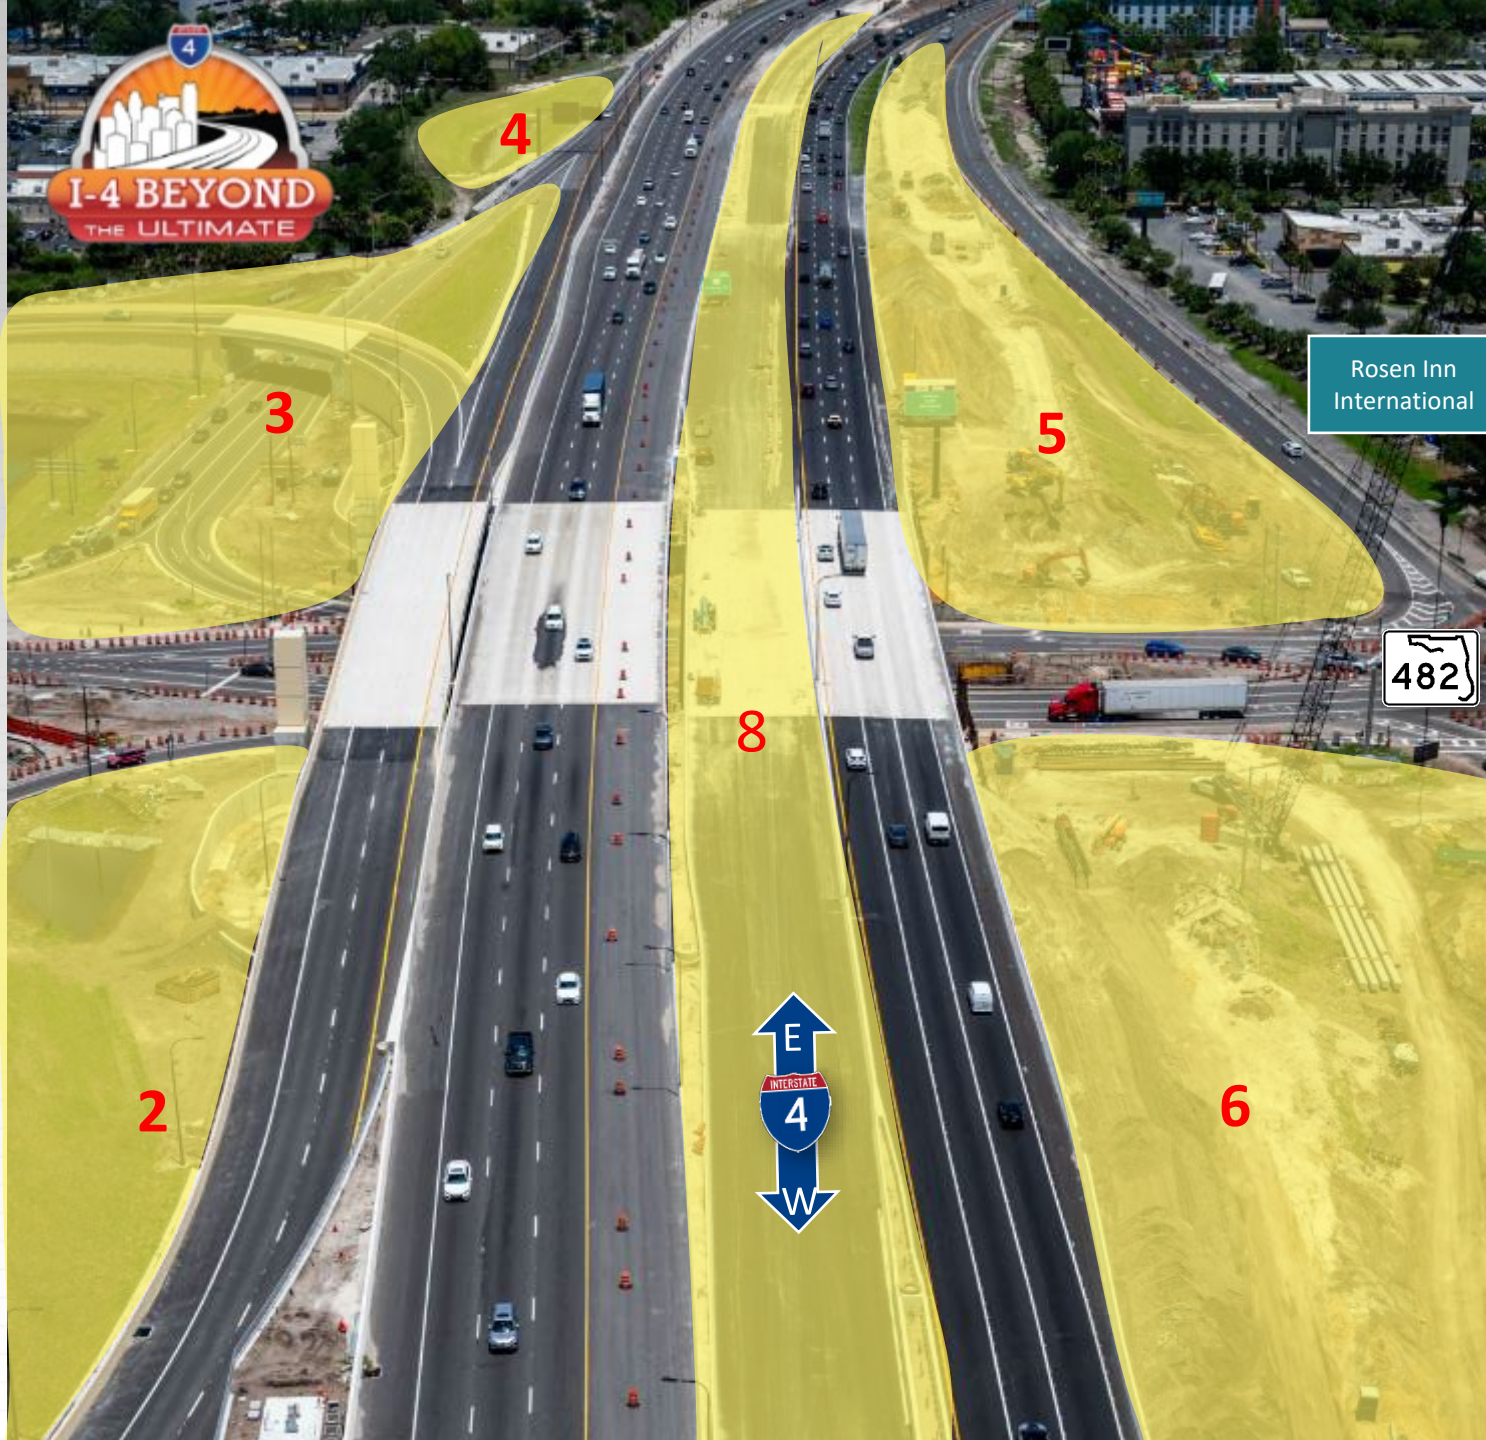





Agenda — Current Project Status

- **Past Project Status — FDOT to review past 7 days**

- Bridge pile driving and bridge work at Sand Lake Road (Area 6)
- Eastbound I-4 entrance ramp shift (Area 5)
- Force main installation and testing (Area 3)
- I-4 median paving (Area 8)
- Turkey Lake Road outside grading and widening
- Place and compact lime rock (Area 8)
- Embankment material placement (Area 6)
- Barrier wall installation (Areas 4 and 8)
- Signal and sign structure installation
- Excavate and grade ponds
- Utility relocation
- Drainage installation (Areas 1, 2, and 3)
- Ongoing mowing and litter pickup

- **Committee's Comments & Suggestions**

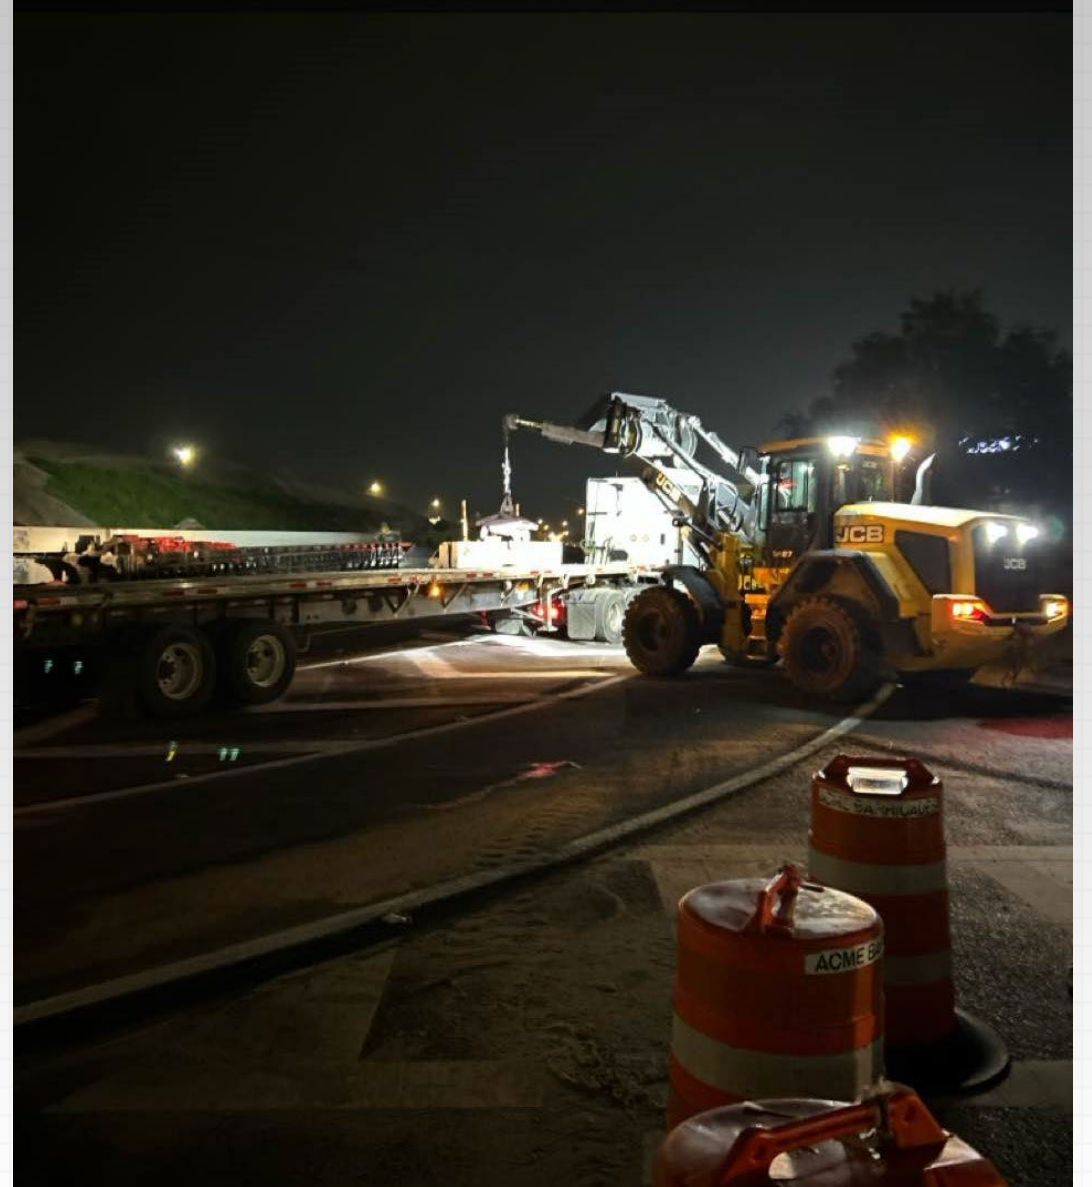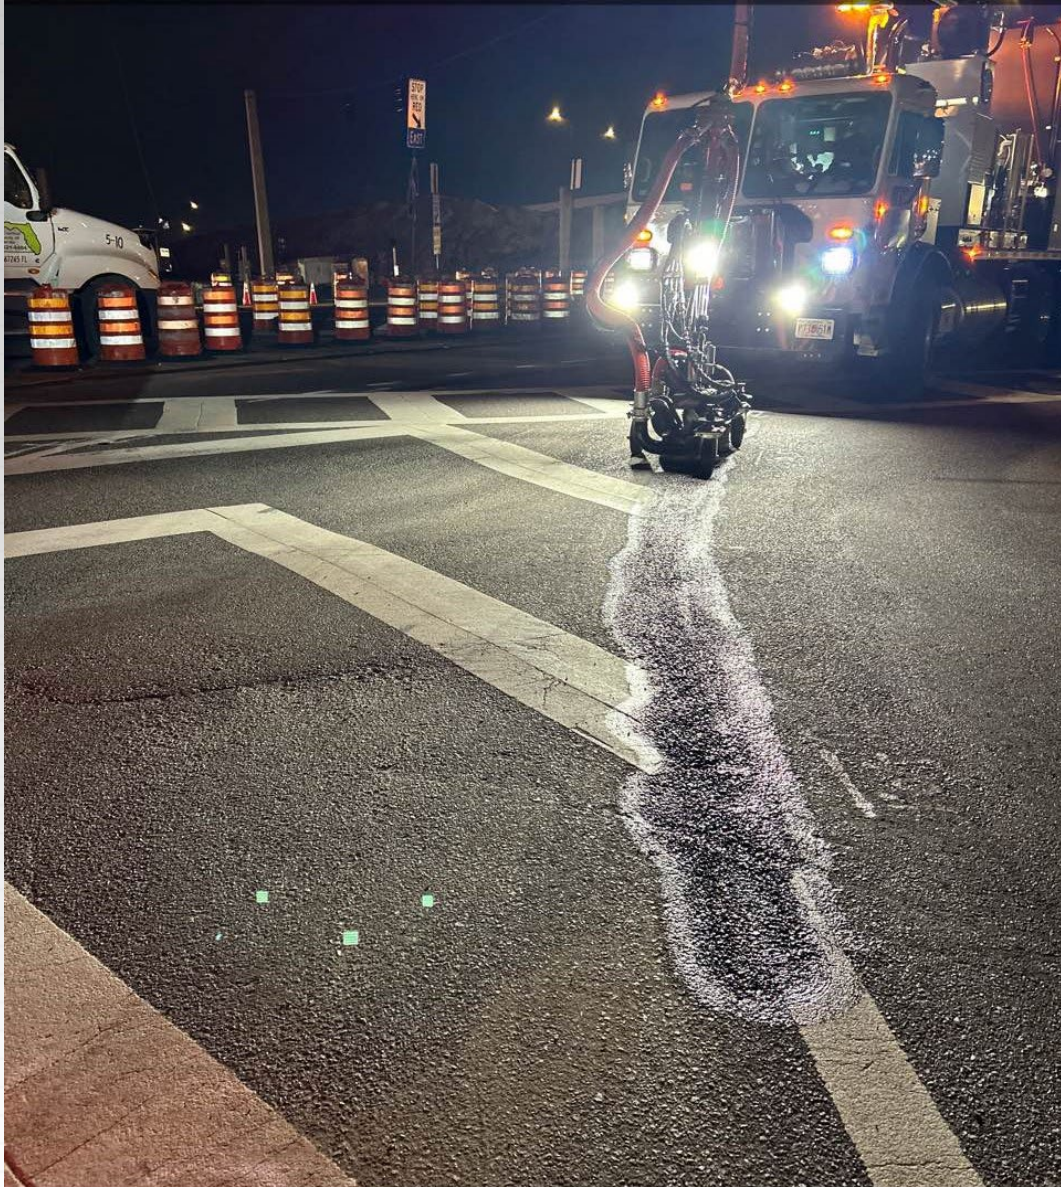









Agenda — Future Project Status

- **Future Project Status — FDOT to review next 7 days**
 - Bridge pile driving at Sand Lake Road (Area 6)
 - Force main installation crossing Sand Lake Road/Turkey Lake Road
 - Turkey Lake Road outside grading and widening
 - Place and compact lime rock (Area 8)
 - Embankment material placement (Area 6)
 - Barrier wall installation (Areas 4 and 8)
 - Signal and sign structure installation
 - Excavate and grade ponds
 - Utility relocation
 - Drainage installation (Areas 1, 2, and 3)
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Future Project Status

- **Future Project Status — FDOT to review next 14 – 21 days**
 - Miscellaneous bridge work at Sand Lake Road (Area 6)
 - Force main installation crossing Sand Lake Road/Turkey Lake Road
 - Embankment material placement (Area 6)
 - Paving (Area 6)
 - Place and compact lime rock (Area 8)
 - Barrier wall installation (Areas 4 and 8)
 - Turkey Lake Road outside grading and widening
 - Excavate and grade ponds
 - Sign and signal structure installation
 - Drainage installation (Areas 1, 2, and 3)
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Cleanliness Review

- **Cleanliness Review**
 - Committee's observations over past 7 days
- **Condition Review**
 - Committee's observations over past 7 days
(fencing, wraps, barricades, temporary signage)



Agenda — Old Business

- **Public Input or Comments**
- **Commitments Update**
 - Fencing and screening
 - Mowing and cleaning
 - Clean Team
 - Express lanes signage/access
 - Hardscaping and aesthetics
 - Ponds



Agenda — New Business

Next meeting: 07/08/2026
