



I-4 and Sand Lake Road Interchange Design-Build

08/19/2026

I4Beyond.com



Status as of August 17, 2026

Days Used	Total Days	% Days Complete	Last Contract Day
1,233	1,784	69.1%	2/19/2028

D-Pile Delivery				Current Week										Week 1				Halloween Horror Nights				Week 2					
Sand Lake SWN				17-Aug	18-Aug	19-Aug	20-Aug	21-Aug	22-Aug	23-Aug	24-Aug	25-Aug	26-Aug	27-Aug	28-Aug	29-Aug	30-Aug	31-Aug	1-Sep	2-Sep	3-Sep	4-Sep	5-Sep	6-Sep			
Activity ID	Activity Description	Foreman / Sub	Sign	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN			
Roadway																											
1W730	PG Curb/Sidewalk Ramp L to McDonalds	Marcel C.	Tyler								X	X	X	X	X			X	X	X	X	X					
1W100	Place Embankment - Area 4 - 6060 - 4264	Marcel C.	Tyler	X	X	X	X	X				X	X	X	X	X											
MSK300	Exc/Grade Pond 266D	Marcel C.	Tyler															X	X	X	X	X					
	Exc/Grade Wall 4-2	Phillip A.	Tyler	X	X																						
CP150	PG Inlet - Mtn. site clean up	Phillip A.	Tyler			X	X	X			X	X	X	X	X	X											
	Reinst/Grk/Sidewalk Ramp PG-Turkey Lake	Phillip A.	Tyler			X	X	X			X	X	X	X	X	X											
	Exc/Grade Wall 101	Phillip A.	Tyler								X	X	X	X	X	X		X	X	X	X	X					
ST16000	EB/Ramp L - Mtn/Plc/Pin slab (7239 - 7204)	Jessie W.	Tyler																								
SV1430	EB/Ramp L - Plc/Pin Line Rock (7239 - 7204)	Jessie W.	Tyler	X	X																						
ST16480	EB XL - Mtn/Plc/Pin slab (6252 - 6262)	Jessie W.	Tyler			X	X											X	X	X	X	X					
SV12140	EB XL - Plc/Pin Line Rock (6252 - 6262)	Jessie W.	Tyler					X			X	X	X	X	X	X											
	PG WB Tube Offch	Ion Polanco	Tyler								X	X	X	X	X	X		X	X	X	X	X					
ST16200	Mtn/Plc/Pin base - Sand Lake Rd. Widening/Ramp L (North)	Ion Polanco	Tyler								X	X	X	X	X	X		X	X	X	X	X					
SV12360	14 WB Tube - Plc/Pin Line Rock (Bridge 7 - Daryl Carter)	Ion Polanco	Tyler	X	X	X	X	X	X		X	X	X	X	X	X		X	X	X	X	X					
	Kakemon ramp - Trash pickup and Mowing	BBJ Workes	Jesse Castro	X	X	X	X	X			X	X	X	X	X	X											
	Mowing	BBJ Workes	Tyler															X	X	X	X	X					
	Turkey Lake SB Widening	Michael Bloomfield	Jesse C./Tyler	X	X	X	X	X			X	X	X	X	X	X		X	X	X	X	X					
	Ramp E Traffic Setup																										
	Preliminary																										
	Pave Turb	Hubbard																									
	Protect/Strake 500 LP	TCF																									
	Protect/Ramp E	McShaw																									
	Permanent guardrail	ACME																									
	Permanent Crash Cushion	ACME																									
	Temp Drainage	Lane	Jesse C.																								
	Temp Bridge Signals	Good		N																							
	Temp Lighting	Good		N																							
	Pod Signal Adjustments	Good																									
	WWD																										
	Temp WWD Install Temp Borne and Threading Conduit	Good																									
	Temp WWD Set Temp Poles	Good																									
	Temp WWD Set Signs and Gowners Devices	Good																									
	WWD IP Addresses for Devices (Coordinate w/ RTHC)	Good																									
	Test WWD Gowners (Tuesday Night with Backup Night)	Good				N	N																				
	Night w/																										
	Relocate remaining Barrier	TCF		N																							
	Strip To Ins	McShaw		N																							
	Open Signal Adjustments	Good		N																							
	Pod Signal Adjustments	Good		N																							
	Temp Lighting Adjustments	Good																									
	Signage Adjustments	Lane		N																							
	Swap to Ph 2C - Ramp E			N																							
	Turkey Lake																										
	Widening (star/kaw)	Michael Bloomfield	Jesse C./Tyler	X	X	X	X	X																			
	PG/Pour Curb	Michael Bloomfield / JVD	Jesse C./Tyler								X	X	X	X	X			X	X								
	Exc/Grade Gravity Wall	Michael Bloomfield	Jesse C./Tyler																	X	X	X					
	Drainage / URB Line																										
DN1060	S-56 - 425 - 4 on the jack board pond 201	Isaias Barceas	Jesse Castro	X	X	X	X	X	X		X	X	X	X	X												
DN1060	INSTALL S-519-425 LP 25 FEET	Isaias Barceas	Jesse Castro								X	X	X	X	X												
DN1060	INSTALL S-520-425 LP 25 FEET ON TURKEY LAKE	Isaias Barceas	Jesse Castro															X	X	X	X						
Activity ID	Activity Description	Foreman / Sub	Sign	17-Aug	18-Aug	19-Aug	20-Aug	21-Aug	22-Aug	23-Aug	24-Aug	25-Aug	26-Aug	27-Aug	28-Aug	29-Aug	30-Aug	31-Aug	1-Sep	2-Sep	3-Sep	4-Sep	5-Sep	6-Sep			
				MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN			
DN1100	S-727 TO S-728 INSTALL 36 LP 360	Dakota Mooney	Jesse Castro	X	X	X	X	X			X	X	X	X	X	X											
DN1100	S-728-EX-4 EXTING AND REMOVE PIPE	Dakota Mooney	Jesse Castro																X	X	X	X	X				
U-OCU1510	Install force main on sand lake and turkey lake 24"	Edward Sanchez	Jesse Castro								X	X	X	X					X	X	X	X	X				
U-OCU1590	PM N 5L @ McDonald's cleaning on sand lake and lake	Edward Sanchez	Jesse Castro															X	X	X	X	X					
U-OCU1590	Flush/Pressure Test PM	Edward Sanchez	Jesse Castro	N	N	N	N																				
Structures																											
Autopile 101																											
	remove sidewalk 2	Cristian Flores	Jesse Perez			X	X																				
	remove sidewalk back wall 3	Cristian Flores	Jesse Perez	N																							
SL10750	remove forms cap pier 2	Guadalupe Perez	Jesse Perez	X	X	X	X																				

N/P - Night Pour

X - Day Schedule

NC - Night Time Confirmed

TS-Traffic Shift

T-N - Tentative

N - Night

D-Pile Delivery

N/P - Night Pour	
X - Day Schedule	T-N - Tentative
NC - Night Time Confirmed	N - Night
TS-Traffic Shift	D-Pile Delivery





Agenda — Current Project Status

- **Past Project Status — FDOT to review past 7 days**
 - Eastbound I-4 exit ramp paving and barrier wall work (Area 6)
 - Eastbound I-4 exit ramp traffic shift (Area 6)
 - Bridge support structure work at Sand Lake Road (Areas 5 and 6)
 - Force main installation west of Sand Lake Road/Turkey Lake Road
 - Turkey Lake Road curb/sidewalk widening
 - Place and compact lime rock (Area 8)
 - Embankment material placement (Areas 5 and 6)
 - Barrier wall installation (Areas 4, 6, and 8)
 - Excavate and grade ponds
 - Utility relocation
 - Drainage installation (Areas 5 and 6)
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



New EB I-4 Exit Ramp to Sand Lake Road





EB I-4 Exit Ramp to Sand Lake Road Paving





Toll Equipment Building





Setting Bridge Column & Cap Forms






Setting Bridge Column & Cap Forms





Force Main Work Along Sand Lake Road

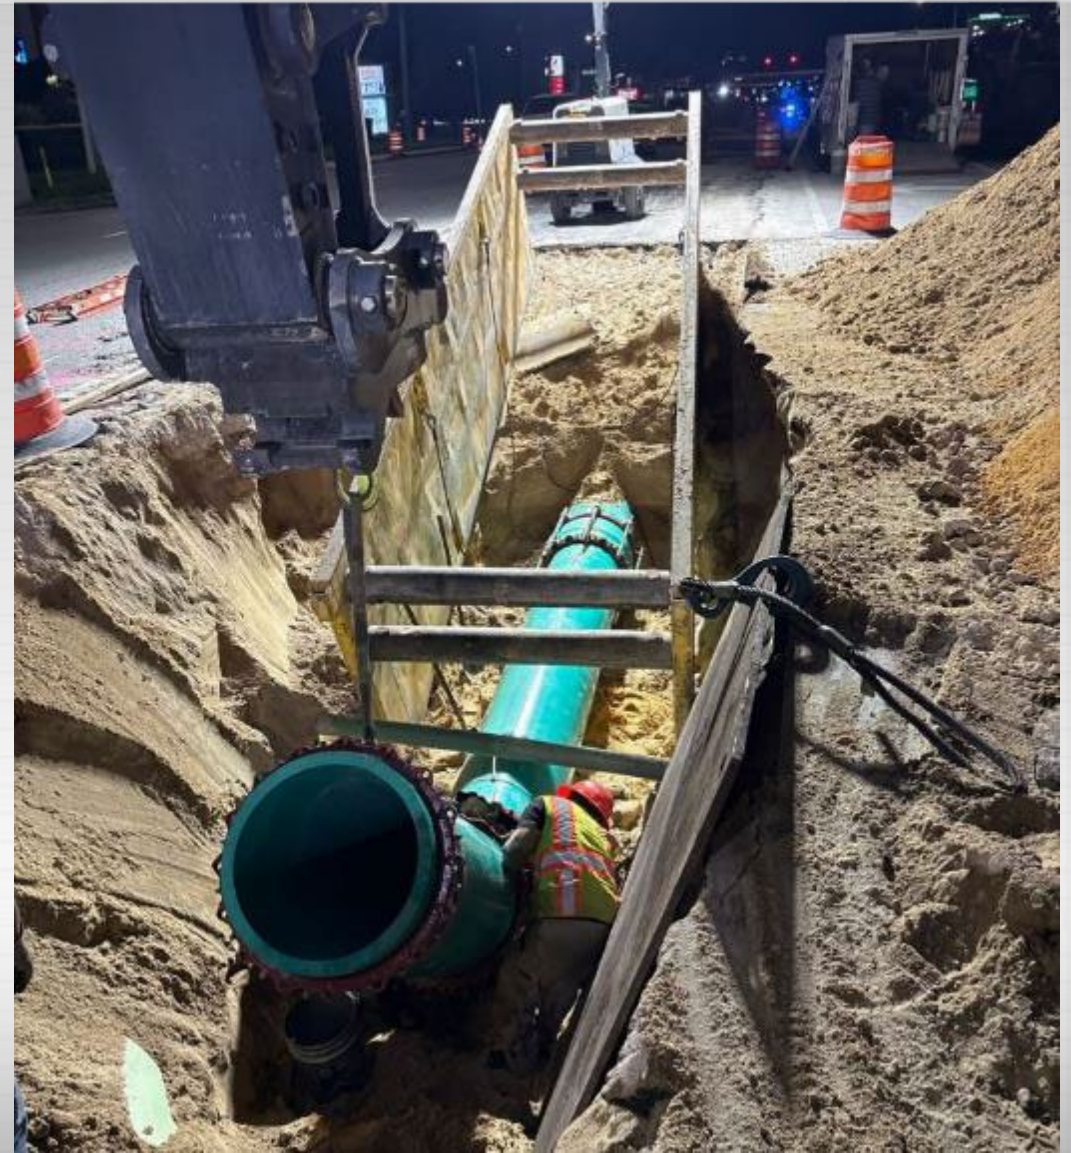



Agenda — Future Project Status

- **Future Project Status — FDOT to review next 7 days**
 - Bridge beam setting over Sand Lake Road (Areas 5 and 6)
 - Force main testing west of Sand Lake Road/Turkey Lake Road
 - Turkey Lake Road curb/sidewalk widening
 - Place and compact lime rock (Area 8)
 - Embankment material placement (Areas 5 and 6)
 - Barrier wall installation (Areas 4, 6, and 8)
 - Signal and sign structure installation
 - Excavate and grade ponds
 - Drainage installation (Areas 5 and 6)
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Future Project Status

- **Future Project Status — FDOT to review next 14 – 21 days**
 - Bridge beam setting over Sand Lake Road (Areas 5 and 6)
 - Force main testing west of Sand Lake Road/Turkey Lake Road
 - Turkey Lake Road curb/sidewalk widening
 - Place and compact lime rock (Areas 5, 6, and 8)
 - Embankment material placement (Areas 5 and 6)
 - Barrier wall installation (Areas 4, 6, and 8)
 - Signal and sign structure installation
 - Excavate and grade ponds
 - Drainage installation (Areas 5 and 6)
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Cleanliness Review

- **Cleanliness Review**
 - Committee's observations over past 7 days
- **Condition Review**
 - Committee's observations over past 7 days
(fencing, wraps, barricades, temporary signage)




Agenda — Old Business

- **Public Input or Comments**
- **Commitments Update**
 - Fencing and screening
 - Mowing and cleaning
 - Clean Team
 - Express lanes signage/access
 - Hardscaping and aesthetics
 - Ponds



Safety Diversions


- **August 16–20 (overnight)**
 - Eastbound I-4 exit ramp to Sand Lake Road
 - Barrier wall installation and ramp shift
 - 10 p.m. to 6 a.m.

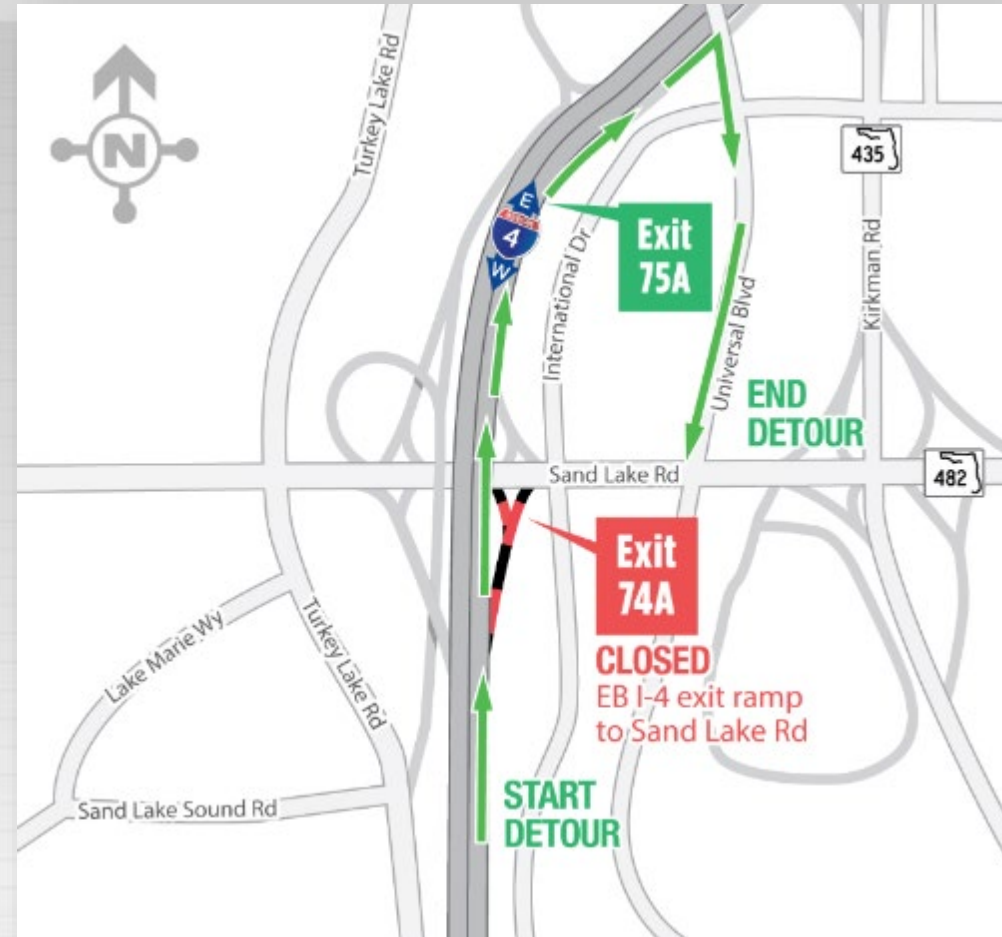



Safety Diversions

- August 23–25, 31 and September 1 (overnight)
 - Full diversion of Sand Lake Road under I-4
 - Bridge beam setting for the reconstruction of eastbound I-4
 - 11:30 p.m. to 6:30 a.m.

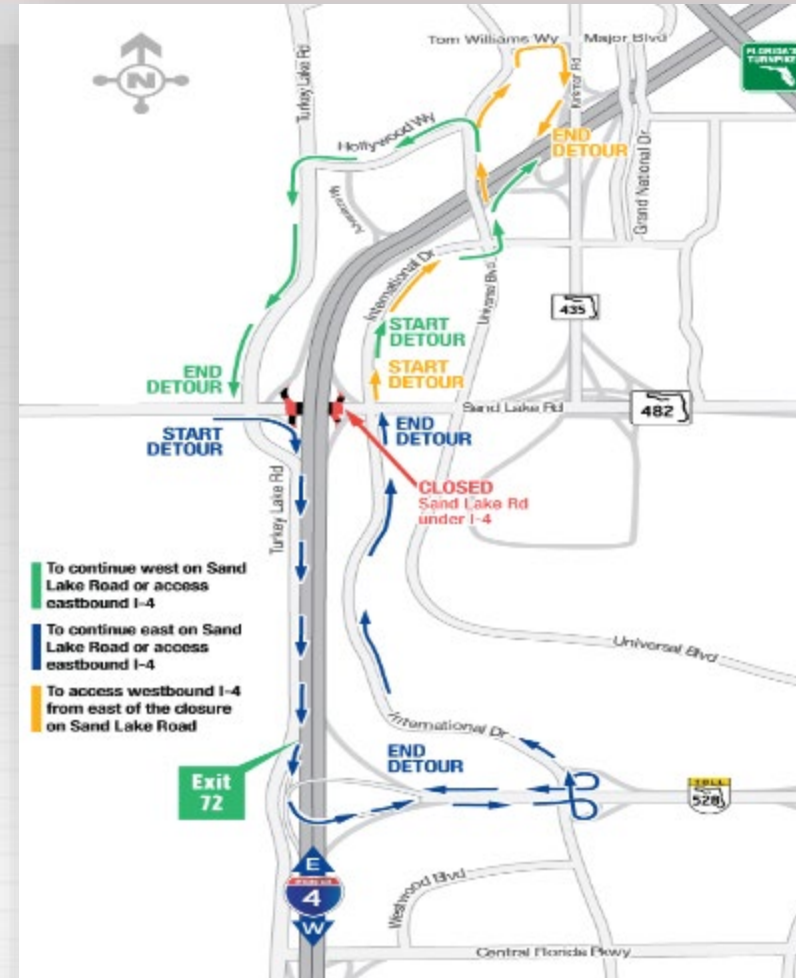



Agenda — New Business

Next meeting: 08/26/2026
