



I-4 and Sand Lake Road Interchange Design-Build

08/26/2026

I4Beyond.com



Status as of August 24, 2026

Days Used	Total Days	% Days Complete	Last Contract Day
1,240	1,784	69.5%	2/19/2028

D-Pile Delivery				Halloween Horror Nights							Halloween Horror Nights							Halloween Horror Nights						
Sand Lake 3470				Current Week							Week 1							Week 2						
Activity ID	Activity Description	Foreman / Sub	Supt	24-Aug	25-Aug	26-Aug	27-Aug	28-Aug	29-Aug	30-Aug	31-Aug	1-Sep	2-Sep	3-Sep	4-Sep	5-Sep	6-Sep	7-Sep	8-Sep	9-Sep	10-Sep	11-Sep	12-Sep	13-Sep
				MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN
	Roadway																							
EW720	Subsoil Excavation Area 4 - 5270+39	Marcos C.	Tyler				X	X	X															
EW720	Place Embankment - Area 4 - 6263 -6284	Marcos C.	Tyler	X	X	X	X	X																
EW600	Pothole/Locate utilities Pond 206D	Marcos C.	Tyler								X	X	X	X	X	X								
	Exc/Grade Pond 206D	Marcos C.	Tyler															X	X	X	X	X	X	
MSE300	Exc/Grade Wall 4-2	Phillip A.	Tyler								X	X	X	X	X									
	Base/Curb/Sidewalk Ramp M2-Turkey lake	Phillip A.	Tyler	X	X	X	X	X	X		X	X	X	X	X	X								
MSE330	Exc/Grade Wall 101	Phillip A.	Tyler															X	X	X	X	X	X	
STAB460	EB XL - Mix/Plc/Fin stab (6252 - 6262)	Jessie W	Tyler								X	X	X	X	X			X	X	X	X	X		
BASE560	EB XL - Plc/Fin Lime Rock (6252 - 6262)	Jessie W	Tyler	X	X	X	X	X																
	FG WB Tube Ditch	Ian Palasz	Tyler	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X		
STAB370	EB/Ramp L - Mix/Plc/Fin stab (7219 - 7234)	Ian Palasz	Tyler	X	X	X	X	X			X	X	X	X	X									
BASE420	EB/Ramp L - Plc/Fin Lime Rock (7219 - 7234)	Ian Palasz	Tyler	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X		
	Night Mot \ Erosion Deficiency Items	Dennis Scott	Tyler	N	N	N	N																	
	Kirkman ramp - Trash pickup and Mowing	Billy Worles	Jose Castro	X	X	X	X	X	X															
	Mowing	Billy Worles	Tyler								X	X	X	X	X	X		X	X	X	X	X	X	
	Turkey Lake SB Widening	Michael Bloomfield	Jose C./Tyler	N	N	N	N			N	N	N	N	N			N	N	N	N	N			N
	Turkey Lake																							
	FG/Pour Curb	Michael Bloomfield / JVD	Jose C./Tyler	X	X	X	X	X	X		X	X												
	Exc/Grade Gravity Wall	Michael Bloomfield	Jose C./Tyler										X	X	X	X								
CIP100/110	Install Gravity Wall	Francisco	Jose Perez															X	X	X	X	X		
	Drainage / Utilities																							
DRG210	INSTALL S-119-125 LF 25 FEET	Isaias Barcenias	Jose Castro	X	X	X	X	X																
DRG380	INSTALL S-120-121 LF 21 FEET ON TURKEY LAKE	Isaias Barcenias	Jose Castro							X	X	X	X	X	X	X								
DRG380	INTSALL S-120-121 LF 21 FEET	Isaias Barcenias	Jose Castro															X	X	X	X	X	X	
DRG1390	S-727 TO S-728 INSTALL 36' LF 380	Dakota Mooney	Jose Castro	X	X	X	X	X	X															
DRG1400	S-728-EX-9 EXITING AND REMOVE PIPE	Dakota Mooney	Jose Castro								X	X	X	X	X	X		X	X	X	X	X	X	
	Structures																							
	Bridge #4																							
	form bridge overhang span 1	Felipe Perez	Jose Perez															N	N	N				
	form bridge overhang span 2	Felipe Perez	Jose Perez			N	N																	
	install false decking over road	Felipe Perez	Jose Perez			N	N						N	N						N	N			
BEAM180	Set Fib 63	Eusebio Perez	James	N	N						N	N	N											
BEAM190	Set Fib 63	Felipe Perez	James	N	N						N	N	N											
	Bridge #7																							
AS190	Approach slab 2	Felipe Perez	Jose Perez	x	x	x																		
	Pylon																							
SUBS350	form Pylon 4-2	Cristian Flores	Jose Perez															x	x	x	x	x	x	
	Subcontractor																							
	DuraStress Bri 3 Span 2 Beam Delivery	DuraStress	Nate	N	N																			
	DuraStress Bri 3 Span 1 Beam Delivery	DuraStress	Nate								N-T	N-T							N-T					
BW370	Median Barrier (WB Toll Site)	Blount Sanford	Isabel								X	X	X	X	X						X	X		
BW380	Median Barrier - WB GUL, XL's, EB GUL (North)	Blount Sanford	Isabel	X	X	X	X	X																

N/P - Night Pour

X - Day Schedule

NC - Night Time Confirmed

TS-Traffic Shift

T-N - Tentative

N - Night

D-Pile Delivery

Activity ID	Activity Description	Foreman / Sub	Supt	24-Aug	25-Aug	26-Aug	27-Aug	28-Aug	29-Aug	30-Aug	31-Aug	1-Sep	2-Sep	3-Sep	4-Sep	5-Sep	6-Sep	7-Sep	8-Sep	9-Sep	10-Sep	11-Sep	12-Sep	13-Sep
				MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN
SUBS350	Pyton 4-2	Shelby	John	x	x	x	x																	
MSE320	RW 4-2	RWH	Nate	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X		
DRG2030	Install 30" J&B S-55 - S404OF (Tube Area 3) Sta: 1345	CFU	jose								X	X	X	X	X									
DRG2050	Install 36" J&B S-71 - S83 (Tube Area 3) Sta: 1385	CFU	Jose	x	x	x	x	x			X	X	X	X	X			X	X	X	X	X		
	APS ON THE NORTH SIDE DITCH BOLT INLETS	APS	JOSE	T	T	x	x	x																
	Mill & Resurface Sandlake Rd Turn Lanes to NB Turkey Lake Rd	Hubbard					N																	
PAVE390	Paving on WB Tube	Hubbard								N	N	N	N	N										
	Mill & Resurface WB Inside Shld Gul (1499+00 - 1509+00)	Hubbard																			N			
PAVE590	WB Express lanes (1499+00 - 1509+00)	Hubbard															N	N	N	N				
	Guardrail Removal (Sta 1336+00 to 1357+50) & Area	Acme																						
	Lighting																							
	Lighting Maintenance (North of SLR on I4)	Conti	Rainer	X	X	X																		
LGHT110	Lighting Load Center B (Ramp K)	Conti	Rainer								X	X	X	X	X			X	X	X	X	X		
LGHT110	Lighting Load Center C (Ramp J)	Conti	Rainer								X	X	X	X	X									
	Service Conduit Lighting Load Center C (Ramp J)	Conti/Vasi	Rainer	X	X	X	X	X																
	ITS																							
ITS100	ITS Load Center B (Ramp K)	Conti	Rainer															X	X	X	X	X		
ITS120	ITS Conduit I-4 EB Sta: 1433 - 1330	Conti/Vasi/KDI	Rainer	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X		
ITS140	ITS DMS Drill Shaft Installation: 72.6 EB DMS	Conti	Rainer								X	X												
ITS140	ITS Drill Shaft Installation: 71.6 WB	Conti	Rainer										X											
ITS140	ITS Drill Shaft Installation: 74.2 WB	Conti	Rainer											X										
	ITS Drill Shaft Installation: 74.6 EB	Conti	Rainer												X									
	Signals																							
	Signal Pole 8 (SLR)	Conti/Reliable	Rainer								X	X												
	Signal Pole 3 (SLR/TLR)	Conti/Reliable	Rainer															N	N					
	Signal Pole 2 (SLR/TLR)	Conti/Reliable	Rainer																	N	N			
	SPM																							
	Drill Shaft OC 3	Conti/Reliable	Rainer											X	X									
SIGN100	Drill Shaft OHS 14 RT	Conti/Reliable	Rainer										X											
	Toll Plaza																							
TOLL240	Loop Boxes Gantry	Conti	Rainer								X	X	X	X	X			X	X	X	X	X		
TOLL110	Load Center and Building Power	Conti	Rainer	X	X	X	X	X			X	X	X	X	X									
	Building Electrical	Conti	Rainer								X	X	X	X	X			X	X	X	X	X		
	Sand Lake Road Closures / Sidewalk																							
	Sand Lake Rd & Ramps																							
	Sand Lake WB Contra flow (Bridge Work)	James	Dennis			N	N						N	N						N	N			
	Sand Lake EB Contra flow (Bridge Work)	James	Dennis			N	N						N	N						N	N			
	Sand Lake EB Full Detour (Beam Placement)	James	Dennis	N	N						N	N						N	N					
	Sand Lake WB Full Detour (Beam Placement)	James	Dennis	N	N						N	N						N	N					
	Sand Lake Rd EB Single Lane	Lane	Dennis	N	N	N	N				N	N						N	N					
	Sand Lake Rd WB Single Lane	Lane	Dennis	N	N	N	N				N	N						N	N					
	Full Closure of Ramp K	Lane	Dennis	N																				
	Single Lane Closure of Ramp K	Lane	Dennis	N	N	N	N				N	N						N	N					
	Single Lane Closure of Ramp L	Lane	Dennis	N	N	N	N				N	N						N	N					
	Single Lane Closure of Ramp J	Lane	Dennis	N	N	N	N				N	N						N	N					
	Single Lane Closure of Ramp M	Lane	Dennis	N	N	N	N				N	N						N	N					
	Turkey Lake Rd South (Single Outside Lanes)	Lane	Dennis	N	N	N	N			N	N	N	N	N			N	N	N	N	N			
	I-4 EB																							
	I-4 Single Lane Closures EB	Lane	Dennis	N	N	N	N				N	N						N	N					
	I-4 WB																							
	I-4 Single Lane Closures WB	Lane	Dennis	N	N	N	N			N	N	N	N	N			N	N	N	N	N			

N/P - Night Pour	
X - Day Schedule	T-N - Tentative
NC - Night Time Confirmed	N - Night
TS-Traffic Shift	D-Pile Delivery





Agenda — Current Project Status

- **Past Project Status — FDOT to review past 7 days**
 - Bridge beam setting over Sand Lake Road (Areas 5 and 6)
 - Eastbound I-4 exit ramp barrier wall placement (Area 6)
 - Turkey Lake Road curb/sidewalk widening
 - Place and compact lime rock (Areas 5, 6, and 8)
 - Embankment material placement (Areas 5 and 6)
 - Barrier wall installation (Areas 4, 6, and 8)
 - Excavate and grade ponds
 - Utility relocation
 - Drainage installation (Areas 5 and 6)
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



EB I-4 Bridge Span 2 Beam Setting Over Eastbound Sand Lake Road





Asphalt Removal on Original EB I-4 Exit Ramp to Sand Lake Road





I-4 Median Barrier Wall Placement





EB I-4 Bridge End Bent Cap Pour





Agenda — Future Project Status

- **Future Project Status — FDOT to review next 7 days**
 - Bridge beam setting over Sand Lake Road (Areas 5 and 6)
 - Paving (Area 8)
 - Turkey Lake Road curb/sidewalk widening
 - Place and compact lime rock (Areas 5, 6, and 8)
 - Embankment material placement (Areas 5 and 6)
 - Barrier wall installation (Areas 4, 6, and 8)
 - Signal and sign structure installation
 - Excavate and grade ponds
 - Drainage installation (Areas 5 and 6)
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Future Project Status

- **Future Project Status — FDOT to review next 14 – 21 days**
 - Bridge support structure work over Sand Lake Road (Areas 5 and 6)
 - Paving (Area 8)
 - Turkey Lake Road curb/sidewalk widening
 - Place and compact lime rock (Areas 5, 6, and 8)
 - Embankment material placement (Areas 5 and 6)
 - Barrier wall installation (Areas 4, 6, and 8)
 - Signal and sign structure installation
 - Excavate and grade ponds
 - Drainage installation (Areas 5 and 6)
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Cleanliness Review

- **Cleanliness Review**
 - Committee's observations over past 7 days
- **Condition Review**
 - Committee's observations over past 7 days
(fencing, wraps, barricades, temporary signage)




Agenda — Old Business

- **Public Input or Comments**
- **Commitments Update**
 - Fencing and screening
 - Mowing and cleaning
 - Clean Team
 - Express lanes signage/access (in-progress)
 - Hardscaping and aesthetics
 - Ponds



Safety Diversions

- August 31 & September 1 (overnight)
 - Full diversion of Sand Lake Road under I-4
 - Bridge beam setting for the reconstruction of eastbound I-4
 - 11:30 p.m. to 6:30 a.m.

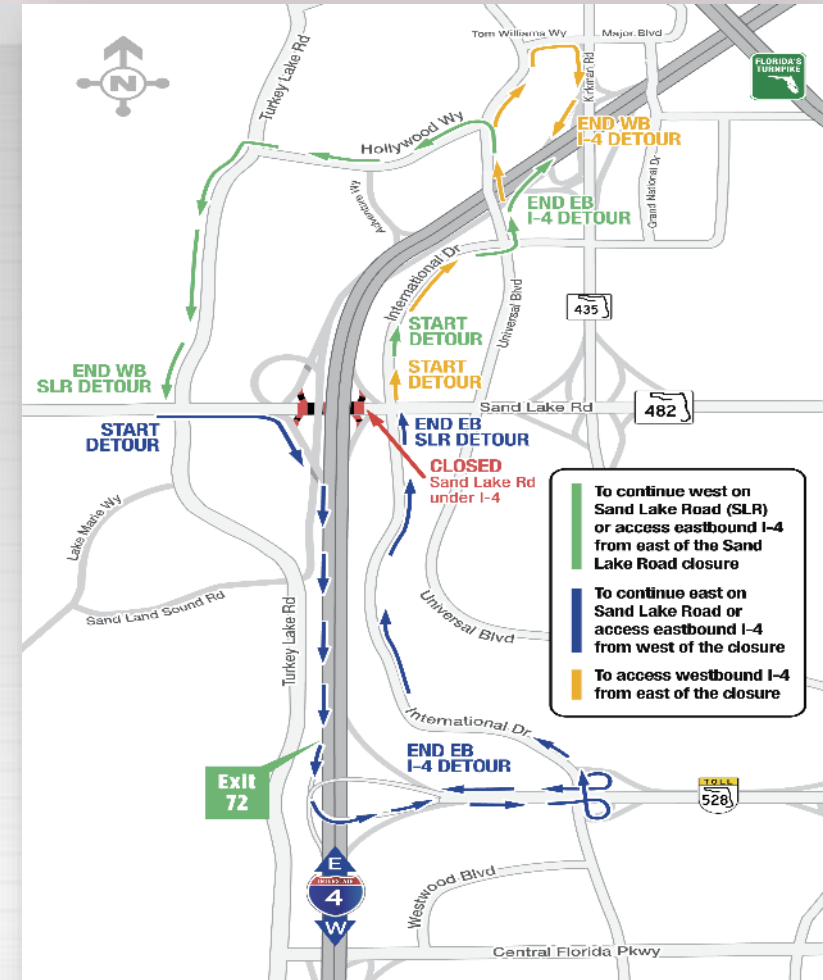



Agenda — New Business

Next meeting: 09/02/2026
