



I-4 and Sand Lake Road Interchange Design-Build

09/02/2026

I4Beyond.com



Status as of August 31, 2026

Days Used	Total Days	% Days Complete	Last Contract Day
1,247	1,784	69.9%	2/19/2028

D-Pile Delivery			Halloween Horror Nights														Halloween Horror Nights							Halloween Horror Nights						
Sand Lake 3470																														
Activity ID	Activity Description	Foreman / Sub	Supt	Current Week							Week 1							Week 2												
				31-Aug	1-Sep	2-Sep	3-Sep	4-Sep	5-Sep	6-Sep	7-Sep	8-Sep	9-Sep	10-Sep	11-Sep	12-Sep	13-Sep	14-Sep	15-Sep	16-Sep	17-Sep	18-Sep	19-Sep	20-Sep						
				MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN						
	Roadway																													
EW600	Base/Curb/Sidewalk Sand Lake Under Bridges	Marcos C.	Tyler	X	X	X	X	X				X	X	X	X															
	Exc/Grade Pond 206D	Marcos C.	Tyler									X	X	X	X	X		X	X	X	X	X								
MSE300	Exc/Grade Wall 4-2	Phillip A.	Tyler	X	X	X	X	X																						
	FG for Sod - Misc. site clean up	Phillip A.	Tyler																											
MSE330	Exc/Grade Wall 101	Phillip A.	Tyler									X	X	X	X	X		X	X	X	X	X								
EW580	Place Embankment Ramp K/EB I4 - 7189+78 -- 7200+00	Phillip A.	Tyler															X	X	X	X	X	X							
EW720	Place Embankment - Area 4 - 6263-6284	Jessie W	Tyler	X	X	X	X	X																						
STAB460	Balance/Mix - Area 4 - 6263-6284	Jessie W	Tyler									X	X	LBR	LBR			LBR	LBR	LBR										
EW580	Balance/Mix - EB I4 - 7207-Bridge 4	Jessie W	Tyler											X	X	X		LBR	LBR	LBR	LBR	LBR								
EW570	Balance/Mix - EB Widening - 1440-1454	Jessie W	Tyler															X	X	X	LBR	LBR								
BASE550	Plc/Fin Limerock - Area 4 - 6263-6284	Jessie W	Tyler																		X	X	X							
DRG1400	FG WB Tube Ditch	Ian Palasz	Tyler	X	X	X	X	X				X	X	X	X															
STAB300	EB/Ramp L - Mix/Plc/Fin stab (7219 - 7234)	Ian Palasz	Tyler	X	X	X	X	X																						
BASE360	EB/Ramp L - Plc/Fin Lime Rock (7219 - 7234)	Ian Palasz	Tyler	X	X	X	X	X				X	X	X	X			X	X	X	X	X								
	Mowing and Litter Pick Up	Billy Worles	Jose Castro	X	X	X	X	X				X	X	X	X	X		X	X	X	X	X	X							
	Clean Team Sand Lake Sidewalks, Trash pickup and Mowing	Billy Worles	Jose Castro	X	X	X						X	X					X	X	X										
	Sand Lake off and on ramps to I-4 - Trash pickup and Mowing	Billy Worles	Jose Castro				X	X						X	X						X	X								
	Base/Curb/Sidewalk Sand Lake (100-110)	Michael Bloomfield	Jose C./Tyler	N	N	N	N				N	N	N	N			N	N	N	N	N									
	Turkey Lake SB Widening	Michael Bloomfield	Jose C./Tyler														N													
	Turkey Lake																													
	FG/Pour Curb	Michael Bloomfield / JVD	Jose C./Tyler	X	X																									
CIP100/110	Exc/Grade Gravity Wall	Michael Bloomfield	Jose C./Tyler			X	X	X																						
CIP100/110	Install Gravity Wall	Francisco	Jose Perez									X	X	X	X			X	X	X	X	X								
	Drainage / Utilities																													
DRG380	INSTALL -233-A TO S-242-A INSTALL ADS 36' INCH 73"LF	Isaias Barcenas	Jose Castro	X																										
DRG380	INSTALL-242- 242-A INSTALL 235"LF OF 36INCH ADS	Isaias Barcenas	Jose Castro		X	X	X	X				X	X	X	X	X														
DRG380	INSTALL - S-240 TO S-242 DITCH BOLT INLET 30' DRAINAGE 194" LF	Isaias Barcenas	Jose Castro															X	X	X	X	X	X							
DRG1400	S-728-EX-9 EXITING AND REMOVE PIPE	Dakota Mooney	Jose Castro	X	X	X	X	X				X	X	X	X	X														
DRG1390	S-723-721 INSTALL DOG HOUSE TO 36' DRAINAGE	Dakota Mooney	Jose Castro															X	X	X	X	X	X							
	S-219 TO S-219 OF 15 FEE 18" ADS X	manny presiado	Jose Castro	X	X	X	X																							
	S-219-S-221 INSTALL 47" FEET 18" ADS	manny presiado	Jose Castro					X				X	X	X	X	X														
	INSTALL S-221-S-223 47 FEET 18" ADS	manny presiado	Jose Castro															X	X	X	X	X	X							
	Structures																													
	Bridge #4																													
	form bridge overhang span 1	Felipe Perez	Jose Perez								N	N	N																	
	form bridge overhang span 2	Felipe Perez	Jose Perez															N	N	N										
	install false decking over road	Felipe Perez	Jose Perez			N	N				N		N	N																
	form edge form	Felipe Perez	Jose Perez															x	x	x	x	x	x							
BEAM180/190	Set Fib 63	Eusebio Perez	James	N	N							N																		
BEAM180/190	Set Fib 63	Cristian Flores	James									N																		
BEAM180/190	Set Fib 63	Felipe Perez	James	N	N							N																		
	Pylon																													
	unload pylon rebar 4-2	Cristian Flores	Jose Perez																											
SUBS370	form Pylon 4-2	Cristian Flores	Jose Perez									x	x	x	x	x		x	x	x	x	x	x							
	Subcontractor																													
	Turkey Lake Curb and Gutter, Siderwalk	JVD	Isabel	N	N	N																								
	Sand Lake Curb/Sidewalk	JVD	Isabel								N	N	N					N	N	N										
BEAM180/190	DuraStress Bri 3 Span 1 Beam Delivery	DuraStress	Nate	N-T	N-T							N-T																		
BW370	Median Barrier (WB Toll Site)	Blount Sanford	Isabel	OUT	OUT	OUT	X	X				X	X	X	X															
BW380	Median Barrier - WB GUL, XL's, EB GUL (North)	Blount Sanford	Isabel									X	X																	

N/P - Night Pour	
X - Day Schedule	T-N - Tentative
NC - Night Time Confirmed	N - Night
TS-Traffic Shift	D-Pile Delivery

Activity ID	Activity Description	Foreman / Sub	Supt	31-Aug	1-Sep	2-Sep	3-Sep	4-Sep	5-Sep	6-Sep	7-Sep	8-Sep	9-Sep	10-Sep	11-Sep	12-Sep	13-Sep	14-Sep	15-Sep	16-Sep	17-Sep	18-Sep	19-Sep	20-Sep
				MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN
MSE330	Dig Out Level Pad RW 101	Marcos	Tyler	X	X	X	X	X																
MSE330	Pour Level Pad RW 101	RWH	Nate																					
MSE330	RW 101	RWH	Nate															X	X	X	X	X		
MSE320	RW 4-2	RWH	Nate															X	X	X	X	X		
	Phase 3 Express Lane Barrier Wall	TCP	Nate															N	N					
	Express Lane Phase 3 Shift	McShea	Nate															N	N					
DRG2030	Install 30" J&B S-55 - S4040F (Tube Area 3) Sta: 1345	CFU	jose	X	X	X	X	X																
DRG2050	Install 36" J&B S-71 - S83 (Tube Area 3) Sta: 1385	CFU	Jose															X	X	X	X	X		
	Mill & Resurface Sandlake Rd Turn Lanes to NB Turkey Lake Rd	Hubbard					N																	
PAVE390	Paving on WB Tube	Hubbard			N	N																		
	Mill & Resurface WB Inside Shld Gul (1499+00 - 1509+00)	Hubbard		N																				
	<i>Lighting</i>																							
	Lighting Maintenance (OHC 14)	Conti	Rainer										X	X										
LGHT110	Lighting Load Center B (Ramp K)	Conti	Rainer															X	X	X	X	X		
LGHT110	Lighting Load Center C (Ramp J)	Conti	Rainer																					
	Service Conduit Lighting Load Center C (Ramp J)	Conti/Vasi	Rainer																					
	<i>ITS</i>																							
	ITS Pull Boxes I-4 WB Sta: 1554 - 1479	Conti	Rainer	X	X	X	X	X				X	X	X	X	X		X	X	X	X	X		
	ITS Fiber I-4 WB Sta: 1554 - 1479 (1479 Backbone Splice)	Conti/PCS	Rainer																					
ITS100	ITS Load Center B (Ramp K)	Conti	Rainer										X	X	X	X		X	X	X	X	X		
ITS100	ITS Fiber I-4 WB Sta: 1554 - 1479	Conti/PCS	Rainer																					
ITS100	ITS Pole 73.6 WB-B Conduit	Conti	Rainer																					
ITS120	ITS Conduit I-4 EB Sta: 1433 - 1330	Conti/Vasi/KDI	Rainer															X	X	X	X	X		
ITS120	ITS Conduit I-4 EB Sta: 1433 - 1480	Conti/Vasi/KDI	Rainer																					
ITS100	ITS Conduit I-4 WB Sta: 1554 - 1479	Conti/Vasi/KDI	Rainer															X	X	X	X	X		
ITS140	ITS DMS Drill Shaft Installation: 72.6 EB DMS	Conti	Rainer															X	X					
ITS140	ITS Drill Shaft Installation: 71.6 WB	Conti	Rainer																	X				
ITS140	ITS Drill Shaft Installation: 74.2 WB	Conti	Rainer																					
	ITS Drill Shaft Installation: 74.6 EB	Conti	Rainer																		X			
	<i>Signals</i>																							
	DDI Signal Conduit	Conti/Vasi/KDI	Rainer	X	X	X	X	X				X	X	X	X	X		X	X	X	X	X		
	DDI Signal Cabinet	Conti	Rainer																					
	DDI Standalone Signals	Conti	Rainer																					
	DDI Peds East	Conti	Rainer															X	X	X	X	X		
	DDI Peds West	Conti	Rainer				X	X				X	X	X	X	X								
	DDI Service Wire and Load Center	Conti	Rainer																					
	Mast Arm Installations DDI	Conti	Rainer																					
	DDI in Final Config	Conti	Rainer																					
	Mast Arm Install SLS/TLR	Conti	Rainer																					
	Signal Pole 8 (SLR)	Conti/Reliable	Rainer											X	X									
	Signal Pole 3 (SLR/TLR)	Conti/Reliable	Rainer																N	N				
	Signal Pole 2 (SLR/TLR)	Conti/Reliable	Rainer															N						
	<i>SPM</i>																							
	Drill Shaft OC 14	Conti/Reliable	Rainer																					
	Drill Shaft OC 3	Conti/Reliable	Rainer																					
SIGN100	Drill Shaft OHS 14 RT	Conti/Reliable	Rainer										X	X										
SIGN100	Drill Shaft OHS 15 LT	Conti/Reliable	Rainer																					
	<i>Toll Plaza</i>																							
TOLL240	Loop Boxes Gantry	Conti	Rainer										X	X	X	X		X	X	X	X	X		
TOLL110	Load Center and Building Power	Conti	Rainer	X	X	X	X	X																
	Building Electrical	Conti	Rainer	X	X	X	X	X					X	X	X	X		X	X	X	X	X		
	Set WB Gantry	Conti	Rainer																					
	Building Flat Work	Conti/JVD	Rainer																					
	Sand Lake Officers Scheduled																							
	Place S if police are scheduled & # once total of officers confirmed		Nate																					
	Orange County		Nate																					
	FHP		Nate	N	N	N	N						N	N	N	N								
	Critical Protection Services		Nate	N	N	N	N						N	N	N	N								

N/P - Night Pour

X - Day Schedule

NC - Night Time Confirmed

TS-Traffic Shift

T-N - Tentative

N - Night

D-Pile Delivery

Activity ID	Activity Description	Foreman / Sub	Supt	31-Aug	1-Sep	2-Sep	3-Sep	4-Sep	5-Sep	6-Sep	7-Sep	8-Sep	9-Sep	10-Sep	11-Sep	12-Sep	13-Sep	14-Sep	15-Sep	16-Sep	17-Sep	18-Sep	19-Sep	20-Sep
				MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN
	Sand Lake Road Closures / Sidewalk																							
	<u>Sand Lake Rd & Ramps</u>																							
	Sand Lake WB Contra flow (Bridge Work)	James	Dennis			N	N				N		N	N				N	N	N	N			
	Sand Lake EB Contra flow (Bridge Work)	James	Dennis			N	N				N		N	N				N	N	N	N			
	Sand Lake EB Full Detour (Beam Placement)	James	Dennis	N	N							N												
	Sand Lake WB Full Detour (Beam Placement)	James	Dennis	N	N							N												
	Sand Lake Rd EB Single Lane	Lane	Dennis	N	N							N						N	N					
	Sand Lake Rd WB Single Lane	Lane	Dennis	N	N							N						N	N					
	Full Closure of Ramp K	Lane	Dennis																					
	Single Lane Closure of Ramp K	Lane	Dennis	N	N							N												
	Single Lane Closure of Ramp L	Lane	Dennis	N	N							N												
	Single Lane Closure of Ramp J	Lane	Dennis	N	N							N												
	Single Lane Closure of Ramp M	Lane	Dennis	N	N							N												
	Turkey Lake Rd South (Single Outside Lanes)	Lane	Dennis	N	N	N	N				N	N	N	N			N	N	N	N	N			N
	<u>I-4 EB</u>																							
	I-4 Pacing Operation EB 74.5 DMS	Lane/Conti	Dennis																					
	I-4 Single Lane Closures EB	Lane	Dennis	N	N							N					N	N	N	N	N			N
	I-4 Double Lane Closures EB	Lane	Dennis																					
	<u>I-4 WB</u>																							
	I-4 Single Lane Closures WB	Lane	Dennis	N	N	N	N					N	N	N			N	N	N	N	N			N

N/P - Night Pour	
X - Day Schedule	T-N - Tentative
NC - Night Time Confirmed	N - Night
TS-Traffic Shift	D-Pile Delivery





Agenda — Current Project Status

- **Past Project Status — FDOT to review past 7 days**
 - Bridge beam setting over Sand Lake Road (Areas 5 and 6)
 - Turkey Lake Road curb/sidewalk widening
 - Place and compact limerock (Areas 5, 6, and 8)
 - Embankment material placement (Areas 5 and 6)
 - Barrier wall installation (Areas 4, 6, and 8)
 - Excavate and grade ponds
 - Drainage installation (Areas 5, 6, and 7)
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Eastbound I-4 Bridge Reconstruction: First Seven Beams Set Over Sand Lake Road





Overhang Installation: First Seven Beams





Beam Installation Preparations for Remaining Beams





I-4 Median Barrier Wall Footer Placement





Agenda — Future Project Status

- **Future Project Status — FDOT to review next 7 days**

- Bridge support structure work over Sand Lake Road (Areas 5 and 6)
- Sand Lake Road/Turkey Lake Road intersection resurfacing (Area 3)
- Paving (Area 8)
- Sand Lake Road under I-4 curb/sidewalk work
- Turkey Lake Road curb/sidewalk widening
- Place and compact limerock (Areas 5, 6, and 8)
- Embankment material placement (Areas 5 and 6)
- Barrier wall installation (Areas 4, 6, and 8)
- Signal and sign structure installation (Area 3)
- Excavate and grade ponds
- Drainage installation (Areas 5 and 6)
- Ongoing mowing and litter pickup

- **Committee's Comments & Suggestions**



Agenda — Future Project Status

- **Future Project Status — FDOT to review next 14 – 21 days**
 - Bridge support structure work over Sand Lake Road (Areas 5 and 6)
 - Paving (Area 8)
 - Sand Lake Road under I-4 curb/sidewalk work
 - Turkey Lake Road curb/sidewalk widening
 - Place and compact limerock (Areas 5, 6, and 8)
 - Embankment material placement (Areas 5 and 6)
 - Barrier wall installation (Areas 4, 6, and 8)
 - Signal and sign structure installation
 - Excavate and grade ponds
 - Drainage installation (Areas 5 and 6)
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Cleanliness Review

- **Cleanliness Review**
 - Committee's observations over past 7 days
- **Condition Review**
 - Committee's observations over past 7 days
(fencing, wraps, barricades, temporary signage)




Agenda — Old Business

- **Public Input or Comments**
- **Commitments Update**
 - Fencing and screening
 - Mowing and cleaning
 - Clean Team
 - Express lanes signage/access (in-progress)
 - Hardscaping and aesthetics
 - Ponds



Safety Diversions

- September 8 (overnight)
 - Full diversion of Sand Lake Road under I-4
 - Bridge beam setting for the reconstruction of eastbound I-4
 - 11:30 p.m. to 6:30 a.m.

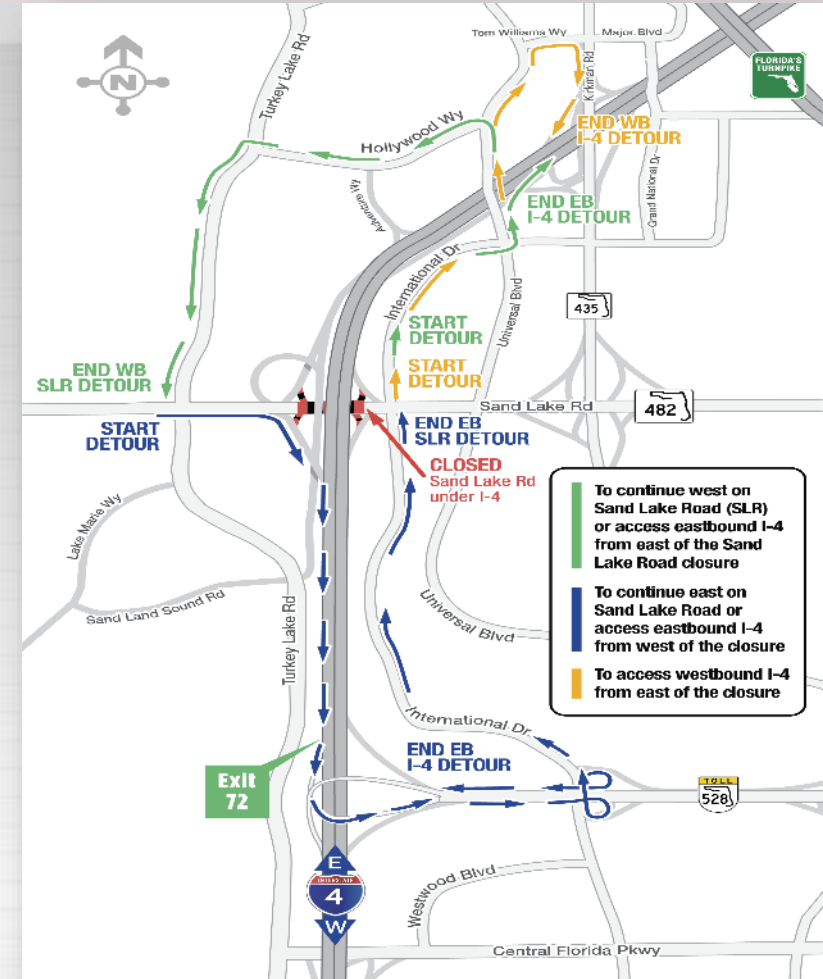



Agenda — New Business

Next meeting: 09/16/2026
