



I-4 and Sand Lake Road Interchange Design-Build

10/07/2026



Status as of October 5, 2026

Days Used	Total Days	% Days Complete	Last Contract Day
1,282	1,793	71.7%	2/28/2028

D-Pile Delivery				Halloween Horror Nights							Halloween Horror Nights							Halloween Horror Nights						
Sand Lake 3470				Current Week							Week 1							Week 2						
Activity ID	Activity Description	Foreman / Sub	Supt	5-Oct	6-Oct	7-Oct	8-Oct	9-Oct	10-Oct	11-Oct	12-Oct	13-Oct	14-Oct	15-Oct	16-Oct	17-Oct	18-Oct	19-Oct	20-Oct	21-Oct	22-Oct	23-Oct	24-Oct	25-Oct
				MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN	MON	TUE	WED	THU	FRI	SAT	SUN
	Roadway																							
EW720	Fill CIP 1-1 - Install Trench Drain	Marcos C.	Tyler	X																				
EW600	Base/Curb/Sidewalk Sand Lake Under Bridges	Marcos C.	Tyler	X	X																			
EW460	FG Curb/Sidewalk Ramp M to Turkey Lake (Rev. 6)	Marcos C.	Tyler			X	X	X			X	X	X	X	X			X	X	X				
	FG Curb/Sidewalk Ramp L to International Drive (Rev. 6)	Marcos C.	Tyler																		X	X	X	
MSE330	Exc/Grade Wall 101	Phillip A.	Tyler	X	X	X	X	X			X	X	X	X	X									
	FG Pond 201	Phillip A.	Tyler	X	X	X	X	X																
EW580	Place Embankment Ramp K/EB I4 - 7189+78 -- 7200+00	Phillip A.	Tyler	X	X	X	X	X			X	X	X	X	X									
	Exc/Grade Pond 206D	Phillip A.	Tyler															X	X	X	X	X		
STAB460	EB XL - Mix/Plc/Fin stab (6252 - 6262)	Jessie W	Tyler	X	X	X																		
BASE560	EB XL - Plc/Fin Lime Rock (6252 - 6262)	Jessie W	Tyler				X	X	X		X	X	X	X										
STAB460	Balance/Mix - Area 4 - 6263-6284	Jessie W	Tyler												X	X								
	Plc/Fin Limerock - Area 4 - 6263-6284	Jessie W	Tyler															X	X	X	X	X	X	
EW580	Balance/Mix - EB I4 - 7207-Bridge 4	Jessie W	Tyler	LBR	LBR	LBR	X	X																
	Plc/Fin Limerock - EB Widening - 1440-1454	Jessie W	Tyler	X	X	X																		
BASE360	EB/Ramp L - Plc/Fin Lime Rock (7219 - 7234)	Ian Palasz	Tyler	X	X																			
	Plc/Fin Lime Rock SLR Widening (210 - 213)	Ian Palasz	Tyler			X	X																	
	Plc/Fin Lime Rock EB GUL (7207 - Bridge 4)	Ian Palasz	Tyler					X	X															
	Plc/Fin Lime Rock EB Widening (1440 - 1454)	Ian Palasz	Tyler								X	X	X	X	X			X	X	X				
	Plc/Fin Lime Rock EB GUL (7190 - 7199)	Ian Palasz	Tyler																		X	X	X	
	Clean Team Sand Lake Sidewalks, Trash pickup and Mowing	Billy Worles	Jose Castro	X	X	X	X	X	X															
	Sand Lake off and on ramps to I-4 - Trash pickup and Mowing	Billy Worles	Jose Castro								X	X	X	X	X	X								
	Turkey Lake Sidewalks, Trash pickup and Mowing	Billy Worles	Jose Castro															X	X	X	X	X	X	
	DRAINAGE INSTALL ON TURKEY LAKE S-119- S-125 S-124 LF 25' ADS-18'	Michael Bloomfield	Jose C./Tyler	N	N	N	N	N		N	N	N												
	INSTALL S-500 TO S-501 ON TURKEY LAKE ROAD	Michael Bloomfield	Jose C./Tyler										N	N										
	INSTALL GRAVITY WALL PRECAST ON TURKEY LAKE	Michael Bloomfield	Jose C./Tyler														X	X	X	X	X	X		X
	Turkey Lake																							
	Drainage	michael bloomfield	Jose C.																					
	Widening (stab/base)	Michael Bloomfield	Jose C./Tyler																					
	FG/Pour Curb	Michael Bloomfield / JV	Jose C./Tyler																					
CIP100/110	Exc/Grade Gravity Wall	Michael Bloomfield	Jose C./Tyler																					
CIP100/110	Install Gravity Wall	Francisco	Jose Perez	X	X	X	X	X																
	Embankment	Michael Bloomfield	Jose C./Tyler																					
	FG/Pour Sidewalk (5654+50 - 5256+10)	Michael Bloomfield / JV	Jose C./Tyler																					
	FG/Pour Sidewalk	Michael Bloomfield / JV	Jose C./Tyler																					
	FG for Sod	Michael Bloomfield	Jose C./Tyler								X	X	X											
	Drainage / Utilities																							
	S-235-A TO S-235--OF INSTALL ADS 36" PIPE 54'LF	Isaias Barcenias	Jose Castro	X	X	X	X	X	X															
	INSTALL - S-240 TO S-242 DITCH BOLT INLET 30" DRAINAGE 194" LF	Isaias Barcenias	Jose Castro								X	X	X	X	X	X								
	S-233-A TO S-239 INSTALL 30" INCH ADS LF-30	Isaias Barcenias	Jose Castro															X	X	X	X	X	X	
	INSTALL 6" UNDERDRAIN ON RAMP K FROM S-242-S-3000 LF 269"	Dakota Mooney	Jose castro	X	X	X																		
	INSTALL 6" UNDER DRAIN ON RAMP K FROM S-3000 TO S-3001 LF 241"	Dakota Mooney	Jose castro				X	X	X		X	X	X	X	X	X								
DRG1400	S- 723- 721 INSTALL DOG HOUSE ON THE NORTH SIDE 36" ADS 120LF	Dakota Mooney	Jose Castro															X	X	X	X	X	X	
	S-528--B TO 528-A CONNECT TO EXIST 30" PIPE ON RAMP -K	manny presiado	Jose Castro	X	X	X																		
	INSTALL S-528-A- TO 528-OF 36" LF ADS PIPE 30" INCH TO THE POND 206-D	manny presiado	Jose Castro				X	X	X															
	INSTALL 60"LF FROM S-84- TO S-83 TO CONNECT J/B 29X45 RCP	manny presiado	Jose Castro								X	X	X	X	X	X								
	INSTALL FROM J/B TO S-71 TO 72 ON THE MIDDLE OF I-4 39"LF 18" ADS	manny presiado	Jose Castro															X	X	X	X	X	X	
	Rangeline - Wet Tap: 24x24 @ International/SLR	Eddie B	Jose Castro	N																				

N/P - Night Pour	
X - Day Schedule	T-N - Tentative
NC - Night Time Confirmed	N - Night
TS-Traffic Shift	D-Pile Delivery

Activity ID	Activity Description	Foreman / Sub	Supt	5-Oct	6-Oct	7-Oct	8-Oct	9-Oct	10-Oct	11-Oct	12-Oct	13-Oct	14-Oct	15-Oct	16-Oct	17-Oct	18-Oct	19-Oct	20-Oct	21-Oct	22-Oct	23-Oct	24-Oct	25-Oct
	Structures																							
	<u>Bridge #4</u>																							
	form edge form	Felipe Perez	Jose Perez													x	x							
REINF260	dry run span 1	Felipe Perez	Jose Perez								x											x	x	
REINF270	dry run span 2	Felipe Perez	Jose Perez					x	x															
DECK180	place concrete span 2	Felipe Perez	Jose Perez									P												
	<u>Pylon</u>																							
SUBS370	form Pylon 4-2	Cristian Flores	Jose Perez	x	x	x	P			B/P														
	hoist rebar pylon 4-1	Cristian Flores	Jose Perez	x	x	x	x	x																
	<u>Wall 4-1</u>																							
	Form C.I.P	Rafeal Nunez	Jose Perez	x	x	x	x	x	x		x	x	x	P	x	x		x	x	x	x	x		
	F/G for junction slab	Rafeal Nunez	Jose Perez	P	x	x	x	x	x															
	form junction slab	Rafeal Nunez	Jose Perez	x	x	x	x																	
	Subcontractor																							
	Turkey Lake Curb and Gutter, Siderwalk	JVD	jose castro	x	N	N	N																	
	Sand Lake Curb/Sidewalk	JVD	Isabel				X																	
BW380	Median Barrier - WB GUL, XL's, EB GUL (North)	Blount Sanford	Isabel	X	X	X	X											X	X	X	X			
BW370	OHC 14 Pedestal	Blount Sanford	Isabel								X	X	X	X	X									
SUBS370	Pylon 4-1 bottom	Shelby	John	x	x																			
MSE330	Dig Out Level Pad RW 101	Phillip A.	Tyler	X	X	X	X	X																
MSE330	Form/Pour Level Pad RW 101	RWH	Nate								X	X	X	X	X									
MSE330	RW 101	RWH	Nate										X	X	X			X	X	X	X	X		
	Express Lane Barrier Wall Pinning	TCP	Nate															N	N					
DRG2050	Install 36" J&B S-71 - S83 (Tube Area 3) Sta: 1385	CFU	Jose	X	X	X	X	X																
	Paving Ramp L & EB GULs	Hubbard			N	N																		
	Sand Lake Widening 210 - 212	Hubbard					N																	
PAVE390	Ramp K/EB Widening 1440 - 1454	Hubbard								N	N	N												
	EB GUL's 7206 - 7213+75	Hubbard											N	N			N							
PAVE590	WB Express lanes 5252 - 5259+20	Hubbard																N	N	N	N			
	<u>Lighting</u>																							
	Lighting Maintenance (I4EB Median/Ramp M)	Conti	Rainer	X	X	X	X	X																
LGHT110	Lighting Load Center C (Ramp J)	Conti	Rainer	X	X	X	X	X			X	X	X	X	X									
	ITS Pull Boxes I-4 WB Sta: 1554 - 1479	Conti	Rainer															X	X	X	X	X		
ITS100	ITS Conduit I-4 WB Sta: 1554 - 1479	Conti/Vasi/KDI	Rainer								X	X	X	X	X			X	X	X	X	X		
ITS140	ITS Drill Shaft Installation: 74.2 WB	Conti	Rainer	N																				
	ITS Drill Shaft Installation: 74.6 EB	Conti	Rainer		N																			
	<u>Signals</u>																							
	DDI Signal Conduit	Conti/Vasi/KDI	Rainer	X	X	X	X	X			X	X	X	X	X									
	<u>Toll Plaza</u>																							
TOLL240	Loop Boxes Gantry	Conti/Blount	Rainer															X	X	X	X	X		
	Building Electrical	Conti	Rainer	X	X	X	X	X			X	X	X	X	X									
	Building Flat Work	Conti/JVD	Rainer								X	X	X	X	X									
	Sand Lake Road Closures / Sidewalk																							
	<u>Sand Lake Rd & Ramps</u>																							
	Sand Lake Rd EB Single Lane	Lane	Dennis		N	N	N			N	N	N	N	N			N	N	N	N	N			N
	Sand Lake Rd WB Single Lane	Lane	Dennis																					
	Single Lane Closure of Ramp L	Lane	Dennis		N	N	N																	
	Turkey Lake Rd South (Single Outside Lanes)	Lane	Dennis	N	N	N	N																	N
	<u>I-4 EB</u>																							
	I-4 Single Lane Closures EB	Lane	Dennis			N	N																	N
	I-4 EB Express Lane Detour																	N	N					
	<u>I-4 WB</u>																							
	I-4 Single Lane Closures WB	Lane	Dennis	N	N						N	N	N	N	N			N	N	N	N			N

N/P - Night Pour

X - Day Schedule

NC - Night Time Confirmed

TS-Traffic Shift

T-N - Tentative

N - Night

D-Pile Delivery





Agenda — Current Project Status


- **Past Project Status — FDOT to review past 7 days**

- Bridge support structure work over Sand Lake Road (Areas 5 and 6)
- Eastbound I-4 entrance ramp paving (Areas 5 and 6)
- Turkey Lake Road curb/sidewalk widening
- Place and compact limerock (Areas 5, 6, and 8)
- Embankment material placement (Areas 5 and 6)
- Barrier wall installation (Areas 4, 6, and 8)
- Signal and sign structure installation (Area 3)
- Excavate and grade ponds
- Drainage installation (Areas 5 and 6)
- Force main work on Sand Lake Road
- Ongoing mowing and litter pickup

- **Committee's Comments & Suggestions**



Eastbound I-4 Bridge Rebar Work

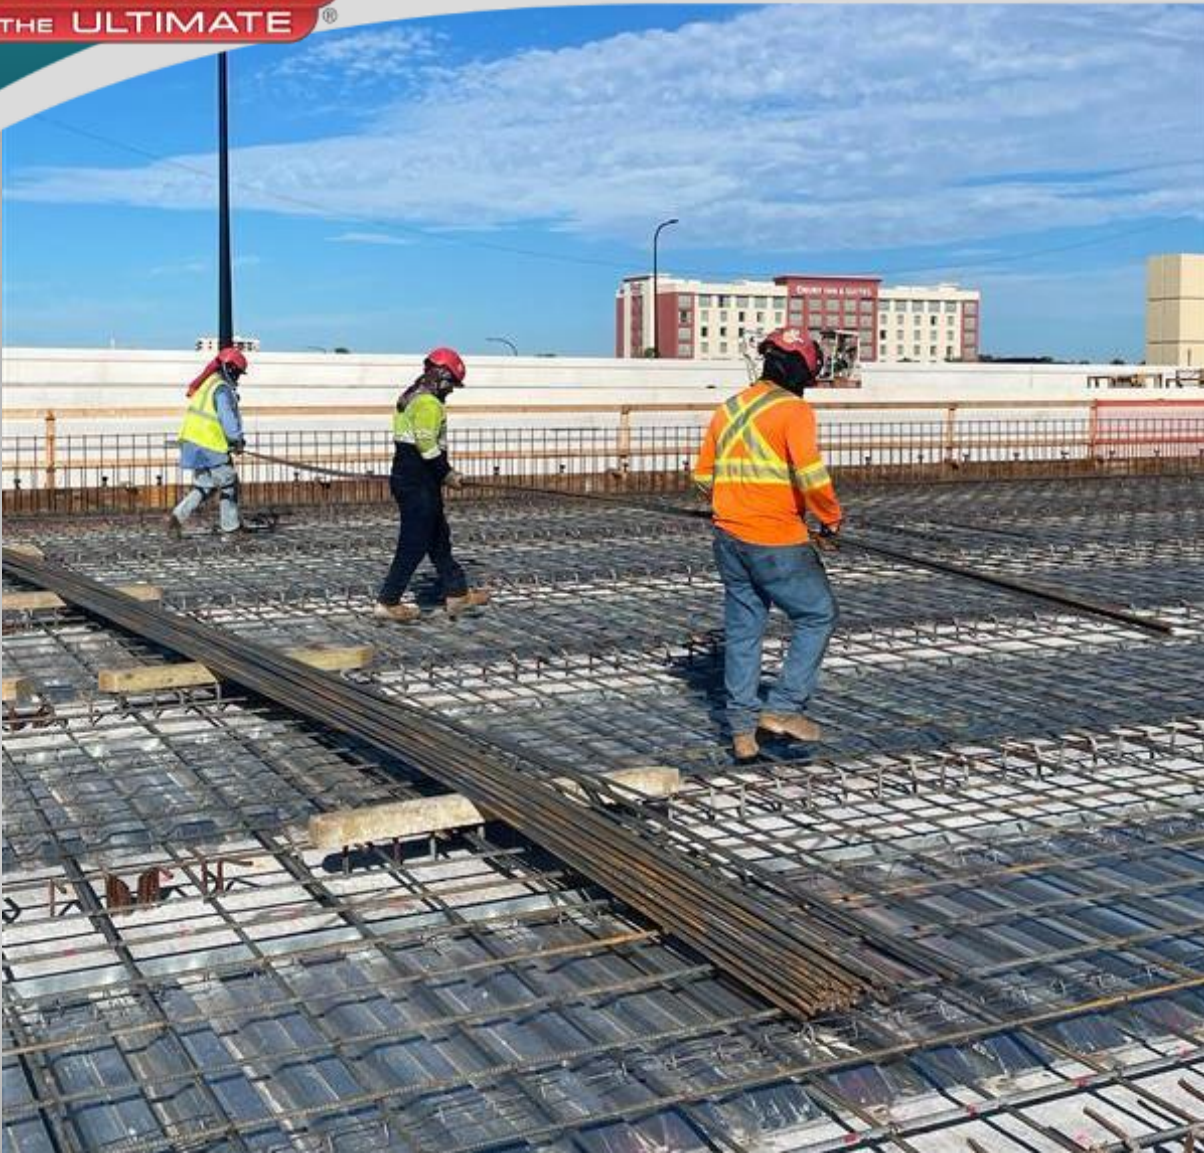



Westbound I-4 Exit Ramp Drill Shaft Work and Concrete Placement





Eastbound I-4 Entrance Ramp Limerock Stabilization





Agenda — Future Project Status

- **Future Project Status — FDOT to review next 7 days**

- Eastbound I-4 bridge concrete deck pour (Area 6)
- Paving (Areas 7 and 8)
- Eastbound I-4 entrance ramp paving (Areas 5 and 6)
- Sand Lake Road under I-4 curb/sidewalk work
- Turkey Lake Road curb/sidewalk widening, gravity wall work
- Place and compact limerock (Areas 5, 6, and 8)
- Embankment material placement (Areas 5 and 6)
- Barrier wall installation (Areas 4, 6, and 8)
- Excavate and grade ponds
- Drainage installation (Areas 5 and 6)
- Ongoing mowing and litter pickup
- Drill shaft placement (Area 8)

- **Committee's Comments & Suggestions**



Agenda — Future Project Status

- **Future Project Status — FDOT to review next 14 – 21 days**
 - Eastbound I-4 bridge concrete deck pour (Area 6)
 - Eastbound I-4 Express barrier wall pinning
 - Paving (Area 8)
 - Sand Lake Road under I-4 curb/sidewalk work
 - Turkey Lake Road curb/sidewalk widening, gravity wall work
 - Place and compact limerock (Areas 5, 6, and 8)
 - Embankment material placement (Areas 5 and 6)
 - Barrier wall installation (Areas 4, 6, and 8)
 - Signal and sign structure installation
 - Excavate and grade ponds
 - Drainage installation (Areas 5 and 6)
 - Ongoing mowing and litter pickup
- **Committee's Comments & Suggestions**



Agenda — Cleanliness Review

- **Cleanliness Review**
 - Committee's observations over past 7 days
- **Condition Review**
 - Committee's observations over past 7 days
(fencing, wraps, barricades, temporary signage)



Agenda — Old Business

- **Public Input or Comments**
- **Commitments Update**
 - Fencing and screening
 - Mowing and cleaning
 - Clean Team
 - Hardscaping and aesthetics
 - Ponds



Safety Diversions

- October 7 and 8 (overnight)
 - Westbound I-4 entrance ramp from Apopka-Vineland Road
 - Ramp shift preparations
 - 10 p.m. to 6 a.m.





New Traffic Pattern – Apopka-Vineland Road

As soon as October 9

- New westbound I-4 entrance ramp from Apopka-Vineland Road
- New traffic pattern on southbound Apopka-Vineland Road at I-4:



1. The current free-flow lane to WB I-4 will no longer be accessible.
2. The right-most through lane will become a right-turn lane to WB I-4
3. Three through lanes will remain
4. Drivers will use the right-most through lane to reach EB I-4 after the signal



Agenda — New Business

Next meeting: 10/14/2026
